

BELVEDERE ELEMENTARY ADDITIONS

EXECUTIVE SUMMARY REPORT



**mcmillan
pazdan
smith**
ARCHITECTURE

AUGUST 2021

BELVEDERE ELEMENTARY ADDITIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Painting
- Finishes
- Flooring
- Landscaping
- Furniture

ACTIVITIES COMPLETE:

- Clearing and Grading
- Footings
- Slabs
- Steel
- Parking and Curbs and Sidewalks
- Steel Decking
- Framing
- Masonry
- Roofing
- Stucco
- Windows
- Canopy
- MEP
- Amphitheater

PROJECT SCHEDULE:

Site Work and New Construction - August 1, 2021
Demo, Related Site Work, New Construction - November 30, 2021

APPLICATIONS FOR PAYMENT:

| | |
|-----------------------------|-----------------|
| Original Contract Sum: | \$10,700,170.00 |
| Net Change by Change Order: | \$0 |
| Contract Sum to Date: | \$10,700,170.00 |
| Amount Paid to Date: | \$8,669,820.00 |

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



PROGRESS PHOTOS:



ENTRANCE VIEW



VIEW TO NORTHWEST



PROGRESS PHOTOS:



PROGRESS PHOTOS:




LOBBY



CORRIDOR



PROGRESS PHOTOS:

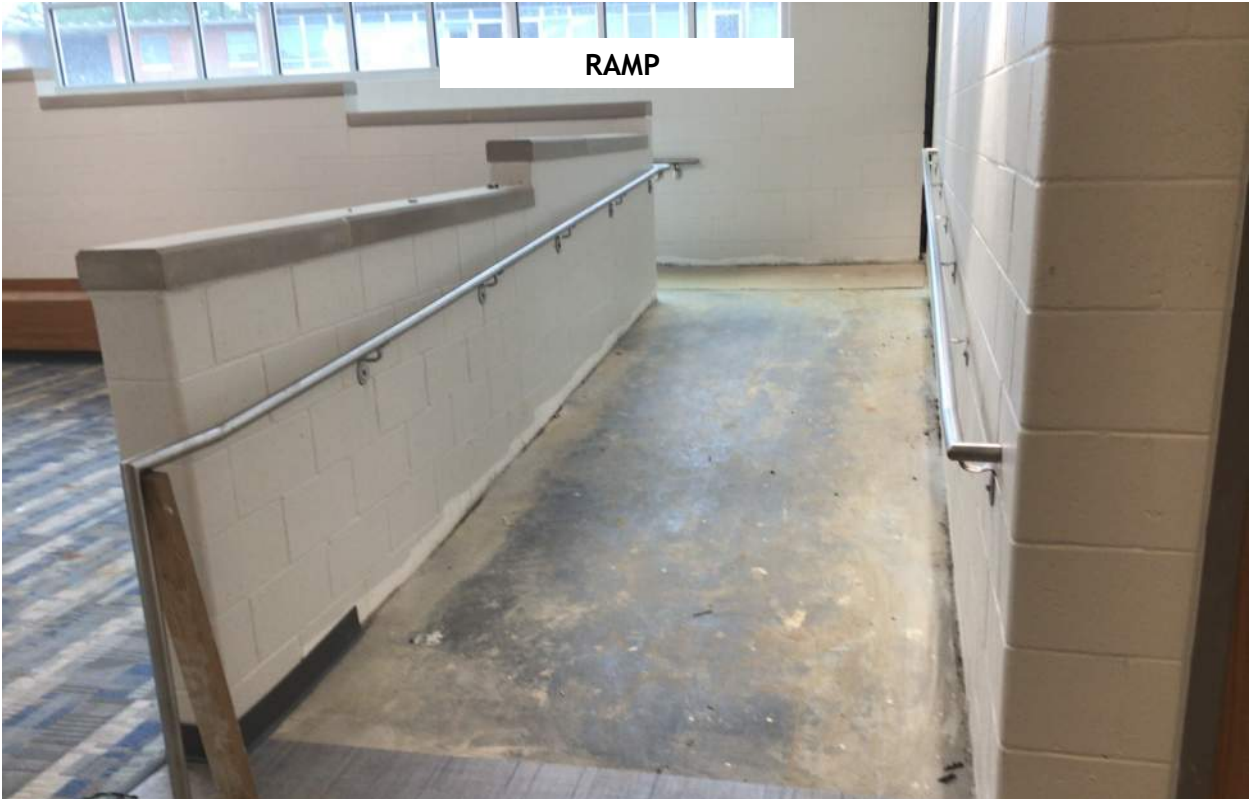

PROGRESS PHOTOS:

