

NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT



mcmillan | pazdan | smith
architecture

March 2015

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The building is almost complete and the General Contractor is coordinating the effort to make the corrections noted in the OSF inspection. Reinspection is scheduled for early April.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015
- OSF reinspection scheduled for early April

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$9,228,635

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:


There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Interior Finishes
- Mechanical
- Plumbing
- Electrical
- Cleaning and Touch-up



PROGRESS PHOTOS:

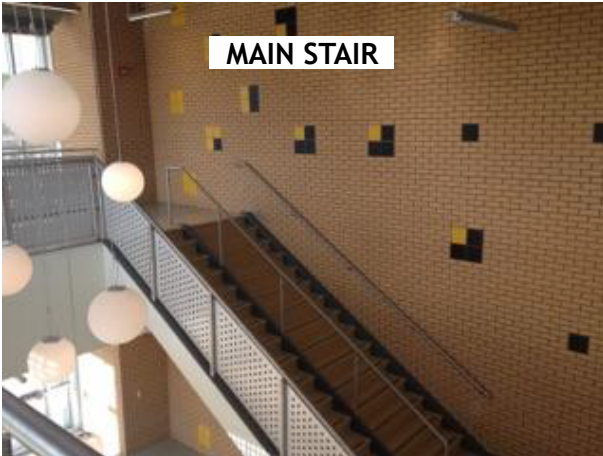

PROGRESS PHOTOS:



MAIN STAIR



EXTERIOR



CLASSROOM



EXTERIOR



CLASSROOM



EXTERIOR

