


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

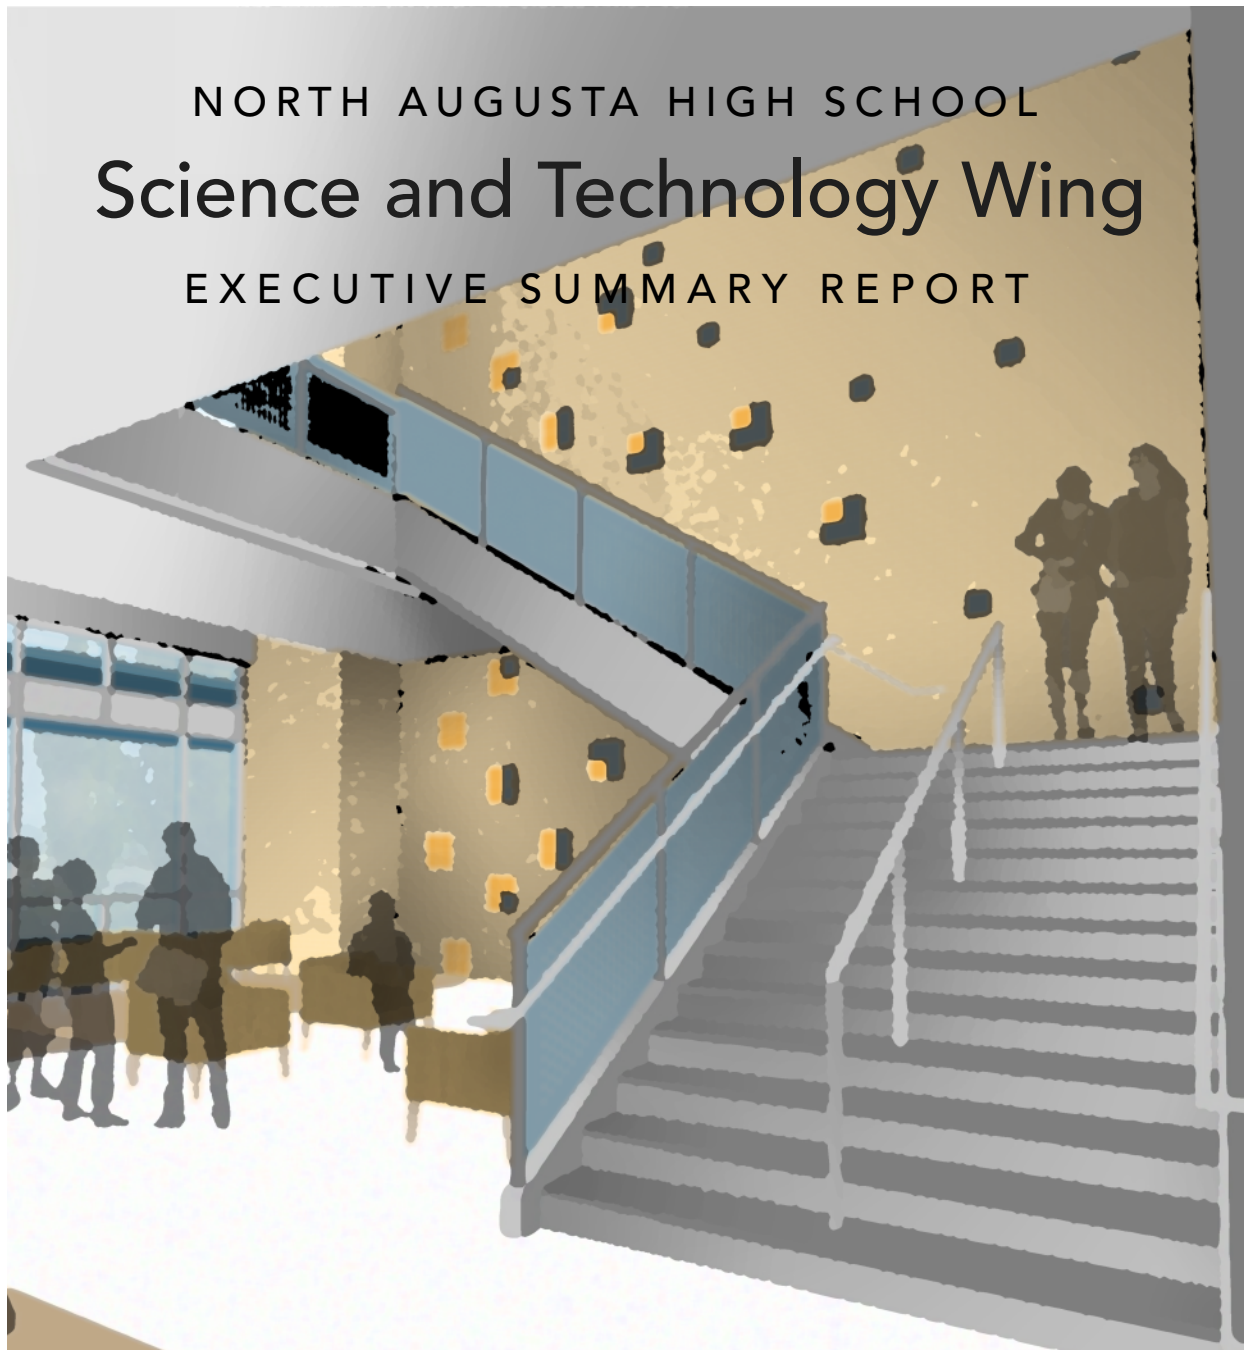

mcmillan | pazdan | smith
architecture

August 2014

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor is coordinating the various scopes of work and submittals. The site preparation portion of the work is ongoing. Placement of the segmental block retaining walls is ongoing. Masonry walls are complete with the brick to start in the next few weeks. First and second floor concrete and steel floor structures are in place. Mechanical, plumbing and electrical trades are progressing well. Roofing will be complete in the next few weeks.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$4,904,766

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Segmental Block Retaining Walls
- Brick Masonry
- Mechanical
- Plumbing
- Electrical



PROGRESS PHOTOS:



PROGRESS PHOTOS:



PLUMBING PROGRESS



STEEL FLOOR STRUCTURE

