


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

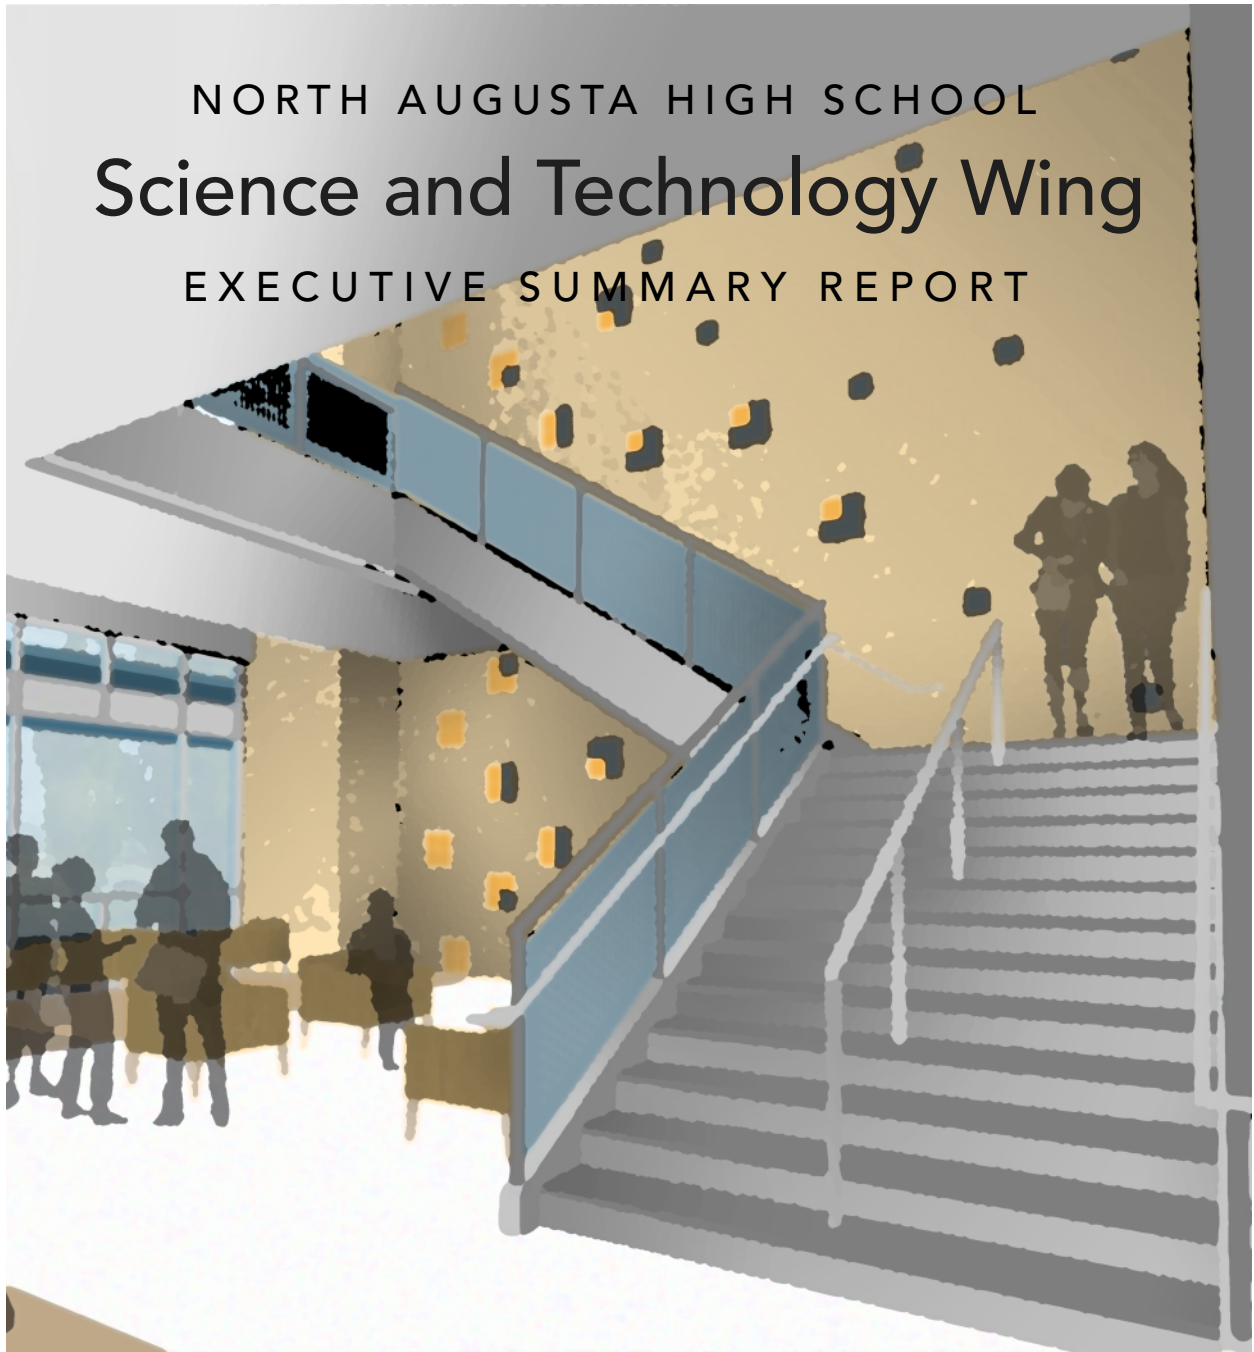

mcmillan | pazdan | smith
architecture

November 2014

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor continues to coordinate the various scopes of work. The site preparation portion of the work is ongoing. Exterior brick application and painting of CMU walls is complete. Acoustical tile ceiling grid installation is nearing completion and window installation is complete. Mechanical, plumbing and electrical trades are still progressing well. The General Contractor is preparing to install interior finishes and casework.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$7,297,778

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:


There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Interior Finishes
- Mechanical
- Plumbing
- Electrical



PROGRESS PHOTOS:

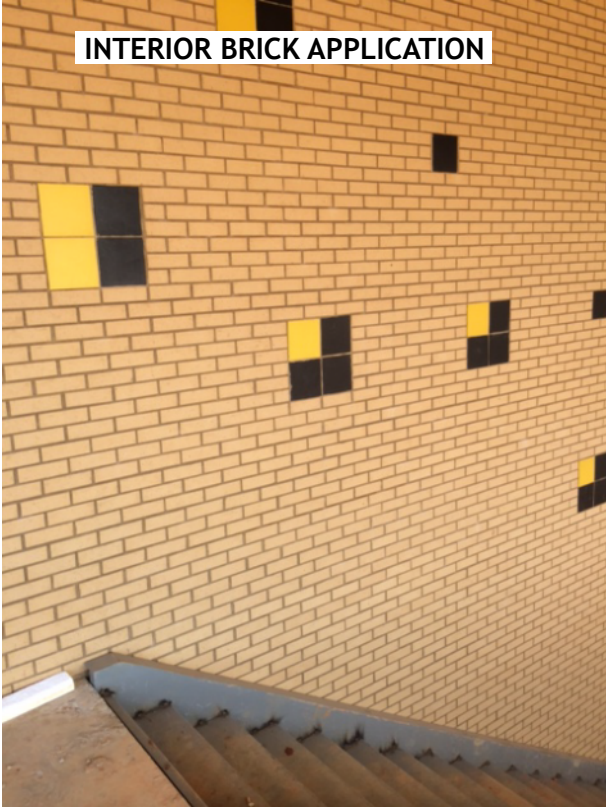

INTERIOR BRICK APPLICATION



EXTERIOR BRICK VENEER



RETAINING WALL



CLASSROOM PROGRESS



PROGRESS PHOTOS:



CURTAINWALL



CLASSROOM PROGRESS



INTERIOR FINISHES



INTERIOR FINISHES

