


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

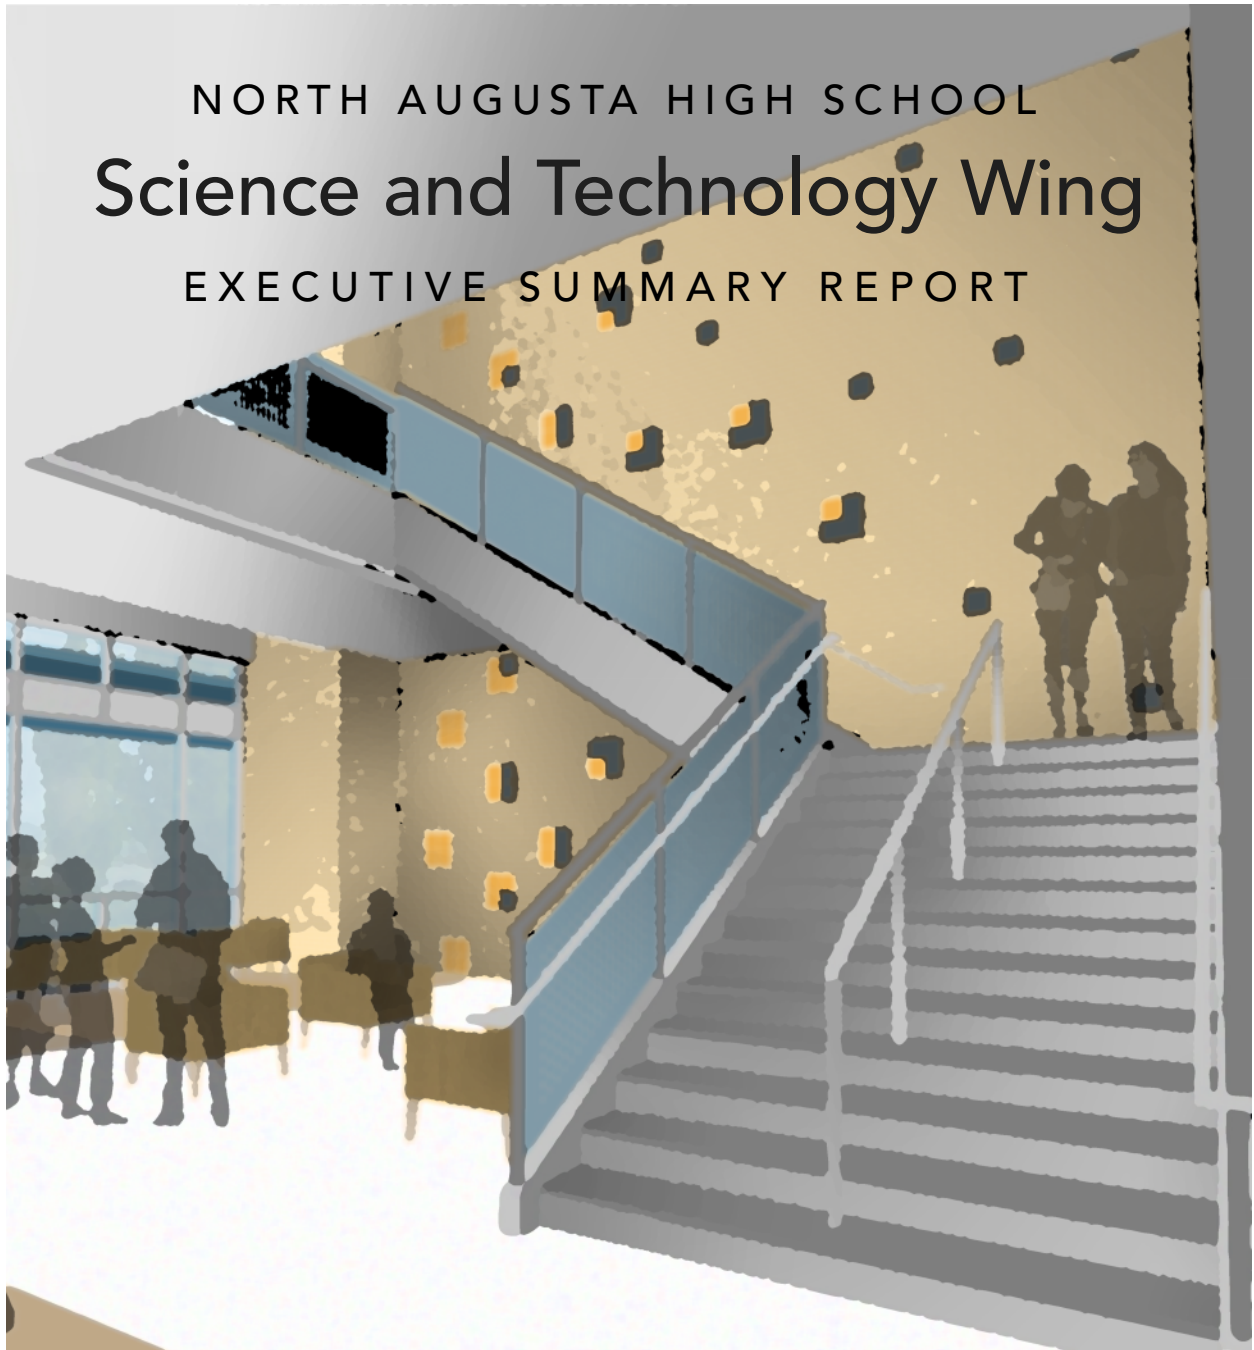

mcmillan | pazdan | smith
architecture

January 2015

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor continues to coordinate the various scopes of work and is preparing for the final OSF inspection. The site preparation portion of the work is ongoing. The acoustical tile ceiling installation is nearing completion. Casework installation is currently underway. Interior finishes, such as painting and terrazzo flooring, are progressing well. Mechanical, plumbing and electrical trades are nearing completion.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$8,589,727

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:


There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Interior Finishes
- Mechanical
- Plumbing
- Electrical
- Ceiling Tile Installation
- Terrazzo Installation
- Casework Installation



PROGRESS PHOTOS:

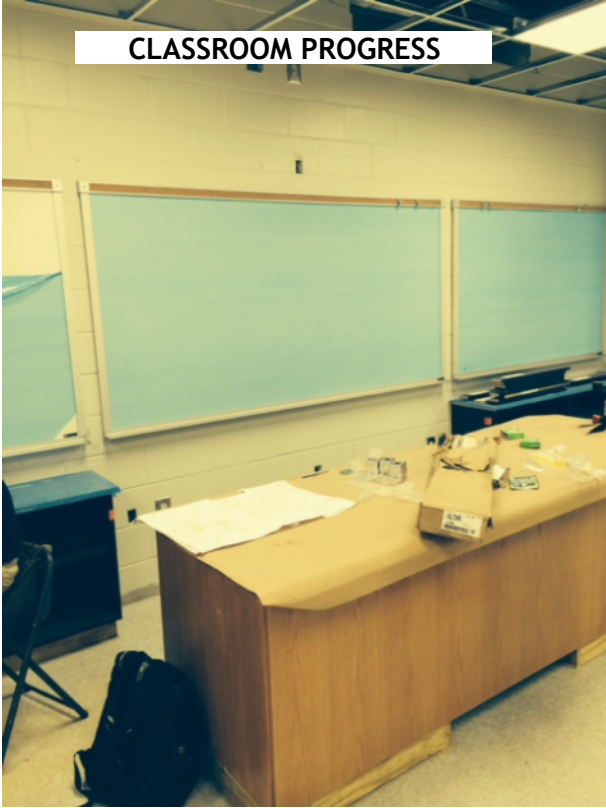

CLASSROOM PROGRESS



CLASSROOM PROGRESS



CLASSROOM PROGRESS



SITE WORK

