


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

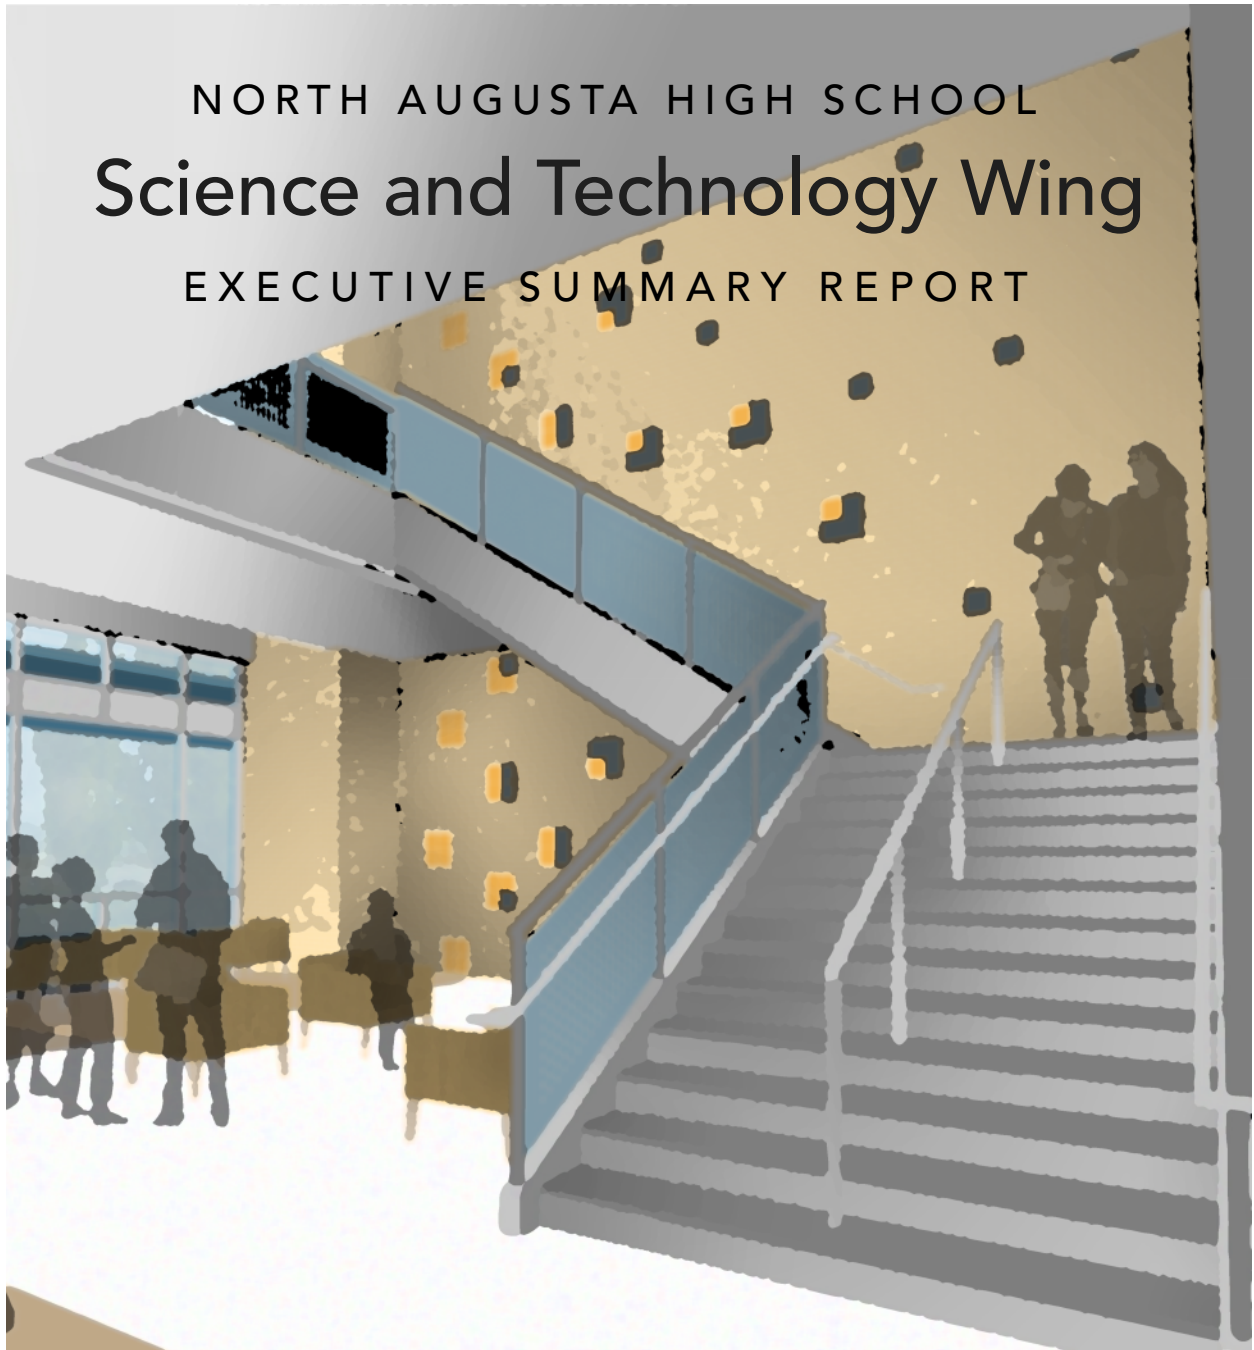

mcmillan | pazdan | smith
architecture

February 2015

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor continues to coordinate the various scopes of work in preparation for the final OSF inspection. The site preparation portion of the work is ongoing. The acoustical tile ceiling installation is complete. Casework installation is complete. Interior finishes, such as painting and terrazzo flooring, are progressing well, and are nearing completion. Mechanical, plumbing and electrical trades are nearing completion as well.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015
- OSF Final Inspection tentatively scheduled for late February

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$8,839,254

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Interior Finishes
- Mechanical
- Plumbing
- Electrical
- Terrazzo Installation
- Cleaning and Touch-up



PROGRESS PHOTOS:



INTERIOR PROGRESS



INTERIOR PROGRESS



WORKROOM PROGRESS



SITE WORK

PROGRESS PHOTOS:

