

North Augusta Middle School Building Addition Package

SUMMARY STATEMENT:

The final OSF inspection for the New Addition was held on May 17, 2011 and substantial completion has been established for that date. There was a problem with the Kitchen Hood and a retest with the OSF inspector was held on May 26, 2011 which successfully passed. Training for the Kitchen staff was conducted on May 31, 2011. The contractor started demolition of the existing stair on June 6, 2011. Once the stairs are demolished the structural steel will be erected and floor slabs poured to enlarge the vestibule area near the elevator. This work will tie all floors of the existing building together with the new building.

PROJECT SCHEDULE: As of May 31, 2011

• Notice to Proceed: November 11, 2009

• Substantial Completion:

Addition & New Stair/Elevator- substantial complete May 17, 2011
Stair Removal, Fire Alarm/Intercom Tie-in August 1, 2011

• Final Completion: August 31, 2011

Days Elapsed/Percentage: 567 of 659 days / 86.04%

PROJECT ACCOUNTING: As of May 31, 2011

•	Original Contract Sum:	\$ 6,544,900.00
•	Net Change by Change Orders:	\$ 119,587.00
•	Contract Sum to Date:	\$ 6,664,487.00
•	Total Completed & Stored to Date:	\$ 6,509,688.00

APPROVED CHANGES:

• No new approved changes this month.

PENDING CHANGES:

- The contractor provided credit pricing for deletion of the Genesis System and the High Performance paint in the Kitchen area. Contractor has provided a credit of \$142.00 which is being reviewed.
- COR 049/PR 025 to add a sink at the Synergy Lab work is pending.
- PR 027 to add guardrails at curtainwall windows pricing was received from the subcontractor in the amount of \$1620. Waiting on contractor to provide final proposal.
- COR 030 for irrigation head adjustment. Subcontractor cost of \$475. Cost approved work to proceed. Waiting on contractor to provide final proposal.



ACTIVITIES UNDERWAY:

- Demolishing concrete at existing stair.
- Completing OSF punchlist items; only items 4, 10, 20, 21, 22 & 28 remain.
- Completing general punchlist items.
- Compiling O&M Manuals and As-Built drawings. The Contractor stated they will submit them by June 17, 2011
- Contractor needs to arrange Owner training on the Mechanical and Electrical systems.
- Preparing exterior for final punch, too many obvious items at this time.


PROGRESS PHOTOS:




Concrete Removal at Existing Stair

New Exit Sign required by OSF, 2nd Floor Corridor





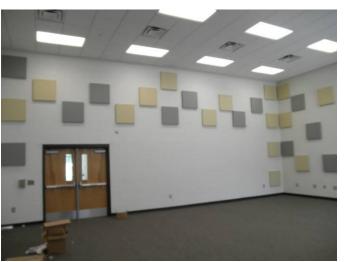

Chorus Room

