

# BELVEDERE ELEMENTARY ADDITIONS

## EXECUTIVE SUMMARY REPORT



**mcmillan  
pazdan  
smith**  
ARCHITECTURE

---

April 2021

---

# BELVEDERE ELEMENTARY ADDITIONS

## ACTIVITIES CURRENTLY UNDERWAY:

- MEP
- Ceiling Grid
- Painting
- Amphitheater
- Windows
- Stucco
- Finishes

## ACTIVITIES COMPLETE:

- Clearing and Grading
- Footings
- Slabs
- Steel
- Parking and Curbs
- Steel Decking
- Framing
- Masonry
- Roofing

## PROJECT SCHEDULE:

Site Work and New Construction - August 1, 2021  
Demo, Related Site Work, New Construction - November 30, 2021

## APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$10,700,170.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$10,700,170.00
Amount Paid to Date:	\$6,477,292.00

## REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



**PROGRESS PHOTOS:**



**ENTRANCE VIEW**



**VIEW TO NORTHEAST**





**PROGRESS PHOTOS:**




**HVAC**



**PAINTING & CEILING GRID**



**PROGRESS PHOTOS:**

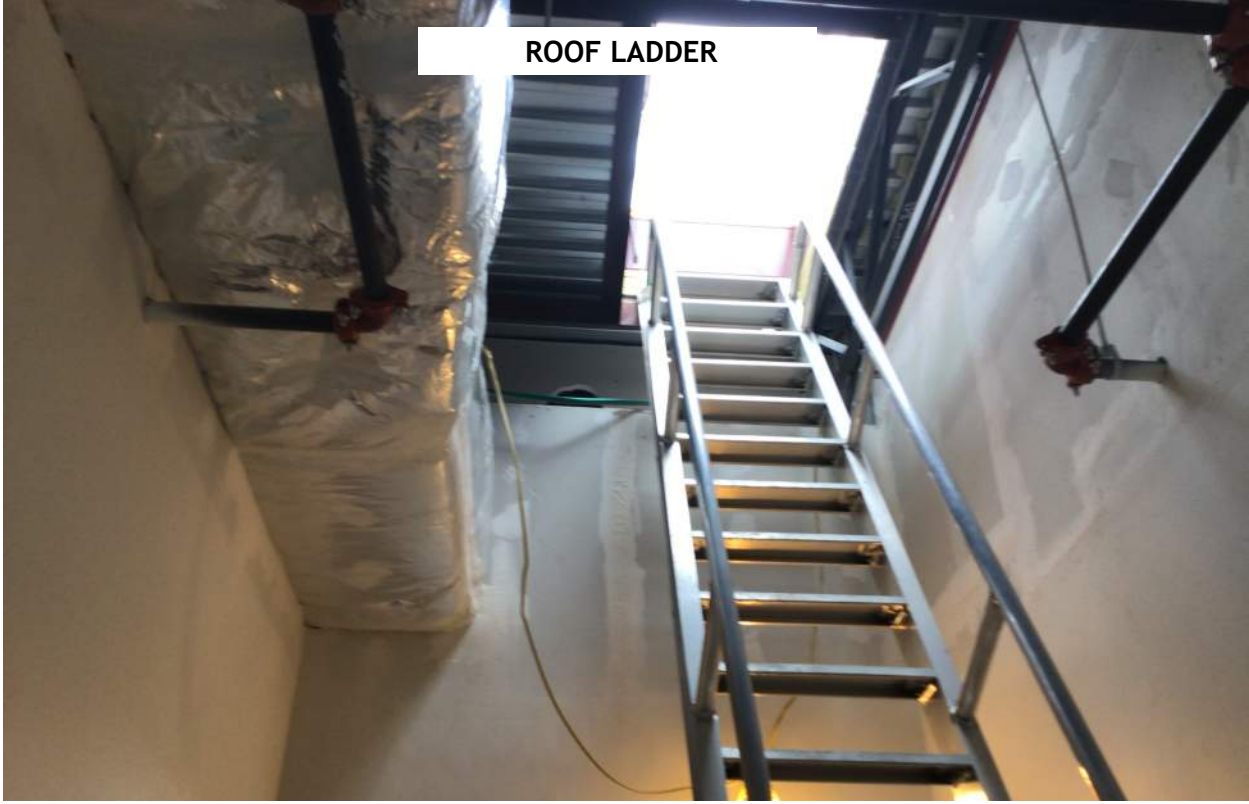

**ROOF LADDER**



**METAL ROOF**

