


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

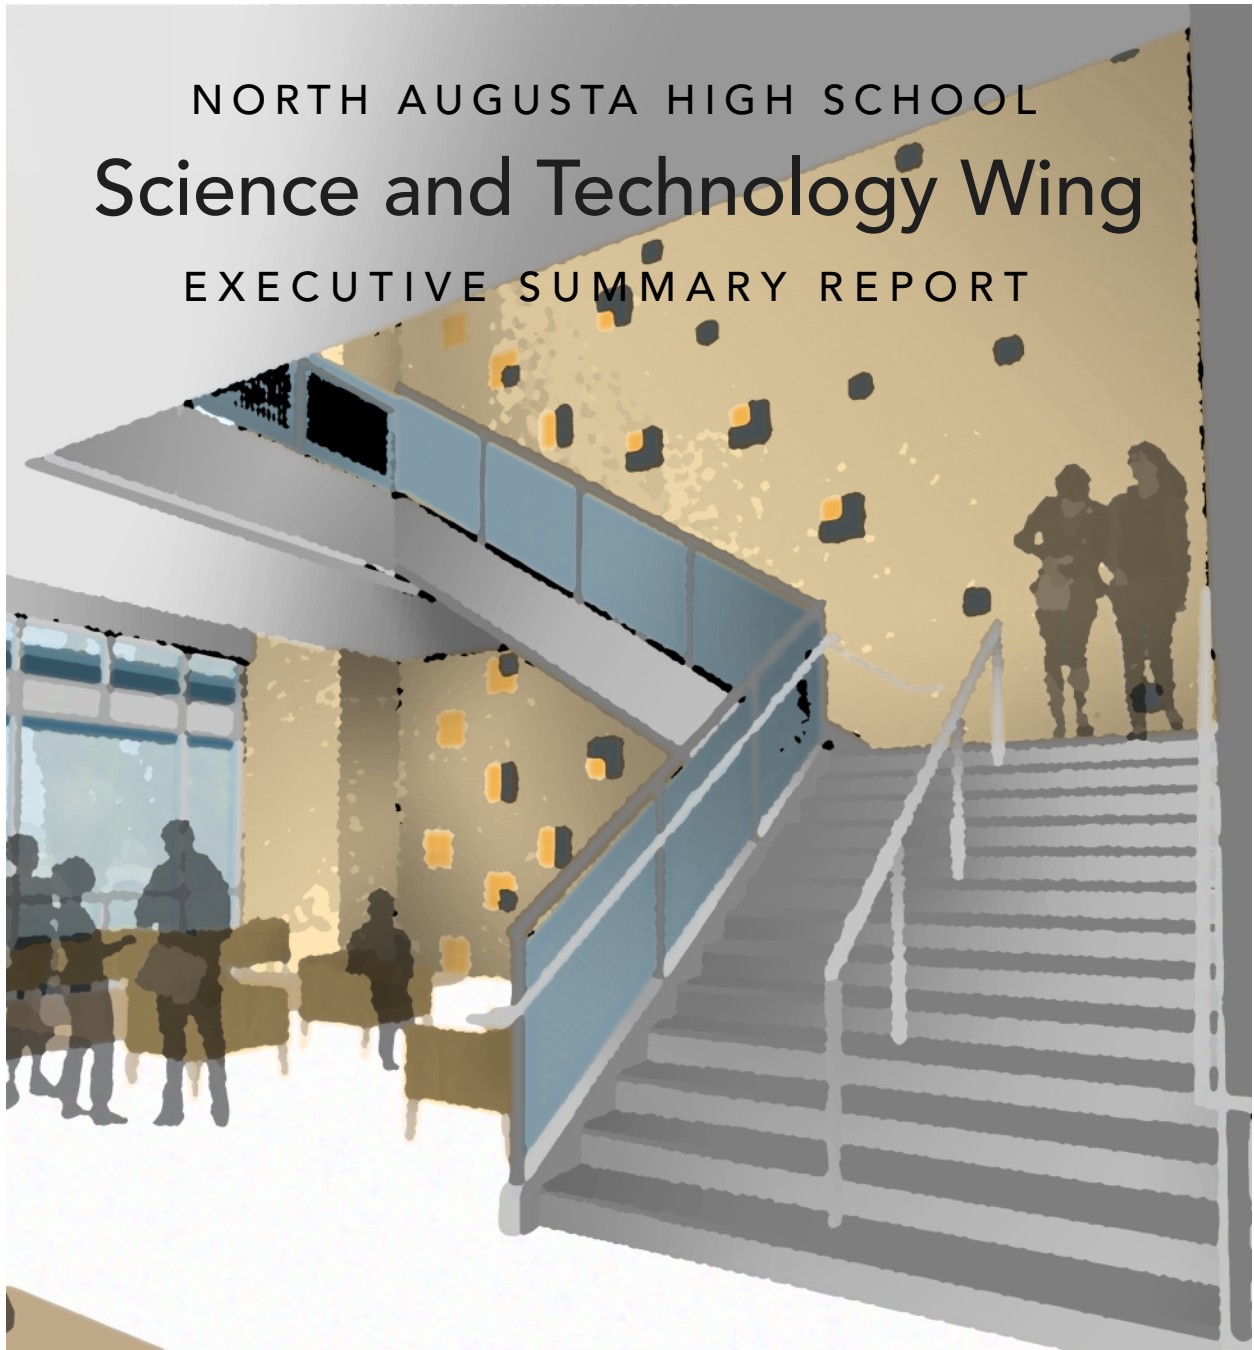

mcmillan | pazdan | smith
architecture

June 2014

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor is coordinating the various scopes of work and submittals. The site preparation portion of the work is ongoing. Placement of the segmental block retaining walls is ongoing. Placement of concrete floor slab is complete. Masonry walls are being constructed in preparation for the first floor steel floor structure. Mechanical, plumbing and electrical trades are progressing well.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$3,166,802

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Segmental Block Retaining Walls
- Concrete Block Masonry
- Mechanical
- Plumbing
- Electrical



PROGRESS PHOTOS:



PROGRESS PHOTOS:



CONCRETE BLOCK MASONRY



PLUMBING & MASONRY

PROGRESS PHOTOS:



PROGRESS PHOTOS:

