

PHASE II ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

EXECUTIVE SUMMARY REPORT



**mcmillan
pazdan
smith**
ARCHITECTURE

October 2017

PHASE II ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

PHASE II A

ACTIVITIES CURRENTLY UNDERWAY:

- Interior Finishes
- Mechanical/Electrical/Plumbing/Fire Protection

ACTIVITIES COMPLETE:

- Grading Operations
- Storm Drain Installation
- Foundation Installation
- Below Grade Waterproofing
- Concrete Floor Slabs
- Steel Erection
- CMU Walls
- Elevated Slabs
- Exterior Moisture Barrier
- Brick Veneer
- Retaining Wall Installation
- Underground Utilities
- Storefront/Curtainwall Installation
- Roofing
- Casework
- Acoustical Tile Ceilings



PHASE II ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2018

APPLICATIONS FOR PAYMENT:

Original Contract Sum: \$39,984,978.00

Net Change by Change Order: \$0

Contract Sum to Date: \$39,984,978.00

Amount Paid to Date: \$23,832,487.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.





CAFETERIA ENTRANCE



MAIN LOBBY





CAFETERIA



MEDIA CENTER






CAFETERIA



MEDIA CENTER



MAIN LOBBY

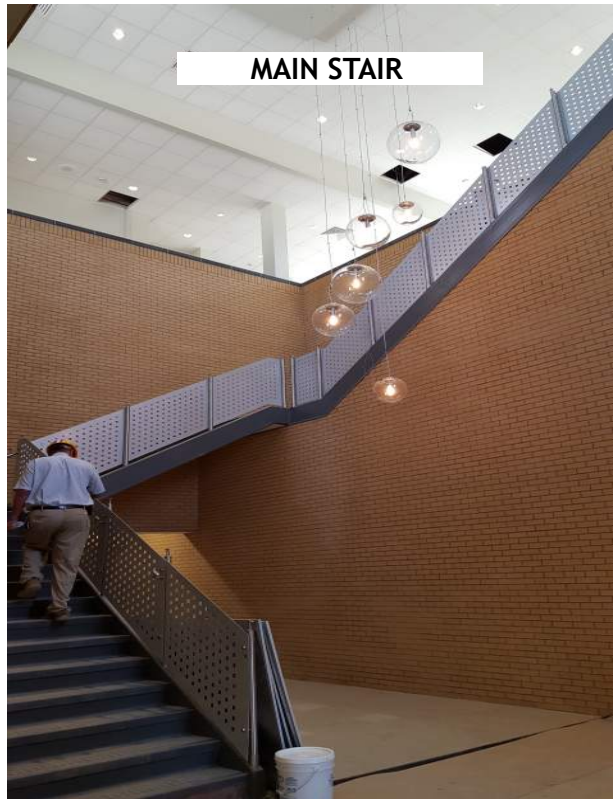

MAIN STAIR

