


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT

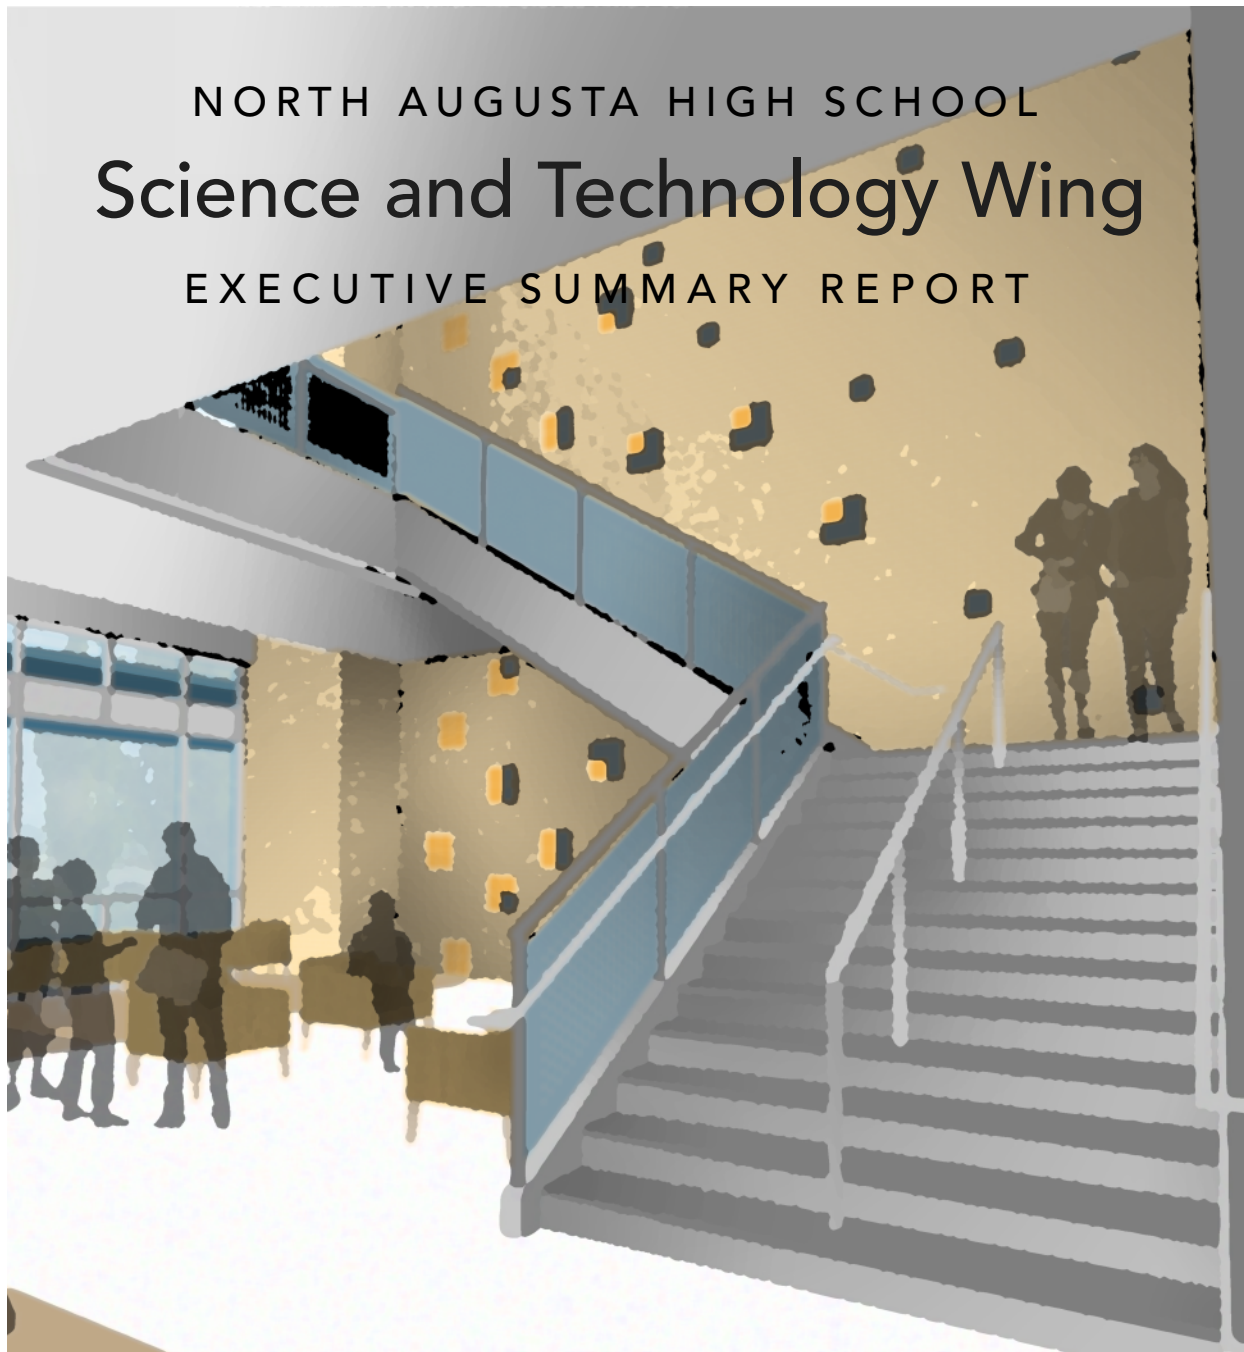

mcmillan | pazdan | smith
architecture

October 2014

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The General Contractor continues to coordinate the various scopes of work. The site preparation portion of the work is ongoing. Exterior brick application and painting of CMU walls is ongoing. Acoustical tile ceiling grid installation and window installation have begun. Roofing is ongoing and will be complete in the next few weeks. Mechanical, plumbing and electrical trades are progressing well.

PROJECT SCHEDULE:

- Substantial Completion: May 1, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$6,445,965

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Site preparation
- Roofing
- Brick Masonry
- Mechanical
- Plumbing
- Electrical



PROGRESS PHOTOS:




SOUTH WALL ELEVATION



EXTERIOR BRICK AND TILE



MECHANICAL PROGRESS

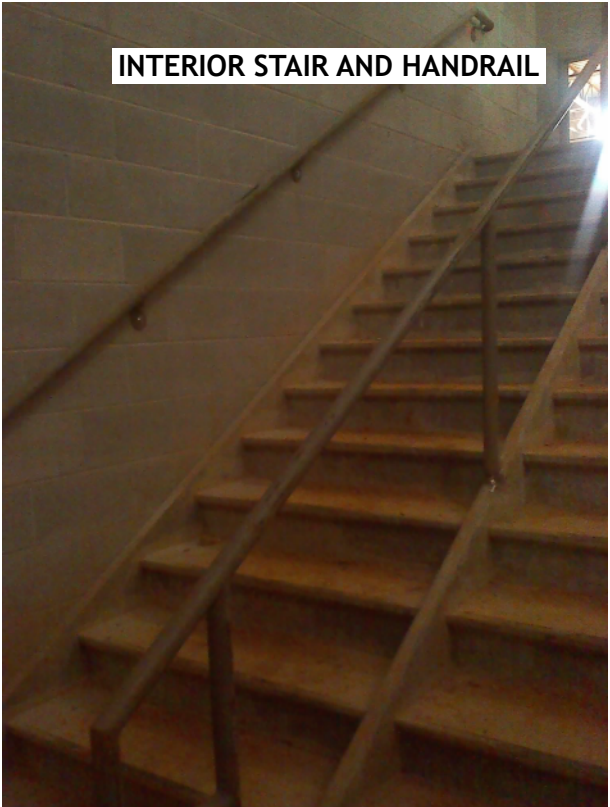

INTERIOR STAIR AND HANDRAIL

