


NORTH AUGUSTA HIGH SCHOOL
Science and Technology Wing
EXECUTIVE SUMMARY REPORT
FINAL REPORT

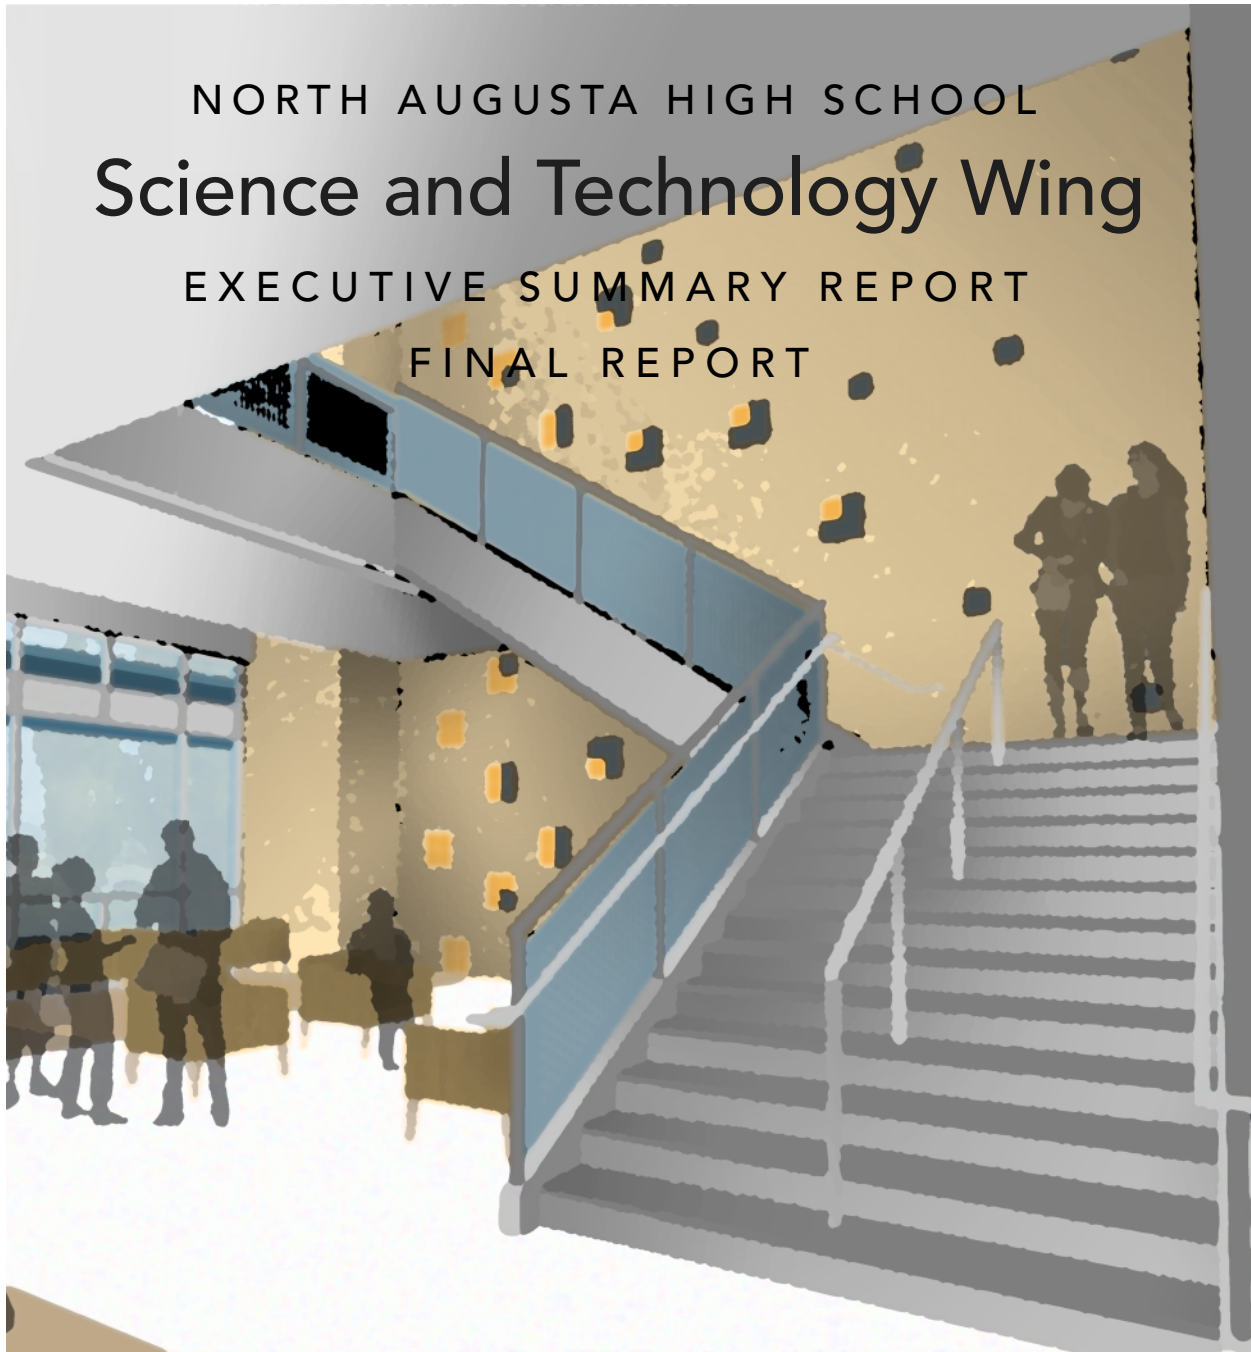

mcmillan | pazdan | smith
architecture

May 2015

NORTH AUGUSTA HIGH SCHOOL SCIENCE AND TECHNOLOGY WING

PROGRESS OF THE WORK:

The building has been determined to be substantially complete and the General Contractor is coordinating the effort to make the corrections noted in the final punchlist. Final closeout documents have been submitted for review.

PROJECT SCHEDULE:

- Substantial Completion Date: April 28, 2015

APPLICATIONS FOR PAYMENT:

- Original Contract Sum: \$10,357,000
- Net Change by Change Order: \$0
- Contract Sum to Date: \$10,357,000
- Amount Paid to Date: \$9,405,643

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:


There have been no requests for change order approved this month.

ACTIVITIES CURRENTLY UNDERWAY:

- Completion of final punchlist items.



FINAL PHOTOS:

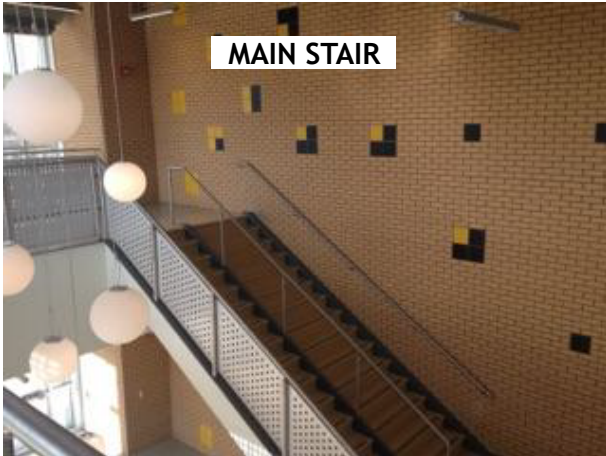

FINAL PHOTOS:



MAIN STAIR



EXTERIOR



CLASSROOM



EXTERIOR



CLASSROOM



EXTERIOR

