



RIDGE SPRING – MONETTA / PHASE ONE
NEW CLASSROOM BUILDING
Final Report

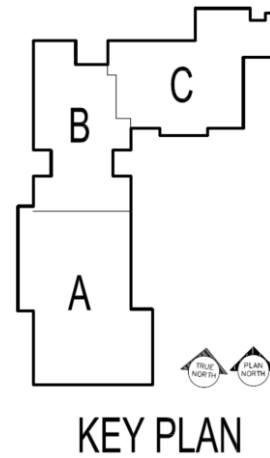

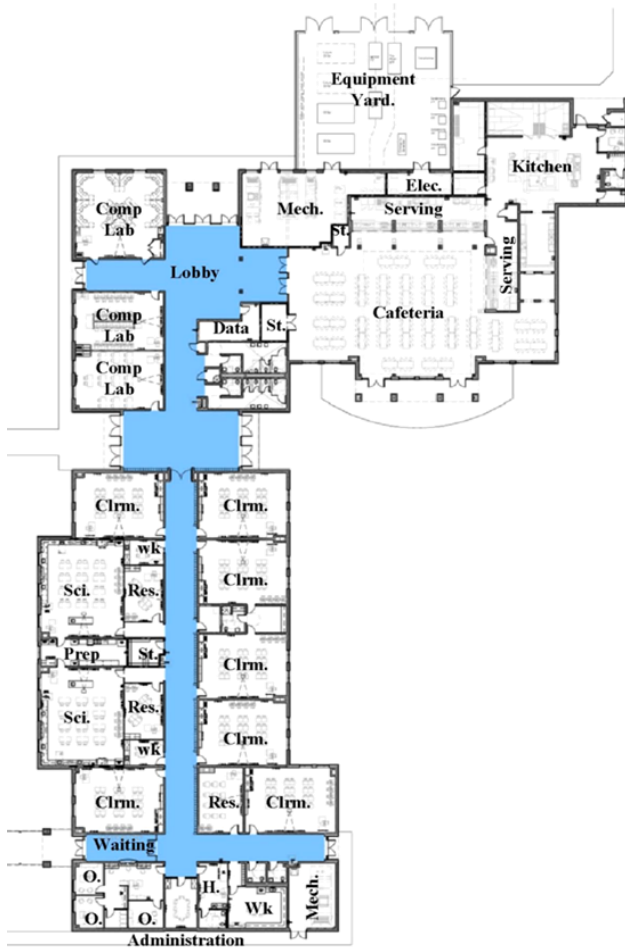

FINAL PROGRESS REPORT
RIDGE SPRING – MONETTA / PHASE ONE
NEW CLASSROOM BUILDING

1. SUMMARY: Contractors finishing punch list items

- OSF inspection complete, no return trip needed
- Canopy extension to High School still needed, this item added late in project

2. PROJECT SCHEDULE:

▪ Notice to Proceed:	February 20, 2013	
▪ Substantial Completion:	July 22 nd - actual date	

3. PROJECT ACCOUNTING:

▪ Original Contract Sum:		\$7,063,000.00
▪ Net Change by Change Orders:		\$145,126.00
▪ Contract Sum to Date:		\$7,208,126.00
▪ Completion as of last pay period	94%	\$6,828,099.00

4. APPROVED CHANGES:

- a. Canopy extension to the High School
-

Date: 8-8-14



William Ashlin, AIAI, CSI ALR Architecture





517 East Blvd. Suite #100 Charlotte, NC 28203 Phone: 704.348.2699 Fax: 704.348.939
