



mcmillan | pazdan | smith
ARCHITECTURE



AIKEN COUNTY
PUBLIC SCHOOLS



Midland Valley High School ADDITIONS

EXECUTIVE SUMMARY REPORT
JULY 2020

Midland Valley High School

ADDITIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site Work including Egress Sidewalks and Canopies
- Mechanical and Electrical Installation
- New Fire Alarm System in Existing Building
- Storefront Door Installation
- Ceiling Grid Installation
- Painting in Progress
- Epoxy Flooring in Progress
- Stairs in Progress
- Preparing to Install Emergency Generator
- Gym Floor in Progress

ACTIVITIES COMPLETE:

- Foundation/Slab Installation
- Plumbing Rough In
- Spray Foam and Rigid Insulation
- CMU Masonry Construction
- Brick Veneer
- Roofing Installation at Parapets nearing completion
- Metal Framing nearing completion
- Sprinkler Pipe Installation nearing completion

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2020

PROJECT SCHEDULE:

Original Contract Sum, Building:	\$14,500,900.00
Original Contract Sum, Sitework:	\$ 3,309,092.00
Original Contract Sum, Building & Site:	\$17,809,992.00
Net Change by Change Order:	\$0
Contract Sum to Date, Building & Site:	\$17,809,992.00
Amount Paid to Date, Building & Site:	\$10,474,396.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



AREA A - CAR LOOP



AREA A - CORRIDOR



AREA A - STUDENT ENTRANCE



AREA A - GYMNASIUM



AREA A - GYMNASIUM

AREA B - COURTYARD




AREA B - COURTYARD



AREA B - COURTYARD



AREA B - COURTYARD

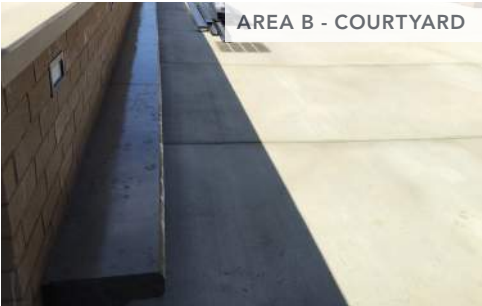


AREA B - DINING




AREA B - DINING



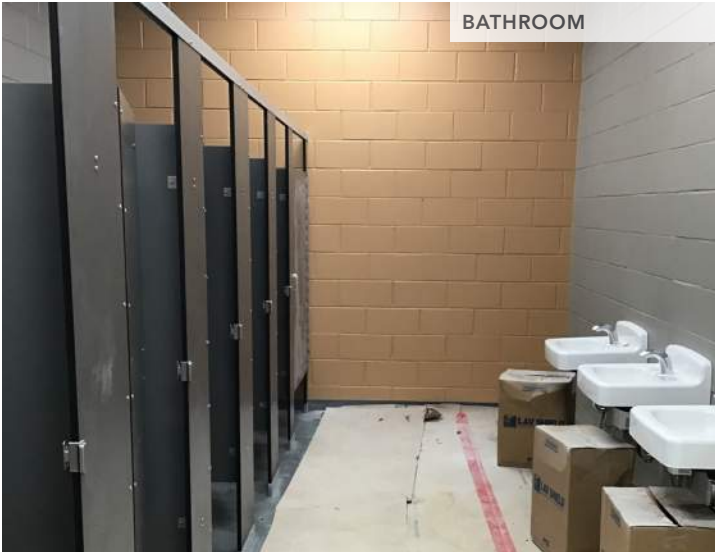


BATHROOM

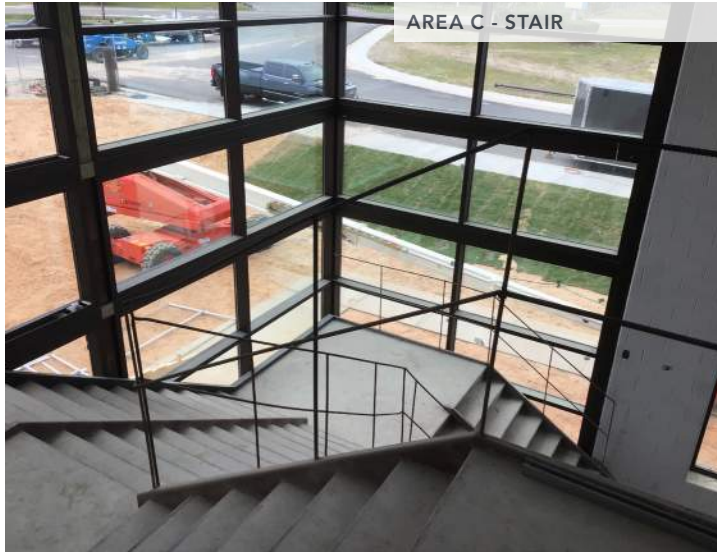

AREA C - STAIR



AREA C - NORTH FACADE

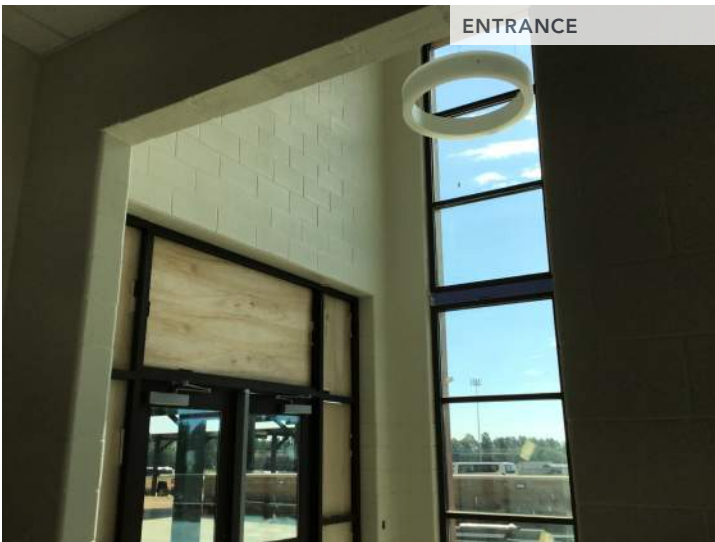

ENTRANCE



AREA C - SOUTH FACADE
