



mcmillan | pazdan | smith
ARCHITECTURE



AIKEN COUNTY
PUBLIC SCHOOLS



Midland Valley High School ADDITIONS

EXECUTIVE SUMMARY REPORT
MARCH 2020

Midland Valley High School

ADDITIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site Work Operations
- CMU Masonry Construction
- Sprinkler Pipe Installation
- Plumbing Rough In and Roof Drain Installation
- Electrical Installation
- Mechanical Preparation and Installation
- Steel Joist and Decking Installation
- Second Floor CMU Masonry and Steel Beams in Classroom Addition
- Metal Framing in Progress
- Spray Foam Insulation
- Brick on site, Preparing for Installation
- Egress Tunnel Constructed

ACTIVITIES COMPLETE:

- Foundation/Slab Installation

PROJECT SCHEDULE:


Substantial Completion Date: December 1, 2020

PROJECT SCHEDULE:

Original Contract Sum, Building:	\$14,500,900.00
Original Contract Sum, Sitework:	\$ 3,309,092.00
Original Contract Sum, Building & Site:	\$17,809,992.00
Net Change by Change Order:	\$0
Contract Sum to Date, Building & Site:	\$17,809,992.00
Amount Paid to Date, Building & Site:	\$ 6,446,072.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.

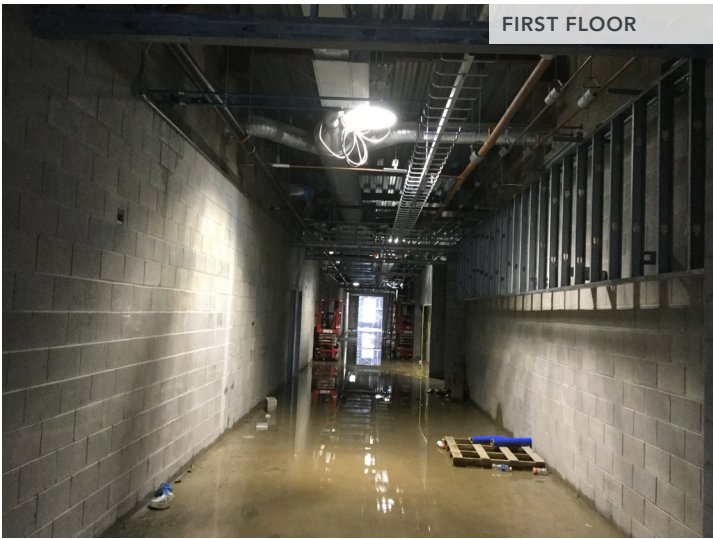

FIRST FLOOR



SECOND FLOOR



AREA C - CLASSROOM ADDITION



BRICK MOCK-UP



FRONT STAIR



AREA A - AUXILIARY GYM



AREA A - CLASSROOMS



AREA A - AUXILIARY GYM



AREA B - DINING



AREA A AND B - EGRESS TUNNEL BY COURTYARD
