

PHASE 2B ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

EXECUTIVE SUMMARY REPORT



**mcmillan
pazdan
smith**
ARCHITECTURE

June 2018

PHASE 2B ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

PHASE 2B

ACTIVITIES CURRENTLY UNDERWAY:

- Ground Floor Masonry Installation
- Door Frame Installation
- Plumbing
- Mechanical
- Electrical

ACTIVITIES COMPLETE:

- Foundation Installation
- Floor Slab Installation
- Ground Floor Masonry Installation

PROJECT SCHEDULE:

Substantial Completion Date: November 1, 2018

APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$39,984,978.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$39,984,978.00
Amount Paid to Date:	\$28,448,047.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



BUILDING PROGRESS PHOTOS:



CORRIDOR WALLS



METAL DECK INSTALLATION AT CORRIDOR




MECHANICAL SUPPORTS ABOVE CEILING



DAMP PROOFING EXTERIOR



BUILDING PROGRESS PHOTOS:

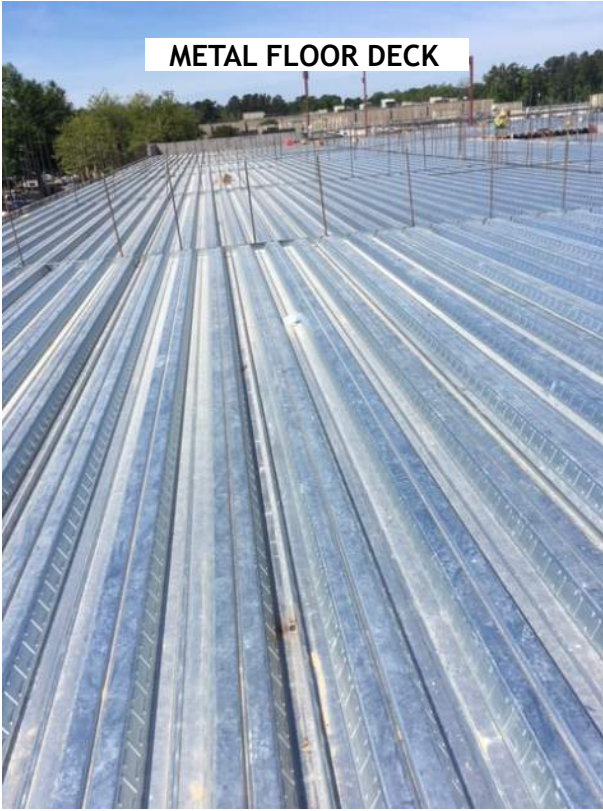

METAL FLOOR DECK



FIRST FLOOR CONCRETE SLAB



DOOR FRAMES FIRST FLOOR



CORRIDOR WATER FOUNTAIN ROUGH IN

