

# AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

## EXECUTIVE SUMMARY REPORT

---



AUGUST 2019

# AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

## ACTIVITIES CURRENTLY UNDERWAY:

- The cafeteria addition is largely complete.
- The administration addition is largely complete.
- On-site paving is complete and landscape and irrigation work are in progress.
- Site fencing is in progress and nearly complete.
- Furniture installation is in progress.
- The work in Areas 1 and 2 is largely complete and final cleaning is in progress.

## PROJECT SCHEDULE:

Notice to Proceed:	December 6, 2019
Substantial Completion Date:	August 2, 2019
<b>Schedule Status:</b>	<b>On Schedule</b>

## PROJECT ACCOUNTING: As of Application for Payment 8 dated 7/31/2019

- |                                       |                 |
|---------------------------------------|-----------------|
| • Original Contract Sum:              | \$ 5,938,100.00 |
| • Net Change by Change Orders:        | \$ 444,848.00   |
| • Contract Sum to Date:               | \$ 6,382,948.00 |
| • Total Completed and Stored to Date: | \$ 6,208,621.00 |


## APPROVED CHANGES:

- |       |   |
|-------|---|
| CO #1 | - Ramp Canopy                             |
| CO #2 | - Foodservice Equipment and DOT Revisions |
| CO #3 | - DOT ROW Revisions                       |
| CO #4 | - AT&T DOT Work                           |

## PENDING CHANGES:

None

## KEY PLAN

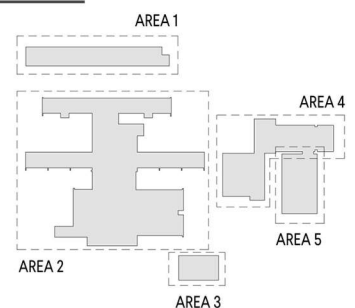

# AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

## BUILDING PROCESS IMAGES:



Progress photo of cafeteria addition exterior.



Progress photo of cafeteria addition exterior.



Progress photo of cafeteria addition interior.



Progress photo of courtyard space between Areas 1 and 2.



New covered entry walkway and building signage.



Furniture installation is in progress.
