

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



FEBRUARY 2020

MILLBROOK ELEMENTARY SCHOOL

ADDITION AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site fencing has been installed to establish the construction perimeter.
- The temporary bus loop has been installed.
- The temporary office space is in progress.
- Demolition of the first wing of the existing classroom building is in progress.
- Minor site demolition is in progress.
- The installation of temporary utilities for Phase 1 is in progress.

PROJECT SCHEDULE:

Notice to Proceed:	January 12, 2020
Substantial Completion Date:	August 12, 2021
Schedule Status:	On Schedule


PROJECT ACCOUNTING: No pay applications have been received.

• Original Contract Sum:	\$ 9,666,700.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 9,666,700.00
• Total Completed and Stored to Date:	\$ 0.00

APPROVED CHANGES: None

PENDING CHANGES: None

KEY PLAN

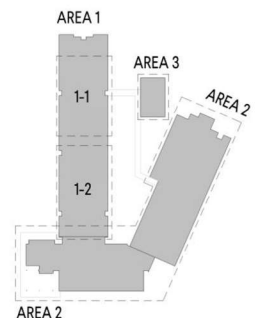

MILLBROOK ELEMENTARY SCHOOL

ADDITION AND RENOVATIONS

BUILDING PROCESS IMAGES:



Construction fencing has been installed.



Demolition is underway.




Construction barricades have been installed.



Temporary office space is under construction.



Sitework is underway to support the Phase 1 site conditions.

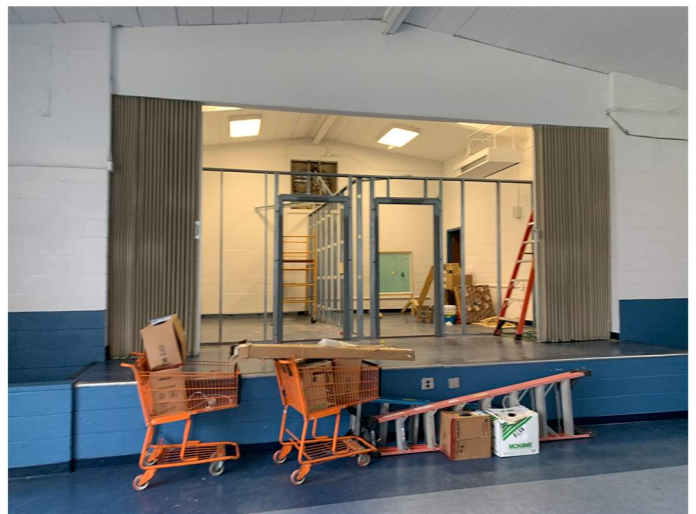

Temporary office space is under construction.
