



mcmillan | pazdan | smith
ARCHITECTURE



AIKEN COUNTY
PUBLIC SCHOOLS



Midland Valley High School ADDITIONS

EXECUTIVE SUMMARY REPORT
AUGUST 2020

Midland Valley High School

ADDITIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Casework, Millwork and Built-In Furniture in Progress
- Flooring in Progress
- Epoxy Flooring in Progress
- Site Work including Egress Sidewalks and Canopies
- Stairs
- Mechanical and Electrical Installation
- Painting
- Locker Installation
- Ceiling Grid Installation

ACTIVITIES COMPLETE:

- Gym Floor
- New Fire Alarm System in Existing Building
- Emergency Generator Installation
- Storefront Door Installation
- Straight Ladder Installed

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2020

PROJECT BUDGET:

Original Contract Sum, Building:	\$14,500,900.00
Original Contract Sum, Sitework:	\$ 3,309,092.00
Original Contract Sum, Building & Site:	\$17,809,992.00
Net Change by Change Order:	\$0
Contract Sum to Date, Building & Site:	\$17,809,992.00
Amount Paid to Date, Building & Site:	\$12,913,918.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.




AREA A - STUDENT ENTRANCE




AREA A - CORRIDOR



AREA A - STUDENT ENTRANCE

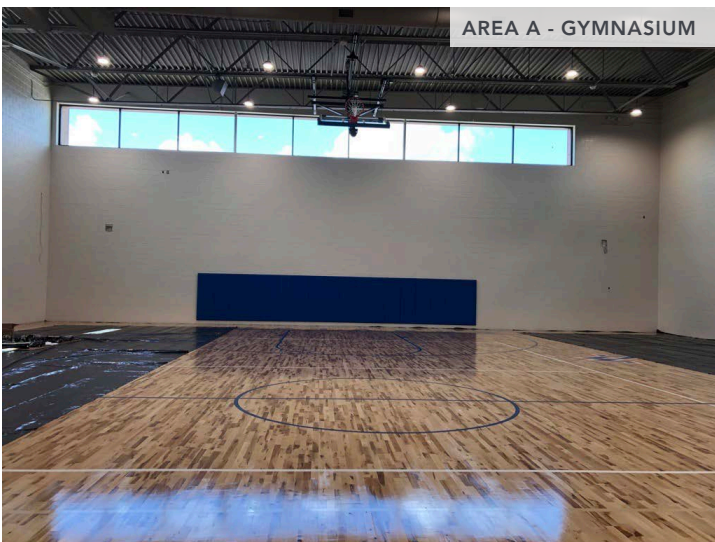

AREA A - GYMNASIUM

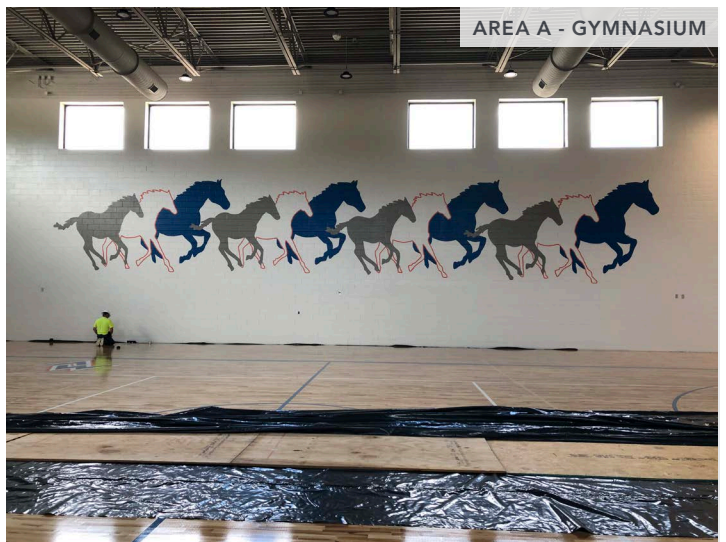

AREA A - GYMNASIUM




AREA B - COURTYARD



AREA B - CANOPY



AREA B - COURTYARD

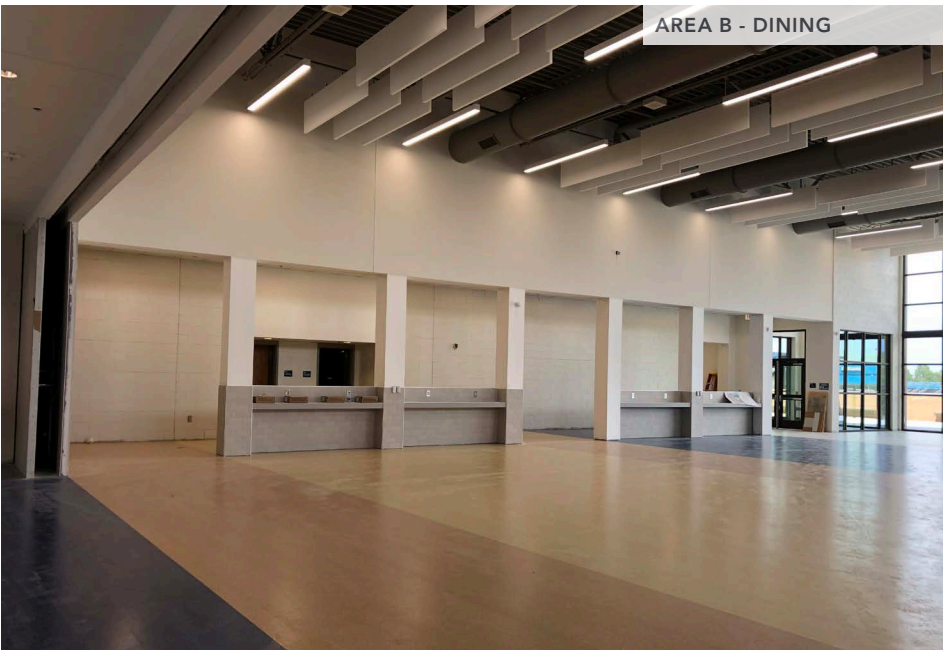

AREA B - DINING



AREA B - DINING




AREA C - NORTH FACADE



AREA C - NORTH FACADE



AREA C - NORTH/WEST FACADE

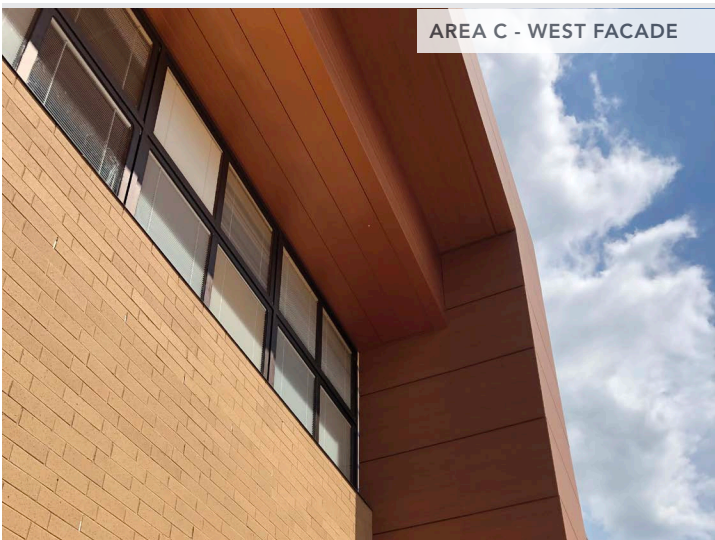

AREA C - WEST FACADE



AREA C - CORRIDOR
