



Midland Valley High School ADDITIONS

**EXECUTIVE SUMMARY REPORT
OCTOBER 2020**

Midland Valley High School

ADDITIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site Work including Sidewalks
- Painting
- Flooring and Stair Finishes
- Casework Installation

ACTIVITIES COMPLETE:

- Foundation/Slab Installation
- Plumbing Rough In
- CMU Masonry Construction
- Brick Veneer
- Roofing
- Metal Framing
- Sprinkler Pipe Installation
- New Fire Alarm System
- Mechanical and Electrical Installation
- Storefront Door and Window Installation
- Ceiling Grid Installation
- Gymnasium Bleachers and Basketball Goals
- Final OSF Inspections complete, with contingency items

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2020

PROJECT BUDGET:

Original Contract Sum, Building:	\$14,500,900.00
Original Contract Sum, Sitework:	\$ 3,309,092.00
Original Contract Sum, Building & Site:	\$17,809,992.00
Net Change by Change Order:	\$ 378,150.00
Contract Sum to Date, Building & Site:	\$18,188,142.00
Amount Paid to Date, Building & Site:	\$14,696,906.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:


Change Order Number 1 was approved on August 2020 for the Landscape and Irrigation work, and to install a Sound System in the existing Main Gym.



MAIN SCHOOL ENTRANCE AND BUS CANOPY



MAIN SCHOOL ENTRANCE

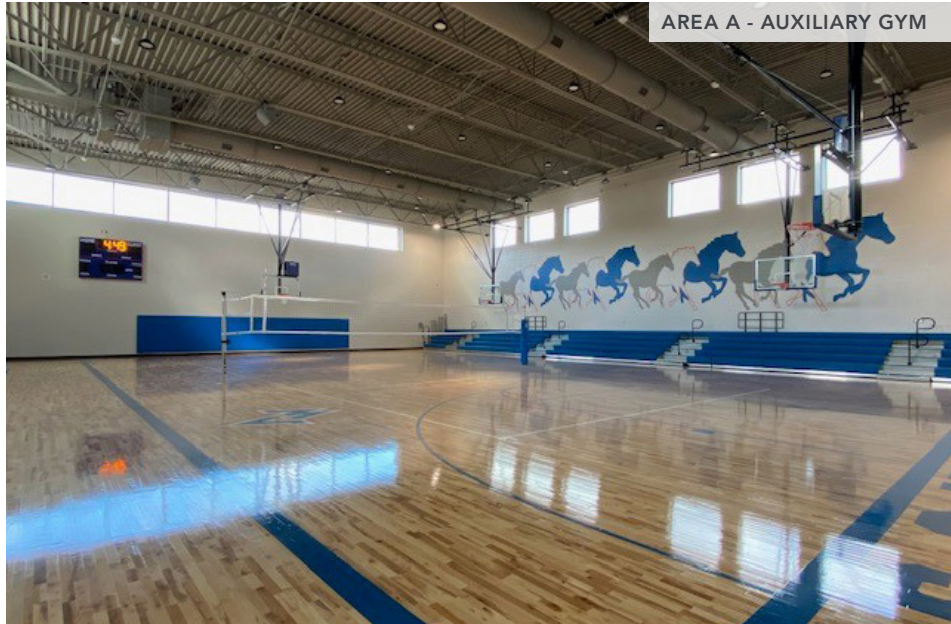

AREA A - AUXILIARY GYM



AREA A - ATHLETIC ADDITION



AREA B - DINING



AREA B - CORRIDOR



AREA C - MAIN STAIR




AREA C - MAIN STAIR




AREA C - ACADEMIC ADDITION



AREA C - SELF CONTAINED CLASSRM

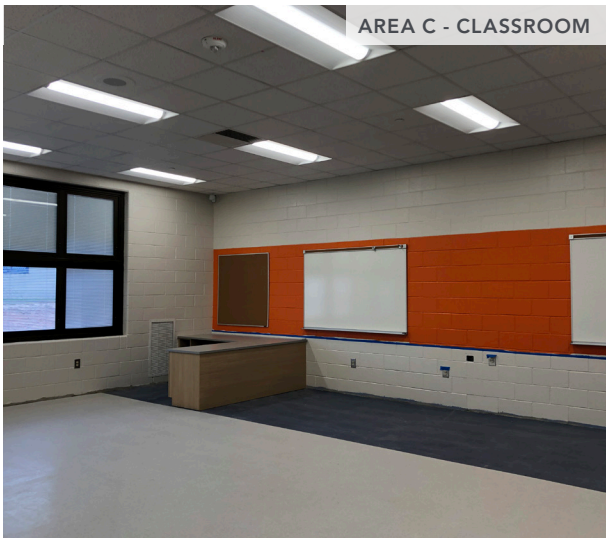

AREA C - CLASSROOM

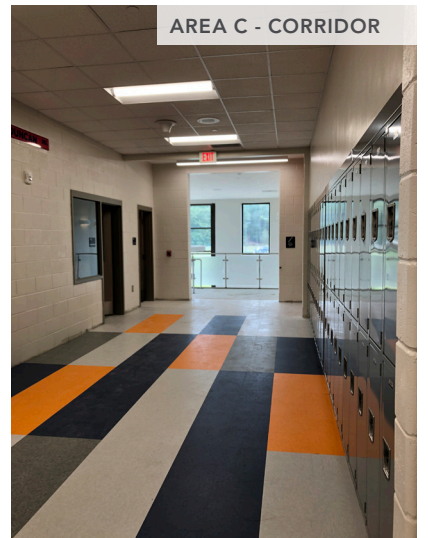

AREA C - CORRIDOR
