

Ridge Spring-Monetta Middle/High School

SUMMARY STATEMENT: Buildings "A", "B", "C" and "D" are Substantially Complete as of January 23, 2020 – OSF inspections were held January 9, 10 and 23, 2020.. Staff and students have moved into the new facility and started classes on January 28, 2020

PROJECT SCHEDULE: As of February 1, 2020:

• Notice to Proceed: August 17, 2018

• Substantial Completion: December 31, 2019 501 of 501 days (100%)

PROJECT ACCOUNTING: As of Application for Payment 16 dated 12/31/2019

• Original Contract Sum: \$32,217,171.00

• Net Change by Change Orders: \$ 0.00

• Contract Sum to Date: \$32,217,171.00

• Total Completed & Stored to Date: \$ 27,918,106.00

APPROVED CHANGES:

None.

PENDING CHANGES:

None.

ACTIVITIES UNDERWAY:

Punchlist work is in-progress.

PROGRESS PHOTOS:




Main Building - Front Elevation



Gymnasium Building – Front Elevations




Area "A" - 2nd Floor - Reading Room

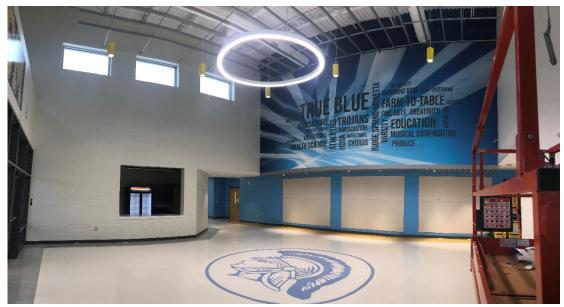

Area "D" – Gymnasium Lobby



Area "D" – Main Gym

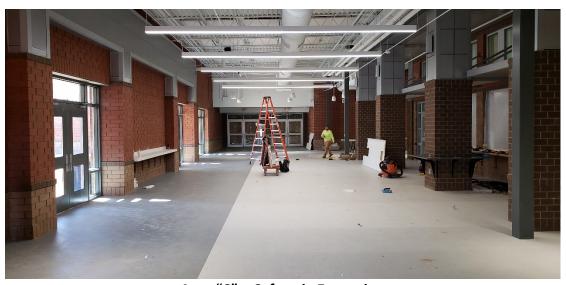

Area "C" - Cafeteria Expansion
