



# LS



**AIKEN COUNTY**  
PUBLIC SCHOOLS

## **AIKEN HIGH SCHOOL PHASE 2B ADDITIONS**

### **EXECUTIVE SUMMARY December 2018**

LS3P Project No. 2201-147220

# Aiken High School – Phase 2B Additions

**SUMMARY STATEMENT:** Both buildings are fully dried in with the exterior brick veneer and roofing substantially complete. Finishes are well underway at the ROTC/Band Building F with ceiling grid, hard tile flooring starting and painting ongoing. The overhead rough-ins continue throughout the Gym Building G. The entrance to F wing sitework is nearing completion with remaining masonry walls at planters. The electrician is pulling wire feeders throughout the ROTC/Band Building F in anticipation of permanent power next month.

## **PROJECT SCHEDULE: As of December 14, 2018**

- Notice to Proceed: December 5, 2017
- Substantial Completion 2B: April 1, 2019 374 of 482 days (78%)

## **PROJECT ACCOUNTING: As of Application for Payment 13 dated 12/10/2018**

- Original Contract Sum: \$ 16,084,080.00
- Net Change by Change Orders: \$ 0.00
- Contract Sum to Date: \$ 16,084,080.00
- Total Completed & Stored to Date: \$ 10,081,888.00

## **APPROVED CHANGES:**

- None.


## **PENDING CHANGES:**

- None.

## **ACTIVITIES UNDERWAY:**

- Completing brick planter walls at entrance sidewalk and courtyards
- Installing MEP overhead in Gym/Art Building G
- Insulating ductwork in ROTC/Band Building F
- Painting in both buildings
- Last remaining window glazing is installed
- Pulling wire in ROTC Band Building F
- Hard tile flooring at Culinary
- Kitchen hoods set
- Gym/Art Building G stairs are ready to be poured

# Aiken High School Campus Key Plan

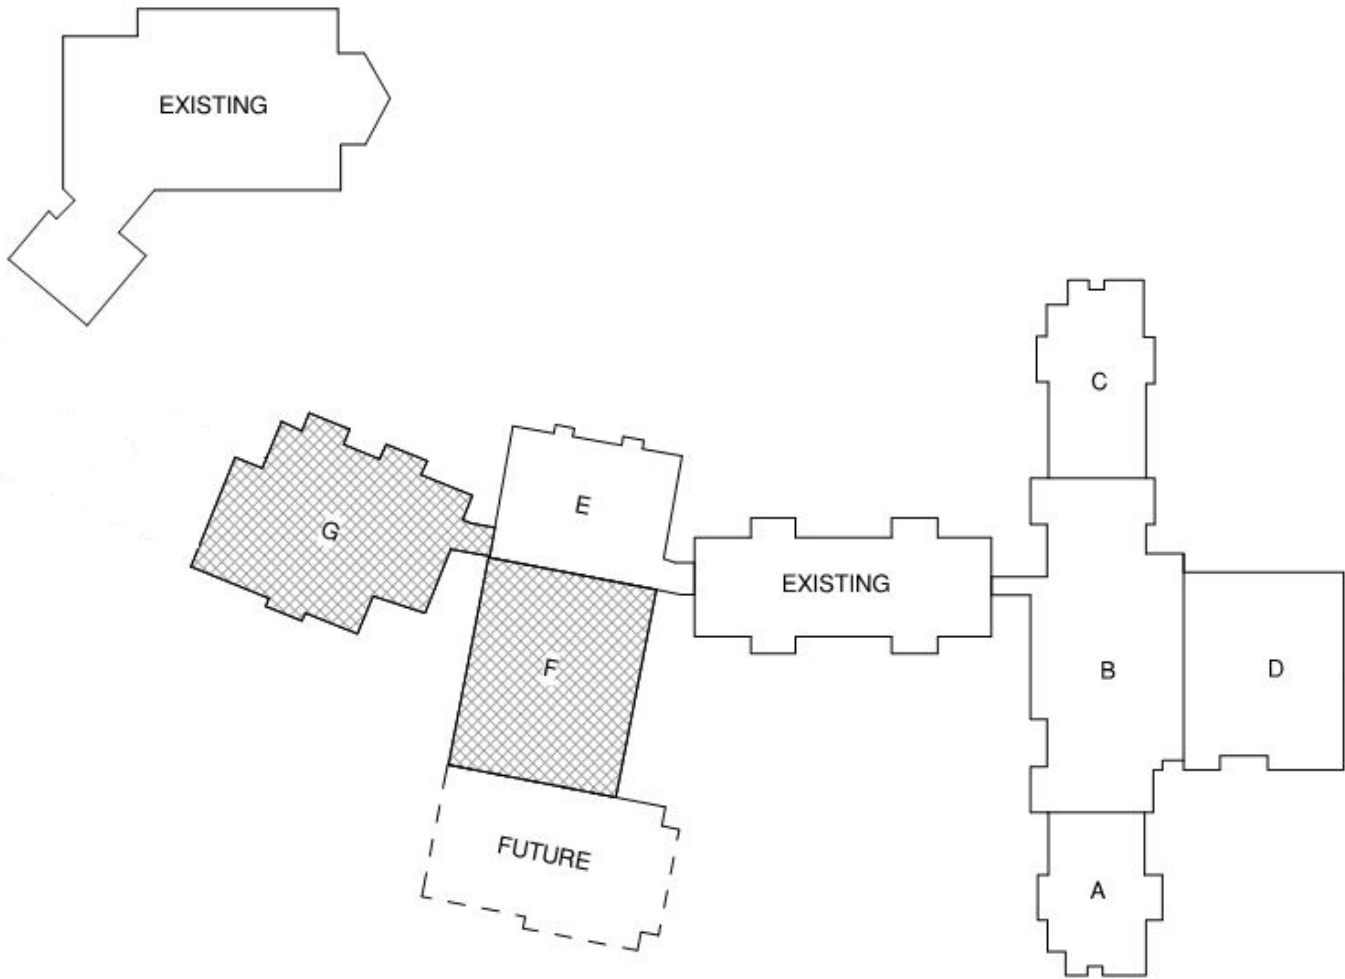

**PROGRESS PHOTOS:**



**Glass windows in, some painting started and overhead rough-in continues in Gym**



**Recent ceiling grid installation along the ROTC/Band corridor**



**Completing planter precast at entrance**



**Painting and hard tile in Culinary area**
