

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



MAY 2019

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Sheathing and waterproofing have been installed on new foodservice addition.
- Interior metal stud framing is in progress in new foodservice addition.
- Interior / exterior metal stud framing is in progress at new cafeteria addition.
- New concrete slab has been installed at new cafeteria addition.
- The kitchen area has been prepped for the new concrete slab.
- Storefront windows have been installed in Area 1.
- Painting of the existing canopies is in progress.
- Wall tile installation is in progress.
- Millwork installation is in progress.

PROJECT SCHEDULE:

Notice to Proceed:	December 6, 2019
Substantial Completion Date:	August 2, 2019
Schedule Status:	On Schedule

PROJECT ACCOUNTING: As of Application for Payment 5 dated 4/19/2019 (and including CO #3)

• Original Contract Sum:	\$ 5,938,100.00
• Net Change by Change Orders:	\$ 341,646.00
• Contract Sum to Date:	\$ 6,279,746.00
• Total Completed and Stored to Date:	\$ 3,274,262.00


APPROVED CHANGES:

CO #1	- Ramp Canopy
CO #2	- Foodservice Equipment and DOT Revisions
CO #3	- DOT ROW Revisions

PENDING CHANGES:

None

KEY PLAN

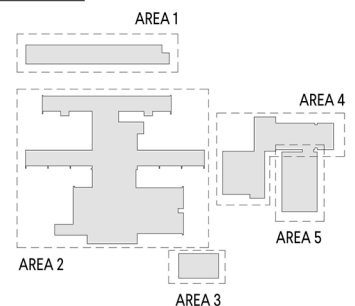

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

BUILDING PROCESS IMAGES:



New storefront windows installed in Area 1.



Interior framing in progress for foodservice administration addition.



Slab prep work for new kitchen slab.



Wall tile installation is in progress in renovated restrooms.



Framing is in progress for new cafeteria addition.



New window openings in cafeteria addition.
