

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



JULY 2019

AREA 3 GRANITEVILLE ELEMENTARY

ADDITIONS AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site fencing installation is in progress.
- Site paving work is in progress with new sidewalks largely complete.
- Block outs for new site canopies have been installed.
- Ceiling grid has been installed for the new administration addition and the renovated kitchen.
- Window film has been installed on the storefront at the exterior access classrooms.
- Storefront installation is largely complete.
- The new cafeteria addition is dried in and sheetrock installation is largely complete.

PROJECT SCHEDULE:

Notice to Proceed:	December 6, 2019
Substantial Completion Date:	August 2, 2019
Schedule Status:	On Schedule

PROJECT ACCOUNTING: As of Application for Payment 7 dated 6/30/2019

• Original Contract Sum:	\$ 5,938,100.00
• Net Change by Change Orders:	\$ 444,848.00
• Contract Sum to Date:	\$ 6,382,948.00
• Total Completed and Stored to Date:	\$ 5,588,902.00


APPROVED CHANGES:

CO #1	- Ramp Canopy
CO #2	- Foodservice Equipment and DOT Revisions
CO #3	- DOT ROW Revisions
CO #4	- AT&T DOT Work

PENDING CHANGES:

None

KEY PLAN

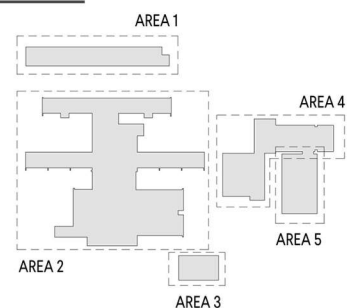

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

BUILDING PROCESS IMAGES:



Progress photo of cafeteria addition exterior.




Progress photo of cafeteria addition exterior.



Progress photo of cafeteria addition interior.



Progress photo of administration addition interior.

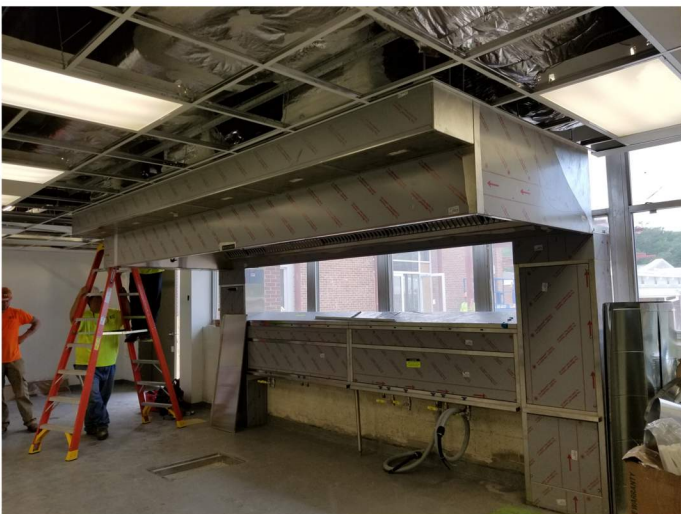

Kitchen hood and interior progress.



Site paving preparation and exterior fencing installation.
