

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

FINAL EXECUTIVE SUMMARY REPORT



SEPTEMBER 2019
FINAL

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- The project is largely complete.
- OSF approved occupancy for the building.
- The ribbon cutting was held on August 10th.
- The building opened on time for the first day of school on August 19th.
- The General Contractor is on site completing punch list items.
- Final Completion is scheduled for September.

PROJECT SCHEDULE:

Notice to Proceed:	December 6, 2019
Substantial Completion Date:	August 2, 2019 (This date was met)
Schedule Status:	On Schedule

PROJECT ACCOUNTING: As of Application for Payment 9 dated 8/31/2019

- | | |
|---------------------------------------|-----------------|
| • Original Contract Sum: | \$ 5,938,100.00 |
| • Net Change by Change Orders: | \$ 444,848.00 |
| • Contract Sum to Date: | \$ 6,382,948.00 |
| • Total Completed and Stored to Date: | \$ 6,370,715.00 |


APPROVED CHANGES:

- | | |
|-------|---|
| CO #1 | - Ramp Canopy |
| CO #2 | - Foodservice Equipment and DOT Revisions |
| CO #3 | - DOT ROW Revisions |
| CO #4 | - AT&T DOT Work |

PENDING CHANGES:

None

KEY PLAN

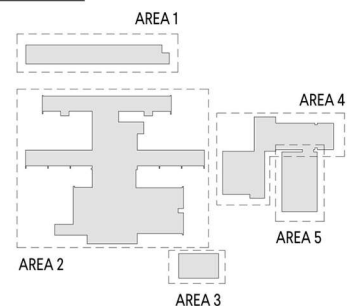

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

BUILDING PROCESS IMAGES:




Ribbon cutting outside new cafeteria.



Ribbon cutting activities inside new cafeteria.



Ribbon cutting activities inside new cafeteria.

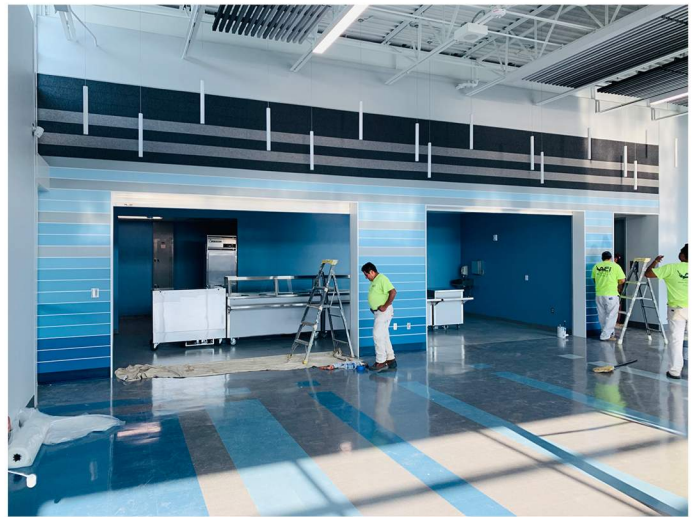

New serving line.



Side view of new cafeteria addition.



New furniture in media center.
