



# PHASE 1 RENOVATIONS & ADDITIONS TO HAMMOND HILL ELEMENTARY SCHOOL

EXECUTIVE SUMMARY REPORT  
DECEMBER 2021



# HAMMOND HILL ELEMENTARY SCHOOL RENOVATIONS AND ADDITIONS

---

## PHASE I ACTIVITIES CURRENTLY UNDERWAY:

- Work continues on the new 2-story classroom addition. Final grading of playground areas and new vehicular cueing lanes is in progress.
- Installation of aluminum canopy at the new drop-off/pickup driveway is complete.
- Installation of solar window shades is complete.
- Existing administration building is currently being reroofed.
- New sanitary sewer lift station has been installed. Underground installation of new sewer force main is nearing completion.
- Installation of ceiling grid is complete at both floor levels
- Installation of interior lights at both floor levels is complete. Exterior lights are currently being installed.
- Fire riser piping and valves have been installed.
- Cabinetry is currently being installed in the new classrooms.
- Installation of new elevator is complete.
- Plumbing fixtures are currently being installed.
- OSF above ceiling inspection was completed November 10th. Minor infractions were identified and are currently being corrected.

## PROJECT SCHEDULE:

Notice to Proceed:	November 16, 2020
Substantial Completion Date Phase 1:	January 14, 2022
Substantial Completion Date Phase 2:	March 24, 2023
Schedule Status:	The project is on schedule.

## PROJECT BUDGET:

Original Contract Sum:	\$15,240,600.00
Net Change by Change Orders:	\$0.00
Contract Sum to Date:	\$15,240,600.00
Total Completed and Stored to Date:	\$9,251,854.00

**APPROVED CHANGES:** None








*NEW 2-STORY CLASSROOM ADDITION EXTERIOR*



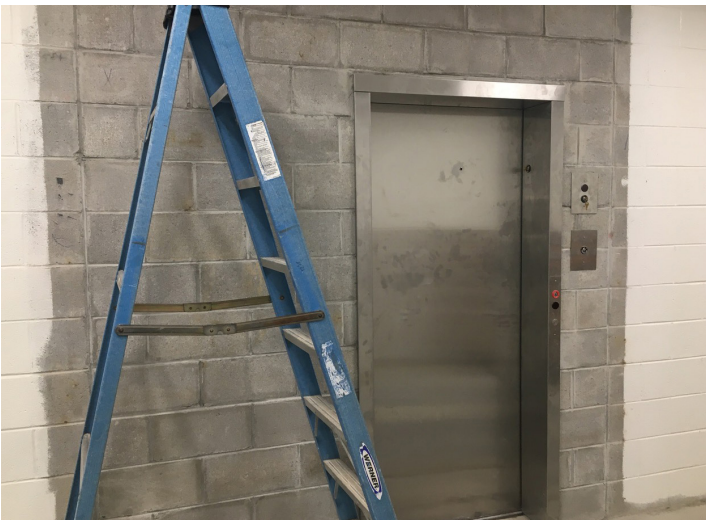

*NEW 2-STORY CLASSROOM ADDITION INTERIOR*
