

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



SEPTEMBER 2021

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- The campus is fully occupied and operating.
- The new stacking drive and associated site area is in progress.

PROJECT SCHEDULE:

Notice to Proceed:	January 12, 2020
Substantial Completion Date:	October 22, 2021
Schedule Status:	The building is scheduled to be complete in June 2021. The site is on target to open for August 2021 w/ about 10 weeks of miscellaneous work to occur after the start of school due to rain delays and other unforeseen conditions.


PROJECT ACCOUNTING: (As of Pay Application #20, dated 09.30.21)

• Original Contract Sum:	\$ 9,666,700.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 9,666,700.00
• Total Completed and Stored to Date:	\$ 8,503,414.39

APPROVED CHANGES: None

PENDING CHANGES: None

KEY PLAN

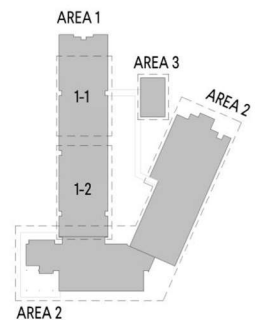

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

BUILDING PROCESS IMAGES:



The campus is fully occupied.



Exterior progress photo.



Exterior progress photo.



Exterior progress photo.



Exterior progress photo.



Exterior progress photo.
