

# MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

## EXECUTIVE SUMMARY REPORT

---



OCTOBER 2021

# MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

## ACTIVITIES CURRENTLY UNDERWAY:

- The campus is fully occupied and operating.
- The new stacking drive and associated site area is in progress.
- Curb in this area is generally complete.
- Gravel and paving are underway.
- Final canopy installation is in progress.

## PROJECT SCHEDULE:

Notice to Proceed:	January 12, 2020
Substantial Completion Date:	December 6, 2021
<b>Schedule Status:</b>	<b>The building is complete and the site is operational. Due to rain delays and unforeseen conditions, the substantial completion date has been extended.</b>


## PROJECT ACCOUNTING: (As of Pay Application #20, dated 09.30.21)

• Original Contract Sum:	\$ 9,666,700.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 9,666,700.00
• Total Completed and Stored to Date:	\$ 8,503,414.39

**APPROVED CHANGES:** None

**PENDING CHANGES:** None

## KEY PLAN

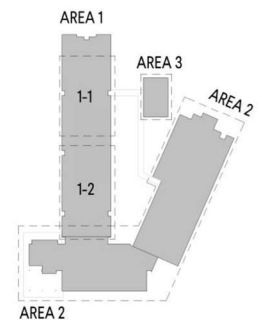



# MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

## BUILDING PROCESS IMAGES:



Exterior progress photo. Curb installation is in progress.



Exterior progress photo. Canopy installation is in progress.



Exterior progress photo. Curb installation is in progress.



Exterior progress photo. Curb installation is in progress.



Exterior progress photo.



Exterior progress photo.
