

PHASE III ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

EXECUTIVE SUMMARY REPORT



**mcmillan
pazdan
smith**
ARCHITECTURE

November 2019

PHASE III ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

ACTIVITIES CURRENTLY UNDERWAY:

- Grading Operations
- Storm Drainage Installation
- Foundation Installation
- Concrete for Slabs
- Masonry Foundations
- Electrical
- Plumbing

ACTIVITIES COMPLETE:

- None

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2020

APPLICATIONS FOR PAYMENT:

Original Contract Sum: \$16,305,245.00

Net Change by Change Order: \$0

Contract Sum to Date: \$16,305,245.00

Amount Paid to Date: \$253,404.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



PROGRESS PHOTOS:




FOUNDATION INSTALLED



UNDERSLAB INSTALLATION



PROGRESS PHOTOS:

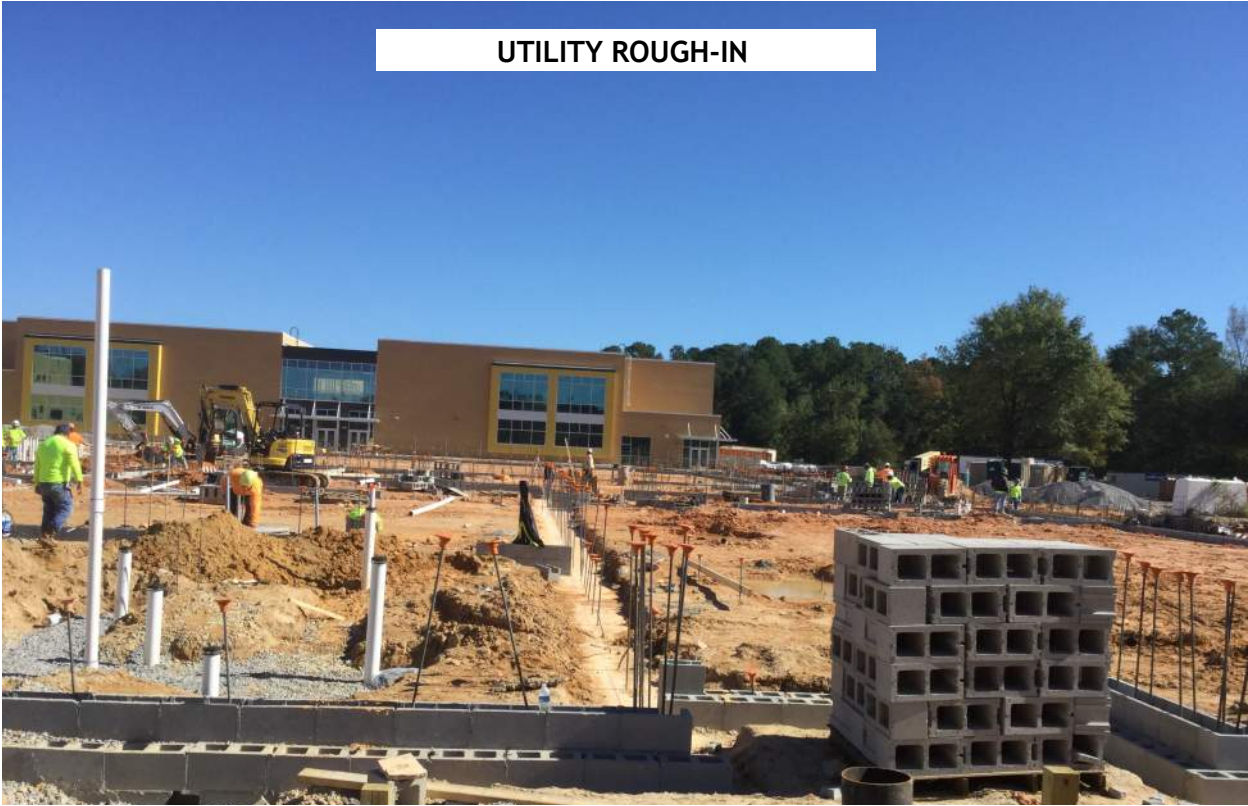

UTILITY ROUGH-IN



SLAB PREPARATION
