

AREA 3 GRANITEVILLE ELEMENTARY ADDITIONS AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



FEBRUARY 2019

AREA 3 GRANITEVILLE ELEMENTARY

ADDITIONS AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site demolition, preliminary grading, and site utility work are ongoing.
- Building demolition work is ongoing.
- The group restrooms have been completely demolished.
- New plumbing infrastructure is being installed.
- Windows scheduled for demolition in Areas 1 and 2 have been removed.
- Demolition work is complete in the existing kitchen building in Area 4.
- Electrical infrastructure work is underway.

PROJECT SCHEDULE:

Notice to Proceed:	December 6, 2019
Substantial Completion Date:	August 2, 2019

PROJECT ACCOUNTING: As of Application for Payment 2 dated 1/25/2019

• Original Contract Sum:	\$ 5,938,100.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 5,938,100.00
• Total Completed and Stored to Date:	\$ 715,295.01


APPROVED CHANGES:

None

PENDING CHANGES:

CO #1 - Ramp Canopy
CO #2 - Foodservice Equipment and DOT Revisions

KEY PLAN

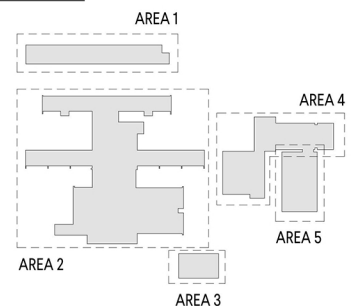

AREA 3 GRANITEVILLE ELEMENTARY

ADDITIONS AND RENOVATIONS

BUILDING PROCESS IMAGES:



SITE GRADING UNDERWAY



EXISTING WINDOWS HAVE BEEN REMOVED



EXISTING RESTROOMS HAVE BEEN DEMOLISHED



EXISTING KITCHEN HAS BEEN DEMOLISHED



NEW PLUMBING IS BEING INSTALLED



GENERAL BUILDING DEMOLITION IS UNDERWAY
