



# MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS


## EXECUTIVE SUMMARY REPORT




**SOUTH ELEVATION**  
SECTION




**EAST ELEVATION**  
SECTION




**NORTH ELEVATION**  
SECTION





**WEST ELEVATION**  
SECTION

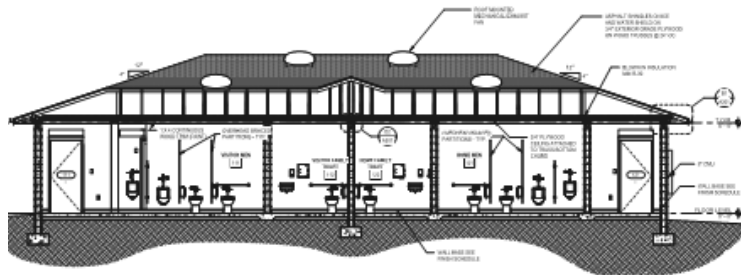

**BUILDING CROSS SECTION - VISITOR MEN/MEN**  
SECTION

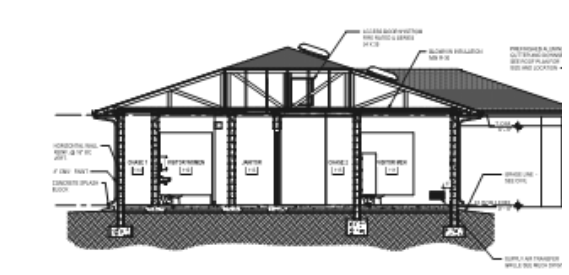

**BUILDING CROSS SECTION**  
SECTION



**mcmillan  
pazdan  
smith**  
ARCHITECTURE

# MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS

## ACTIVITIES CURRENTLY UNDERWAY:

- Masonry Installation
- Door Frame Installation
- Plumbing
- Mechanical
- Electrical
- Site Work

## ACTIVITIES COMPLETE:

- Foundation Installation
- Floor Slab Installation

## PROJECT SCHEDULE:

Substantial Completion Date: July 15, 2018

## APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$798,000.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$798,000.00
Amount Paid to Date:	\$285,817.00

## REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



**BUILDING PROGRESS PHOTOS:**

**DOOR FRAMES INSTALLATION**



**CONCRETE BLOCK INSTALLATION**



**BUILDING PROGRESS PHOTOS:**



**WATER LINE INSTALLATION**



**PLUMBING ROUGH IN**

