



SILVER BLUFF HIGH SCHOOL STADIUM RESTROOMS


EXECUTIVE SUMMARY REPORT

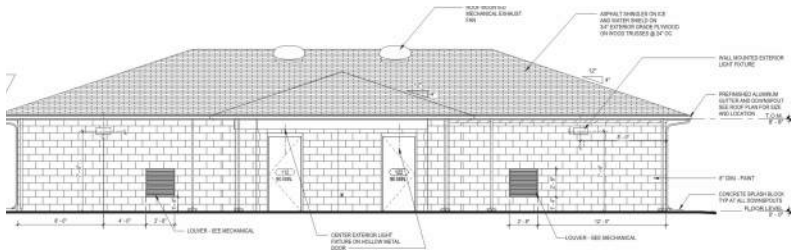


7
SOUTH ELEVATION
1/4" = 1'-0"

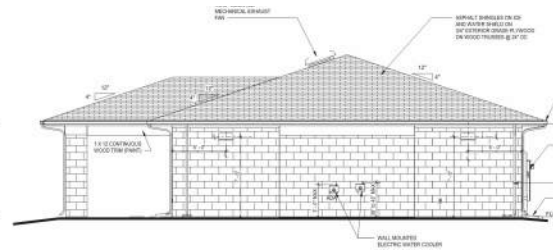


8
EAST ELEVATION
1/4" = 1'-0"

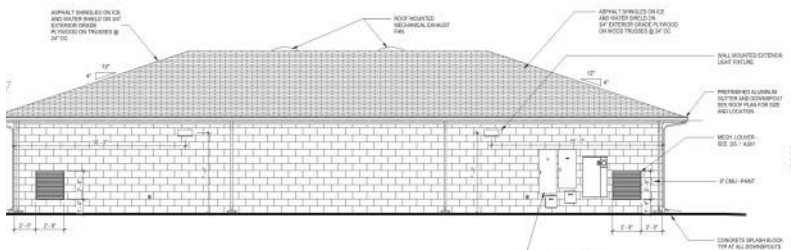


9
NORTH ELEVATION
1/4" = 1'-0"

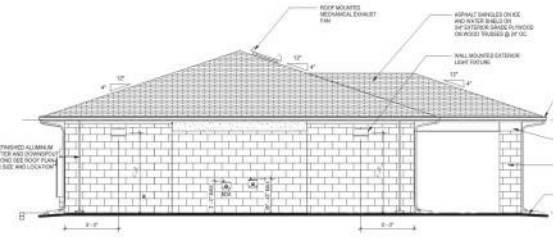



10
WEST ELEVATION
1/4" = 1'-0"

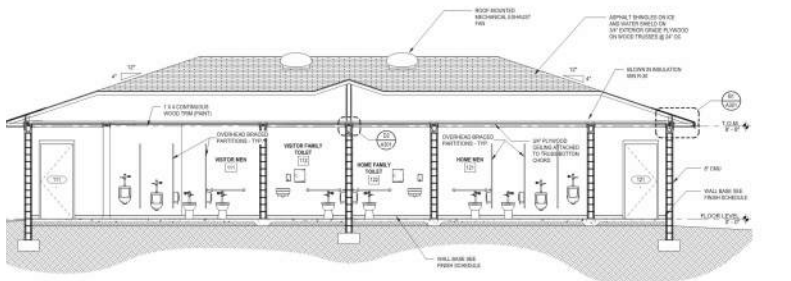

11
BUILDING CROSS SECTION - VISITOR MEN/HOME MEN
1/4" = 1'-0"

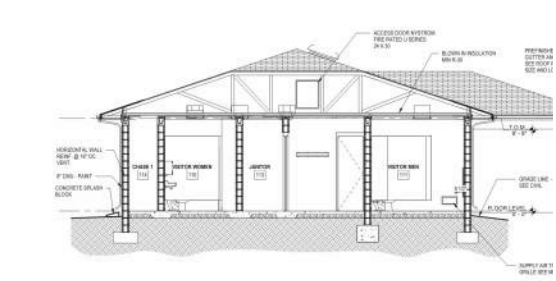

12
BUILDING CROSS SECTION
1/4" = 1'-0"



**mcmillan
pazdan
smith**
ARCHITECTURE

SILVER BLUFF HIGH SCHOOL STADIUM RESTROOMS

ACTIVITIES CURRENTLY UNDERWAY:

- Plumbing
- Electrical
- Roofing
- Site Work

ACTIVITIES COMPLETE:

- Foundation Installation
- Floor Slab Installation
- Masonry Installation
- Door Frame Installation
- Sewer

PROJECT SCHEDULE:

Substantial Completion Date: July 15, 2019

APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$796,000.00
Net Change by Change Order:	\$0.00
Contract Sum to Date:	\$796,000.00
Amount Paid to Date:	\$91,819.75

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:



BUILDING PROGRESS PHOTOS:



WATER LINE INSTALLATION



PLUMBING ROUGH-IN

BUILDING PROGRESS PHOTOS:

