



# SOUTH AIKEN HIGH SCHOOL TOILETS AND CONCESSIONS

## EXECUTIVE SUMMARY REPORT



**BUILDING SECTION**  
1/8" = 1'-0"




**BUILDING SECTION**  
1/8" = 1'-0"




**ELEVATION @ RATED ACCESS DOORS**  
1/8" = 1'-0"




**WEST ELEVATION**  
1/8" = 1'-0"




**EAST ELEVATION**  
1/8" = 1'-0"



1/8" = 1'-0"



1/8" = 1'-0"



1/8" = 1'-0"



**mcmillan  
pazardan  
smith**  
ARCHITECTURE

# SOUTH AIKEN HIGH SCHOOL TOILETS AND CONCESSIONS

## ACTIVITIES IN PROGRESS:

- Sitework
- Plumbing
- Electrical
- Sidewalks
- Interior Finishes
- Exterior Finishes

## ACTIVITIES COMPLETE:

- Concrete Footings
- Concrete Slab
- CMU
- Chase Walls
- Roof Trusses

## PROJECT SCHEDULE:

Substantial Completion Date: August 1, 2017

## APPLICATIONS FOR PAYMENT:

Original Contract Sum: \$693,544.00

Net Change by Change Order: \$0

Contract Sum to Date: \$693,544.00

Amount Paid to Date: \$496,475.00

## REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



**EXTERIOR FINISHES**



**NEW SIDEWALK**



**ELECTRICAL CONDUIT**




**DUCT INSTALLATION**



**MEN'S TOILETS**



**WOMEN'S TOILETS**

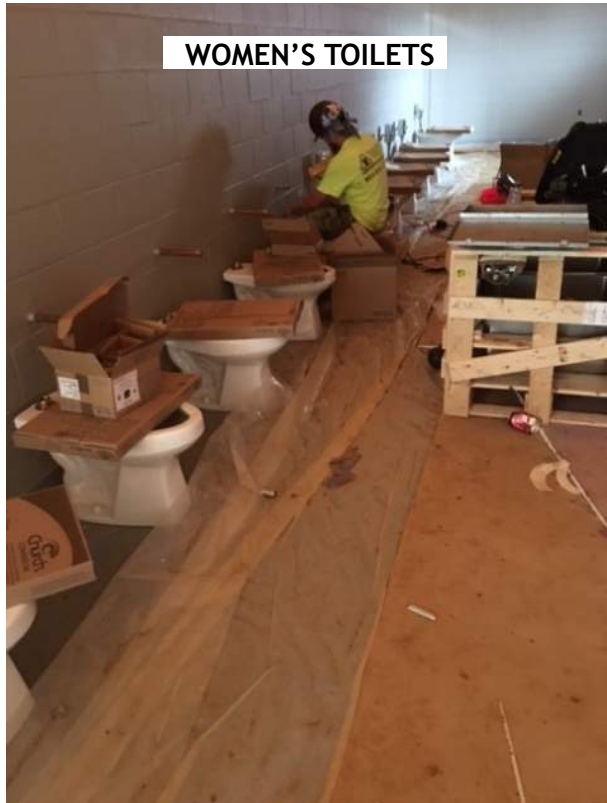

**CONCESSIONS SINK**



**TOILET ROOM SINKS**

