

SOUTH AIKEN HIGH SCHOOL TOILETS AND CONCESSIONS

ACTIVITIES IN PROGRESS:

- Sitework
- Electrical
- Sidewalks

ACTIVITIES COMPLETE:

- Concrete Footings
- Concrete Slab
- CMU
- Chase Walls
- Roof Trusses
- Plumbing
- Interior Finishes
- Exterior Finishes

PROJECT SCHEDULE:

Substantial Completion Date: August 1, 2017

APPLICATIONS FOR PAYMENT:

Original Contract Sum: \$693,544.00

Net Change by Change Order: \$0

Contract Sum to Date: \$693,544.00

Amount Paid to Date: \$496,475.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.





ROLLUP DOOR AT CONCESSIONS STAND



CONCESSIONS COUNTER



CONCESSIONS



CONCESSIONS SINK






WOMEN'S TOILET ROOM



FAMILY TOILET ROOM



HAND WASH SINK

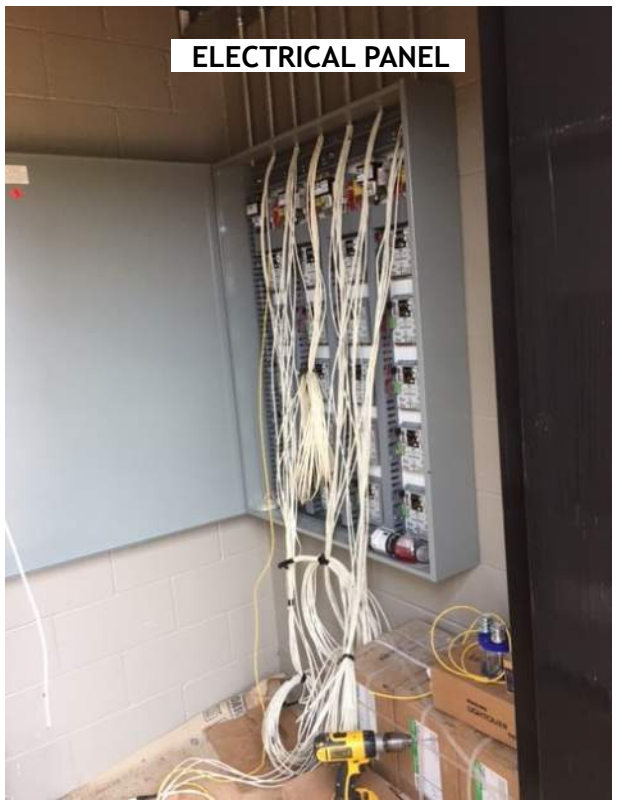

ELECTRICAL PANEL

