


# MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS


## EXECUTIVE SUMMARY REPORT




**SOUTH ELEVATION**  
SECTION




**EAST ELEVATION**  
SECTION




**NORTH ELEVATION**  
SECTION





**WEST ELEVATION**  
SECTION

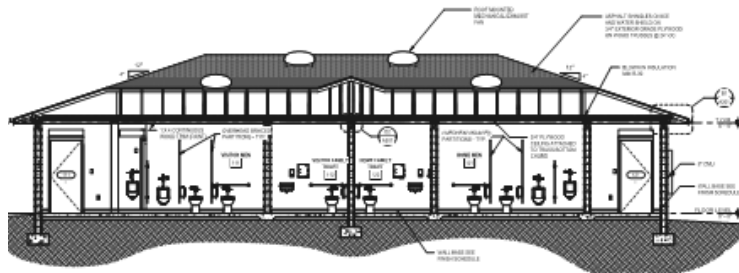

**BUILDING CROSS SECTION - VISITOR MEN/MEN**  
SECTION

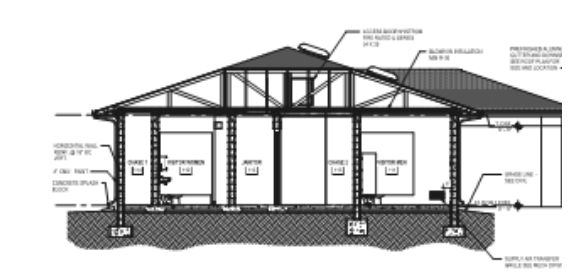

**BUILDING CROSS SECTION**  
SECTION



**mcmillan  
pazdan  
smith**  
ARCHITECTURE

# MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS

## ACTIVITIES CURRENTLY UNDERWAY:

- Punch List
- Review of Closeout Documents

## ACTIVITIES COMPLETE:

- All work is complete.

## PROJECT SCHEDULE:

Substantial Completion Date: August 10, 2018

## APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$798,000.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$798,000.00
Amount Paid to Date:	\$722,902.00

## REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



**BUILDING PROGRESS PHOTOS:**



**VIEW FROM FIELD**



**FAMILY TOILET ENTRANCES**

