

PHASE III ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

EXECUTIVE SUMMARY REPORT



**mcmillan
pazdan
smith**
ARCHITECTURE

August 2020

PHASE III ADDITIONS TO NORTH AUGUSTA HIGH SCHOOL

ACTIVITIES CURRENTLY UNDERWAY:

- Electrical
- Plumbing
- Mechanical
- Lockers and Bleachers
- Retaining Walls
- Flooring
- Casework
- Telecom

ACTIVITIES COMPLETE:

- Foundation Installation
- Grading Operations
- Storm Drainage Installation
- Concrete Slabs
- Steel Installation
- Masonry Walls
- Waterproofing
- Roofing
- Painting
- Windows
- Curb and Gutter/Sidewalks

PROJECT SCHEDULE:

Substantial Completion Date: December 1, 2020

APPLICATIONS FOR PAYMENT:

Original Contract Sum: \$16,305,245.00

Net Change by Change Order: \$0

Contract Sum to Date: \$16,305,245.00

Amount Paid to Date: \$ 10,360,974.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



PROGRESS PHOTOS:




ENTRANCE



COURTYARD/CONNECTOR



PROGRESS PHOTOS:

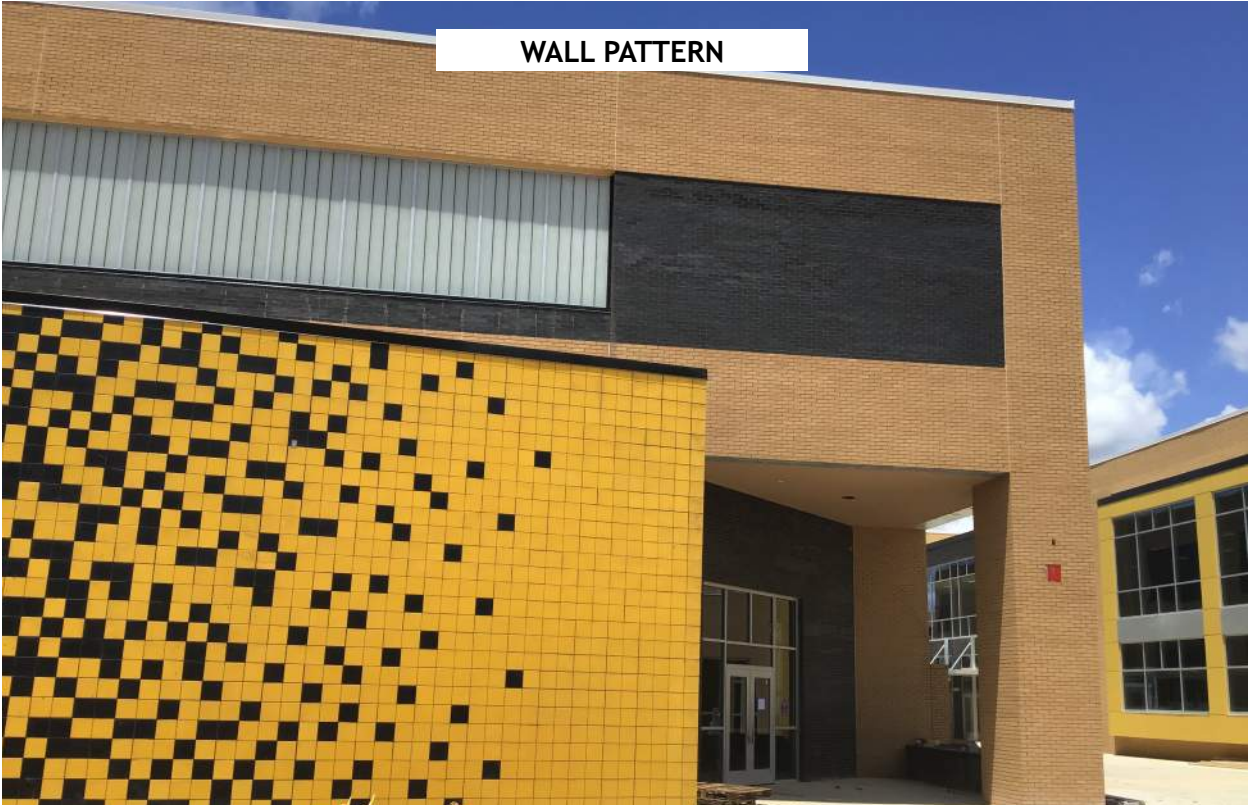

PROGRESS PHOTOS:

