



SILVER BLUFF HIGH SCHOOL STADIUM RESTROOMS


FINAL EXECUTIVE SUMMARY REPORT

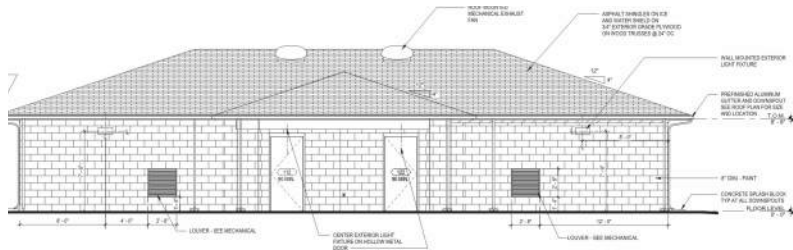


7
SOUTH ELEVATION
1/4" = 1'-0"

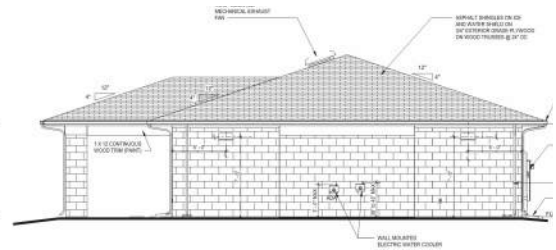


8
EAST ELEVATION
1/4" = 1'-0"

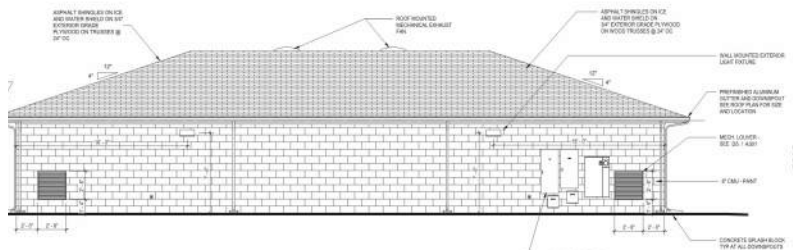


9
NORTH ELEVATION
1/4" = 1'-0"

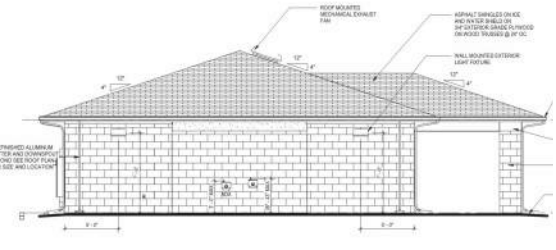


10
WEST ELEVATION
1/4" = 1'-0"

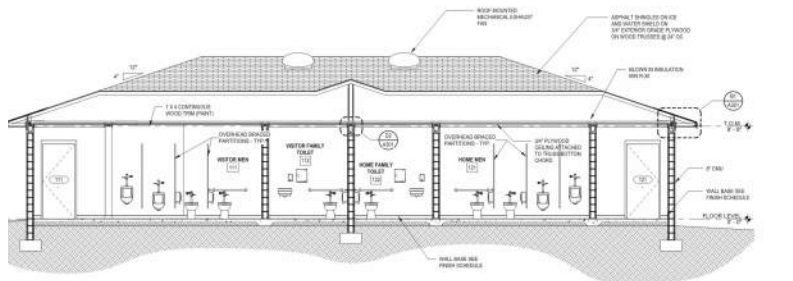


11
BUILDING CROSS SECTION - VISITOR MEN/HOME MEN
1/4" = 1'-0"

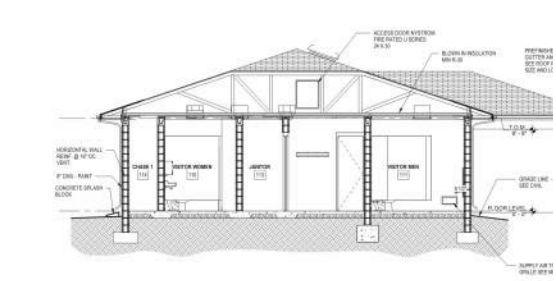

12
BUILDING CROSS SECTION
1/4" = 1'-0"



13
BUILDING CROSS SECTION - VISITOR WOMEN/HOME WOMEN
1/4" = 1'-0"



14
BUILDING CROSS SECTION
1/4" = 1'-0"



SILVER BLUFF HIGH SCHOOL STADIUM RESTROOMS

ACTIVITIES CURRENTLY UNDERWAY:

- Punch List

ACTIVITIES COMPLETE:

- All work is substantially complete.

PROJECT SCHEDULE:

Substantial Completion Date: August 21, 2019

APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$796,000.00
Net Change by Change Order:	\$0.00
Contract Sum to Date:	\$796,000.00
Amount Paid to Date:	\$676,818.99

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH: NONE



BUILDING PROGRESS PHOTOS:



FAMILY TOILETS



TOILETS ENTRANCE



BUILDING PROGRESS PHOTOS:

