


MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS


FINAL EXECUTIVE SUMMARY REPORT




SOUTH ELEVATION




EAST ELEVATION




NORTH ELEVATION





WEST ELEVATION

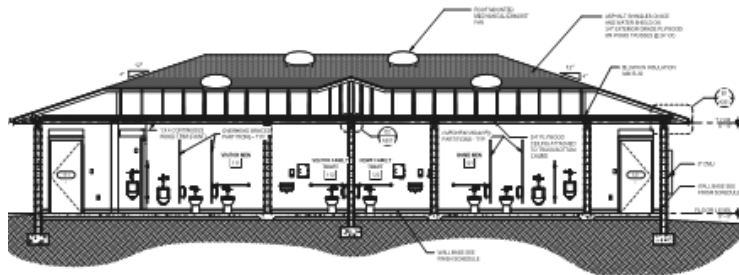

BUILDING CROSS SECTION - VISITOR MEN/MEN

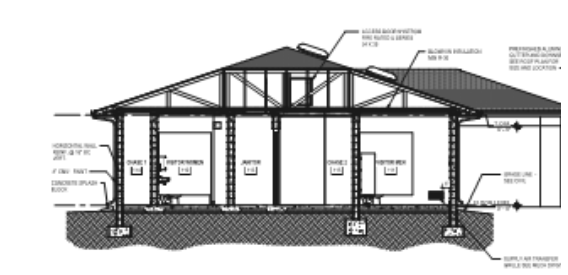

BUILDING CROSS SECTION



**mcmillan
pazardan
smith**
ARCHITECTURE

MIDLAND VALLEY HIGH SCHOOL STADIUM RESTROOMS

ACTIVITIES CURRENTLY UNDERWAY:

- None

ACTIVITIES COMPLETE:

- All work is complete.

PROJECT SCHEDULE:

Substantial Completion Date: August 10, 2018

APPLICATIONS FOR PAYMENT:

Original Contract Sum:	\$798,000.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$798,000.00
Amount Paid to Date:	\$722,902.00

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



BUILDING PROGRESS PHOTOS:

