

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



NOVEMBER 2021

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- The campus is fully occupied and operating.
- The new stacking drive and associated site area is operational.
- Landscaping, striping, and finish work are ongoing in this area.
- The final exterior phase is underway, which includes the playground area and fire access drive.

PROJECT SCHEDULE:

Notice to Proceed:	January 12, 2020
Substantial Completion Date:	December 11, 2021
Schedule Status:	The building is complete and the site is operational. Due to rain delays and unforeseen conditions, the substantial completion date has been extended.


PROJECT ACCOUNTING: (As of Pay Application #21, dated 10.31.21)

• Original Contract Sum:	\$ 9,666,700.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 9,666,700.00
• Total Completed and Stored to Date:	\$ 8,682,923.39

APPROVED CHANGES: None

PENDING CHANGES: None

KEY PLAN

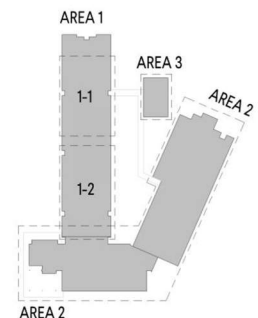

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

BUILDING PROCESS IMAGES:



Exterior progress photo. Asphalt installation is in progress.



Exterior progress photo. Asphalt installation is in progress.



Exterior progress photo. Asphalt installation is in progress.



Exterior progress photo. Asphalt installation is in progress.



Exterior progress photo. Asphalt installation is in progress.



Exterior progress photo.
