

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



MARCH 2020

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- Site fencing has been installed to establish the construction perimeter.
- Building demolition for Phase 1 is largely complete.
- The temporary office has been established.
- Site utility work is in progress in preparation for the building pad.

PROJECT SCHEDULE:

Notice to Proceed:	January 12, 2020
Substantial Completion Date:	August 12, 2021
Schedule Status:	On Schedule


PROJECT ACCOUNTING: (As of Pay Application #2, dated 03.31.20)

• Original Contract Sum:	\$ 9,666,700.00
• Net Change by Change Orders:	\$ 0.00
• Contract Sum to Date:	\$ 9,666,700.00
• Total Completed and Stored to Date:	\$ 195,917.00

APPROVED CHANGES: None

PENDING CHANGES: None

KEY PLAN

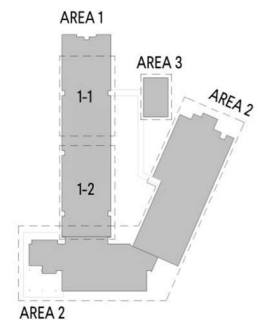

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

BUILDING PROCESS IMAGES:



Demolition of the existing classroom wing is complete.



Demolition of the existing classroom wing is complete.



Site demolition is in progress.



Site fencing has been installed to secure the lay-down area.



Sitework is underway to support the Phase 1 site conditions.



Site utility work is in progress to clear area for new building pad.
