



PHASE 1 RENOVATIONS & ADDITIONS TO HAMMOND HILL ELEMENTARY SCHOOL

EXECUTIVE SUMMARY REPORT
JUNE 2022



HAMMOND HILL ELEMENTARY SCHOOL RENOVATIONS AND ADDITIONS

PHASE I CONSTRUCTION:

- Installation of landscaping is continuing around the perimeter of the new 2-story classroom addition.
- Punch list work is ongoing in the new 2-story classroom building.
- Temporary wall between the new Phase 1 construction and existing admin. wing has been removed.

PHASE 2 CONSTRUCTION:

- Asbestos materials have been removed from the existing 7 & 8 classroom wings. Demolition of the existing 7-classroom wing has started. Wing is approximately 50% demolished.
- Temporary walls have been installed between the demolition areas and the existing buildings to remain.
- Temporary kitchen serving line has been set up in an existing vacant classroom. Food is being cooked off site at North Augusta High School and brought to Hammond Hill Elementary for serving.
- Existing portable classrooms are being prepared to be moved off site.

PROJECT SCHEDULE:

| | |
|--------------------------------------|-------------------------|
| Notice to Proceed: | November 16, 2020 |
| Substantial Completion Date Phase 1: | April 15, 2022 |
| Substantial Completion Date Phase 2: | March 24, 2023 |
| Schedule Status: | Project is on schedule. |

PROJECT BUDGET:

| | |
|-------------------------------------|-----------------|
| Original Contract Sum: | \$15,240,600.00 |
| Net Change by Change Orders: | \$0.00 |
| Contract Sum to Date: | \$15,240,600.00 |
| Total Completed and Stored to Date: | \$11,470,615.00 |

APPROVED CHANGES: None




DEMOLITION OF EXISTING 7-CLASSROOM WING



PORTABLE CLASSROOM BEING PREPARED FOR REMOVAL



TEMPORARY PARTITION BETWEEN EXISTING BUILDING & NEW CONSTRUCTION

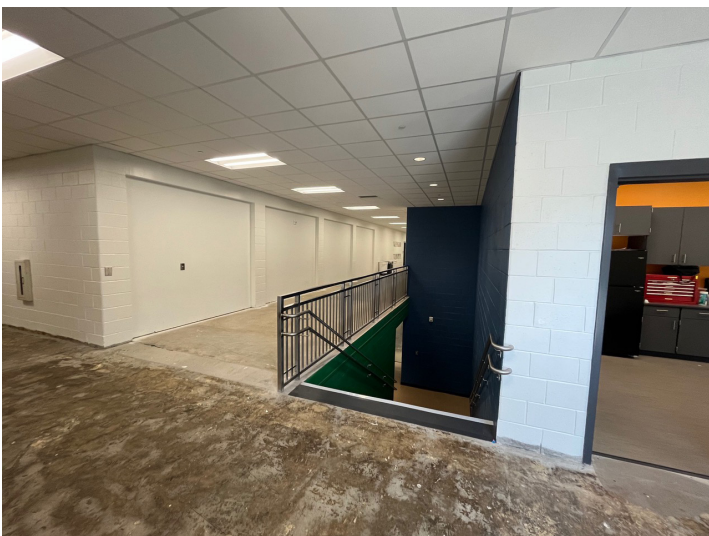

EXISTING WALL REMOVED BETWEEN NEW CONSTRUCTION & EXISTING ADMIN. WING



TEMPORARY KITCHEN SERVING LINE
