



PHASE 2 RENOVATIONS & ADDITIONS TO HAMMOND HILL ELEMENTARY SCHOOL

EXECUTIVE SUMMARY REPORT
NOVEMBER 2022



HAMMOND HILL ELEMENTARY SCHOOL RENOVATIONS AND ADDITIONS

PHASE I CONSTRUCTION:

- The hillside and surrounding area have been graded and grassed at the upper play ground. Installation of irrigation lines around this playground has been completed.

PHASE 2 CONSTRUCTION:

- Grass sod and seeding has been installed on both sides of the new vehicular stacking lanes.
- CMU installation has been completed at the new kitchen and cafeteria addition. Installation of brick veneer is approximately 75% complete.
- Installation of roof bar joists is approximately 90% complete. Installation of metal roof decking has been completed at the kitchen and cafeteria. Perforated acoustical metal decking has been installed above the cafeteria.
- Grading and lowering of the roadway behind the new kitchen continues. Hillside along the south property line has been excavated for the new retaining wall.


PROJECT SCHEDULE:

| | |
|--------------------------------------|-------------------------|
| Notice to Proceed: | November 16, 2020 |
| Substantial Completion Date Phase 1: | April 15, 2022 |
| Substantial Completion Date Phase 2: | March 24, 2023 |
| Schedule Status: | Project is on schedule. |

PROJECT BUDGET:

| | |
|-------------------------------------|-----------------|
| Original Contract Sum: | \$15,240,600.00 |
| Net Change by Change Orders: | \$0.00 |
| Contract Sum to Date: | \$15,240,600.00 |
| Total Completed and Stored to Date: | \$13,023,349.00 |

APPROVED CHANGES: None

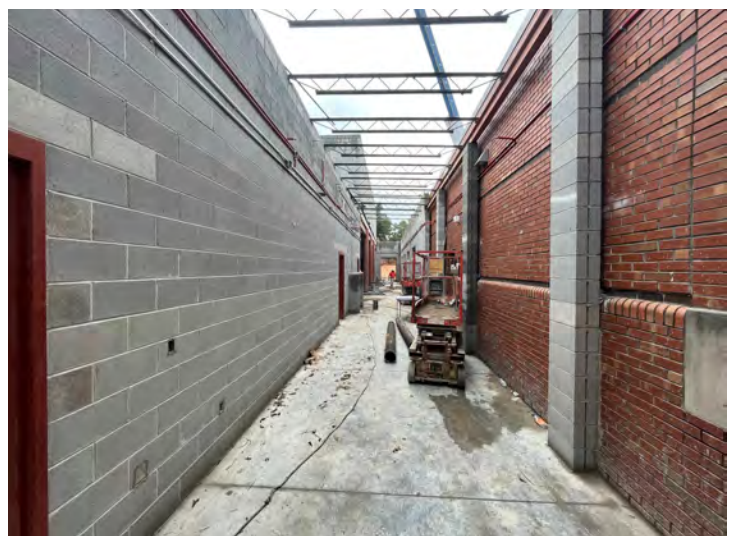

PHASE 2 CONSTRUCTION IN PROGRESS



SODDING, GRASSING & IRRIGATION ON EACH SIDE OF VEHICULAR QUEING LANES COMPLETED.



LOWERING OF ROADWAY & EXCAVATION OF HILLSIDE IS STILL IN PROGRESS



GRADING & GRASSING AROUND NEW PLAYGROUND COMPLETED
