



The New Wagener-Salley High School

EXECUTIVE SUMMARY REPORT
SEPTEMBER 2024

THE NEW Wagener-Salley High School

ACTIVITIES CURRENTLY UNDERWAY:

- Masonry
- Plumbing
- HVAC
- Electrical
- Fire Protection
- Athletic Fields
- Storefront and Glass
- Curb and Gutter and Sidewalks
- Concrete Polishing
- Fire Protection
- Painting
- Sheetrock
- Ceiling Grids
- Roofing
- Flooring
- Grassing

- IT Installation

ACTIVITIES COMPLETE:

- Sub grade block
- Storm Drainage
- Retention Pond
- Slabs
- Modular Walls
- Underground Plumbing
- Steel Framing

- Grading

PROJECT SCHEDULE:

Substantial Completion Date, Scheduled: September 24, 2024

Final Completion for OSF Inspection of Punchlist, IT install, & FFE install : November 15, 2024

PROJECT BUDGET:

Original Contract Sum, Sitework:	\$ 5,027,934.00
Original Contract Sum, Foundations/Steel:	\$ 6,046,282.00
Original Contract Sum, Building:	\$39,565,677.00
Original Contract Sum, Total:	\$50,639,893.00
Net Change by Change Order:	\$ 0
Contract Sum to Date, Building & Site:	\$50,639,893.00
Amount Paid to Date, Building & Site:	\$37,661,785.39

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH

There have been no requests for change order approved this month.



GLASS AT STAIR INSTALL




VIEW TO AREA A



GYM CORRIDOR EXTERIOR



COURTYARD VIEW

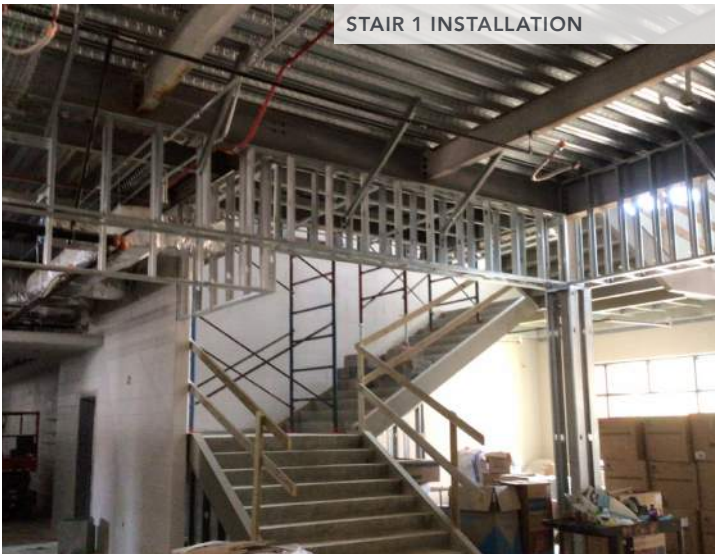

STAIR 1 INSTALLATION



CAFETERIA EXTERIOR VIEW



VESTIBULE ENTRANCE AND GYM



SERVING LINE ROLL UP DOORS



CEILING GRID INSTALL
