

BOARD AGENDA ITEM

July 28, 2026

SUBJECT:

Construction Status Reports for the North Augusta High Auditorium addition and renovation project

BACKGROUND INFORMATION:

In an effort to keep the board current on the status and budget of this school construction project, the architects for this project, McMillan Pazdan Smith (MPS), and the administration prepare a bi-monthly status report for the board's review.

ADMINISTRATIVE CONSIDERATION:

A construction status report for the board is attached for review from McMillan Pazdan Smith (MPS).

RECOMMENDATIONS:


Review and accept the status information as indicated on the report.

ATTACHMENT:

North Augusta High Auditorium addition and renovation project executive summary report

PREPARED BY:

Tim Yarborough
Michael F. Jara



AIKEN COUNTY

PUBLIC SCHOOLS





EXECUTIVE SUMMARY REPORT

NORTH AUGUSTA HIGH SCHOOL AUDITORIUM RENOVATION

AIKEN COUNTY PUBLIC SCHOOL DISTRICT

JULY 2026



AIKEN COUNTY
PUBLIC SCHOOLS



mcmillan
pazdan
smith
ARCHITECTURE

NORTH AUGUSTA HIGH SCHOOL AUDITORIUM RENOVATION

CURRENT AND UPCOMING ACTIVITIES:

- Elevator Slabs and Pits
- Acoustical Clouds – can remove scaffolding when complete
- Transformer/Electrical Work
- Plumbing
- Masonry
- Concrete Slabs in back


ACTIVITIES COMPLETE:

- Duct Work

NEW FRONT ENTRANCE



LOBBY EXPANSION

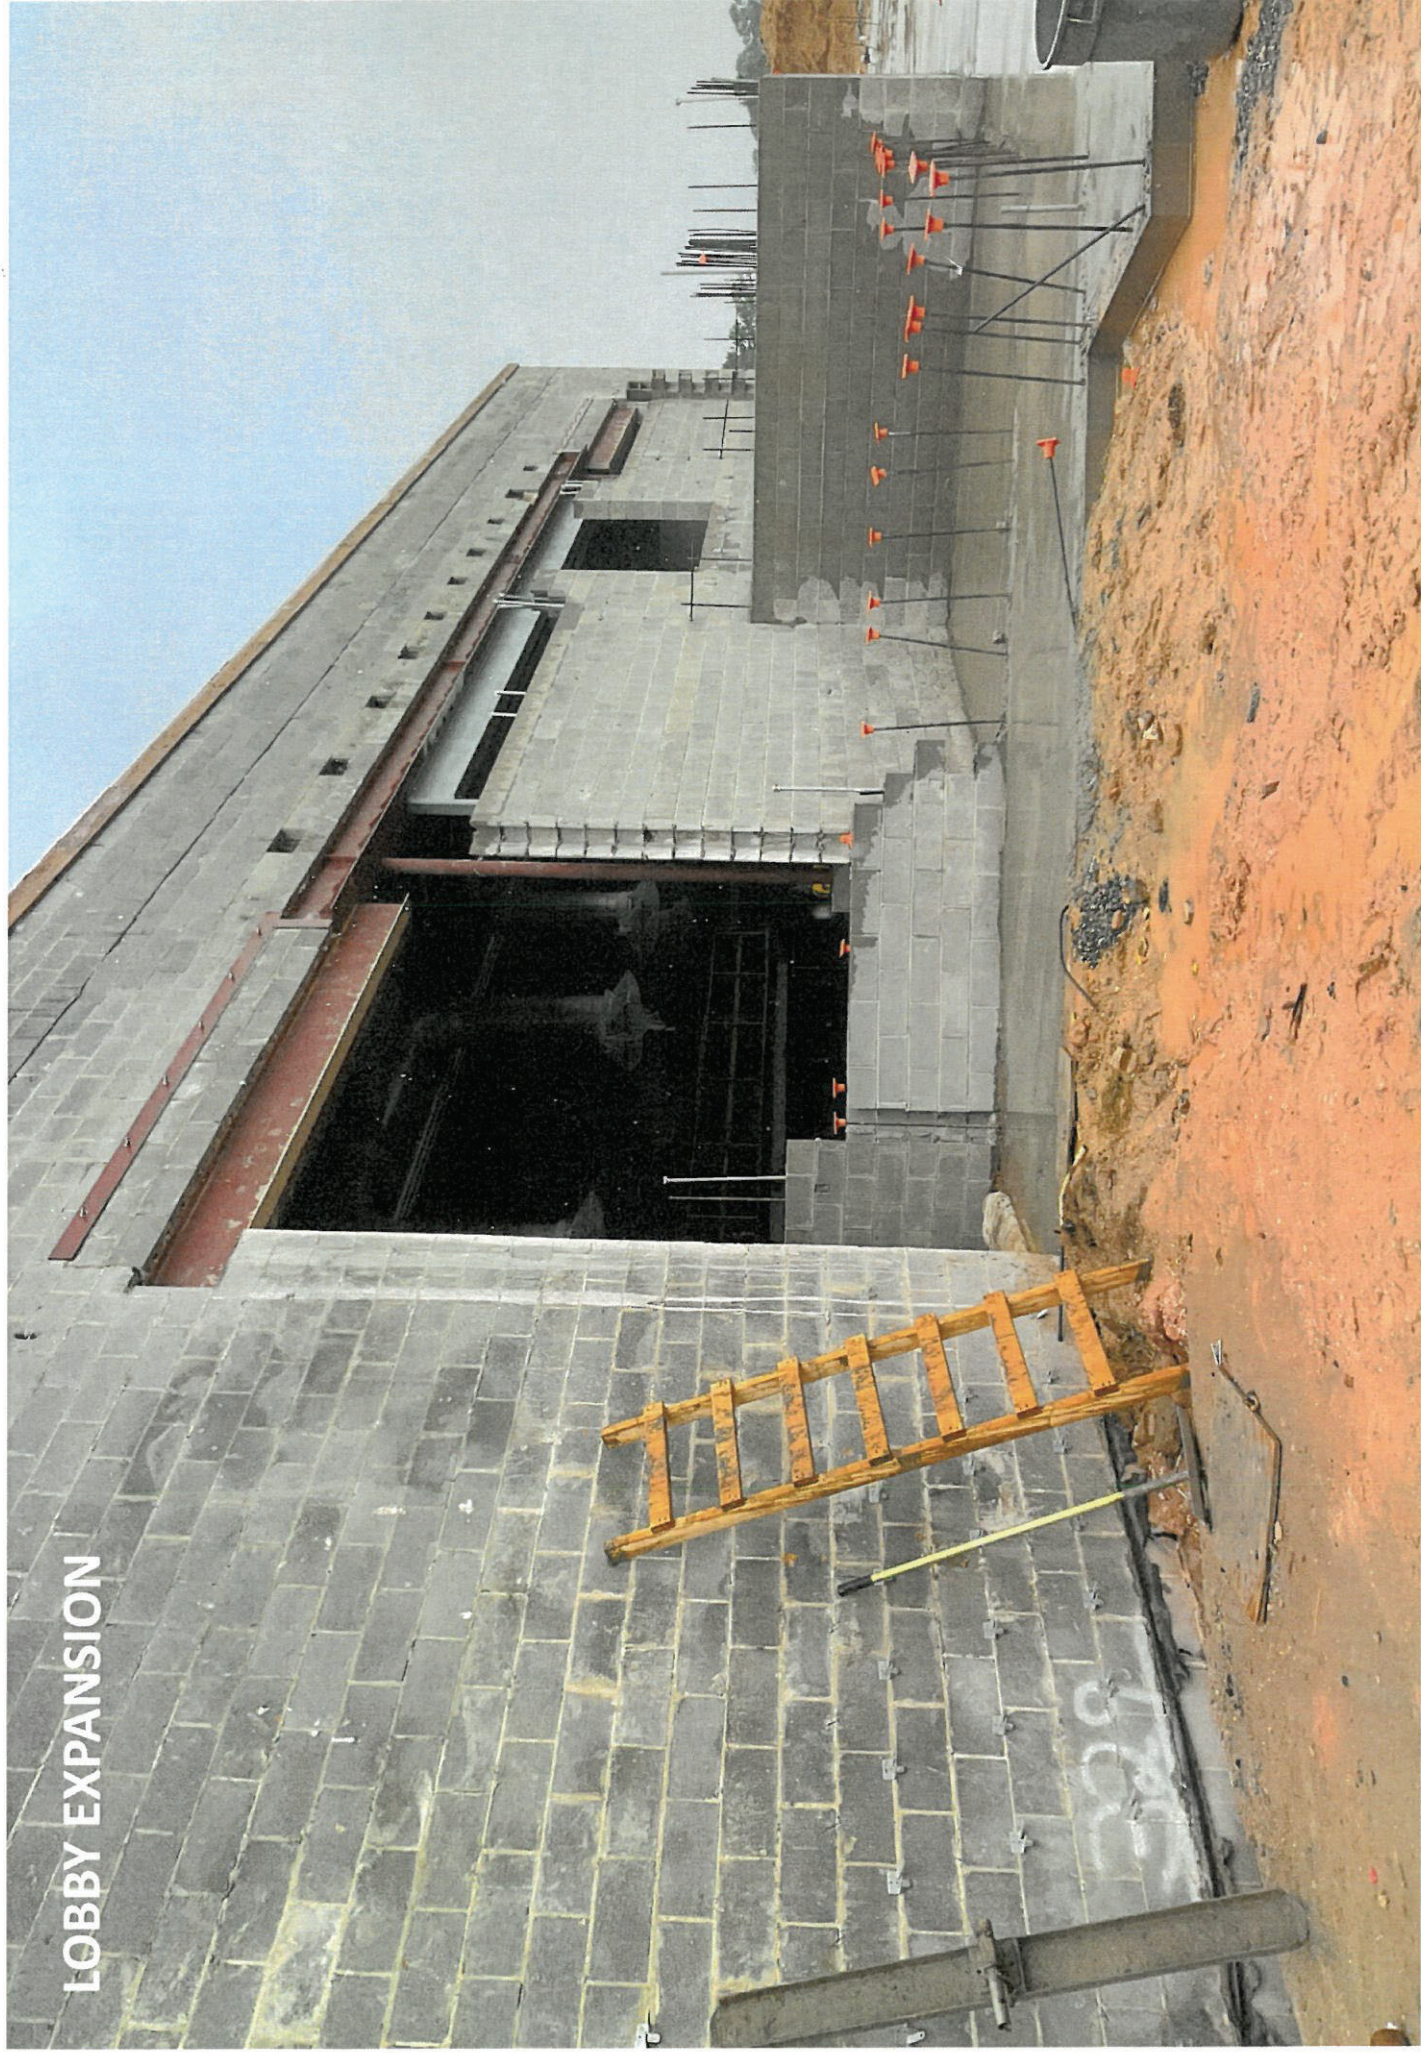

SEATING EXPANSION



REAR SEATING



ACOUSTICAL CLOUD FRONT



ACOUSTICAL CLOUD REAR



REAR VIEW OF AUDITORIUM EXTERIOR



NORTH AUGUSTA HIGH SCHOOL

AUDITORIUM RENOVATION

PROJECT SCHEDULE:

- Estimated date of Final Completion: July 2027
- Project is on schedule.

PROJECT BUDGET:

- Original Contract Sum: \$10,243,907.00
- Net Changes by COs: \$0.00
- Contract Sum to Date: \$10,243,907.00
- Amount Paid to Date: \$ 1,982,431.34 (As of June Pay App)

QUESTIONS & COMMENTS
