



The New Wagener-Salley High School

EXECUTIVE SUMMARY REPORT
NOVEMBER 2024

THE NEW Wagener-Salley High School

ACTIVITIES CURRENTLY UNDERWAY:

- Electrical
- Plumbing
- Fire Protection
- Athletic Fields
- Painting
- Flooring

- IT Installation
- Elevator
- Lab Equipment

- Furniture

- **ACTIVITIES COMPLETE:**
- Foundations and Steel
- Storm Drainage
- Retention Pond
- Slabs
- Modular Walls
- HVAC

- Grading
- Masonry
- Storefront and Glass
- Roofing
- Curb and Gutter, Sidewalks

- Paving

PROJECT BUDGET:

Original Contract Sum, Sitework:	\$ 5,027,934.00
Original Contract Sum, Foundations/Steel:	\$ 6,046,282.00
Original Contract Sum, Building:	\$39,565,677.00
Original Contract Sum, Total:	\$50,639,893.00
Net Change by Change Order:	\$ 0
Contract Sum to Date, Building & Site:	\$50,639,893.00
Amount Paid to Date, Building & Site:	\$42,230,464.61

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH


There have been no requests for change order approved this month.



AG LAB



COSMOTOLOGY LAB

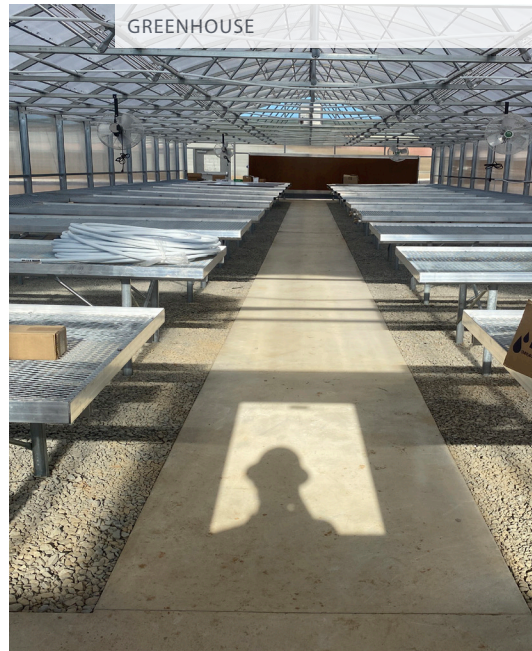

GREENHOUSE



WELDING LAB
