



EAST ELEVATION  
02-11-22

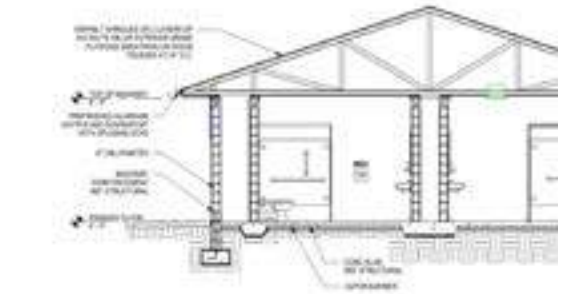

BUILDING SECTION  
02-11-22

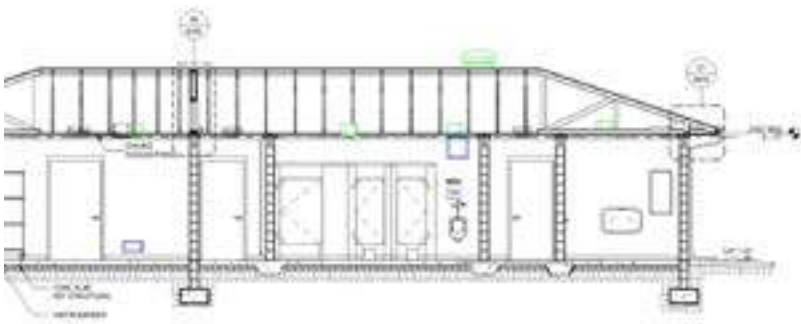

# North Augusta High School RESTROOMS & CONCESSIONS

EXECUTIVE SUMMARY REPORT  
SEPTEMBER 2022

# North Augusta High School

## RESTROOMS & CONCESSIONS

### ACTIVITIES CURRENTLY UNDERWAY:

- Site Work Operations
- Plumbing Rough In
- Electrical Rough In
- Foundation/Slab Installation

### ACTIVITIES COMPLETE:

### PROJECT SCHEDULE:

Substantial Completion Date: November 1, 2022

### PROJECT SCHEDULE:

Original Contract Sum, Building:	\$1,169,900.00
Net Change by Change Order:	\$0
Contract Sum to Date:	\$1,169,900.00
Amount Paid to Date, Building & Site:	\$ 176,595.00

### REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



CONSTRUCTION FENCE



SITE PREPARATION



SLAB INSTALLATION



SLAB INSTALLATION



SITE PREPARATION
