



# The New Wagener-Salley High School

EXECUTIVE SUMMARY REPORT  
JANUARY 2024

# THE NEW Wagener-Salley High School

## ACTIVITIES CURRENTLY UNDERWAY:

- Masonry
- Door Frames
- Plumbing
- HVAC
- Electrical
- Fire Protection
- Athletic Fields
- Steel Deck and Roof Drains
- Window Flashing
- 2nd Floor steel work
  
- Insulation

## ACTIVITIES COMPLETE:

- Sub grade block
- Storm Drainage
- Retention Pond
- Slab Pour
- Modular Walls
  
- Underground Plumbing

## PROJECT SCHEDULE:

Substantial Completion Date, Scheduled: September 24, 2024

Final Completion for OSF Inspection of Punchlist, IT install, & FFE install : November 15, 2024

## PROJECT BUDGET:

Original Contract Sum, Sitework: \$ 5,027,934.00

Original Contract Sum, Foundations/Steel: \$ 6,046,282.00

Original Contract Sum, Building: \$39,565,677.00

Original Contract Sum, Total: \$50,639,893.00

Net Change by Change Order: \$ 0

Contract Sum to Date, Building & Site: \$50,639,893.00

Amount Paid to Date, Building & Site: \$ 20,140,599.84

## REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH

There have been no requests for change order approved this month.



BRICK COMPLETE



AERIAL VIEW



GYM CORRIDOR



GYM CORRIDOR ENTRANCE



GYM EXTERIOR BRICK COMPLETE




SECOND FLOOR STEEL TO BEGIN



ROOF DECK INSTALLED



AERIAL VIEW

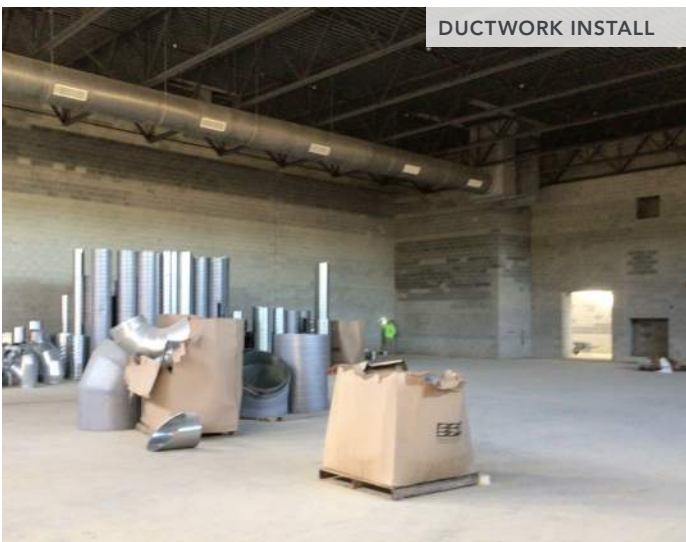

DUCTWORK INSTALL



BRICK COMPLETE
