



The New Wagener-Salley High School

EXECUTIVE SUMMARY REPORT
JULY 2023

THE NEW Wagener-Salley High School

ACTIVITIES CURRENTLY UNDERWAY:

- Grading
- Under Slab
- Slab Pour
- Masonry
- Door Frames
- MEP Rough-In

ACTIVITIES COMPLETE:

- Sub grade block
- Storm Drainage
- Retention Pond

PROJECT SCHEDULE:

Substantial Completion Date, Scheduled: July 1, 2024

PROJECT BUDGET:

Original Contract Sum, Sitework: \$ 5,027,934.00

Original Contract Sum, Foundations/Steel: \$ 6,046,282.00

Original Contract Sum, Building: \$39,565,677.00

Original Contract Sum, Total: \$50,639,893.00

Net Change by Change Order: \$ 0

Contract Sum to Date, Building & Site: \$50,639,893.00

Amount Paid to Date, Building & Site: \$ 7,557,625.38

REQUESTS FOR CHANGE ORDER APPROVED THIS MONTH:

There have been no requests for change order approved this month.



FOOTINGS OF A2 UNDERWAY WITH BAND COURTYARD WALLS BEHIND



INTERIOR VIEW OF SPECIAL ED CLASSROOM TOWARD CORRIDOR



EXTERIOR WEIGHTROOM WALL




RETENTION POND



SPECIAL EDUCATION WING



PE LOCKER ROOM DOOR FRAME INSTALLATION

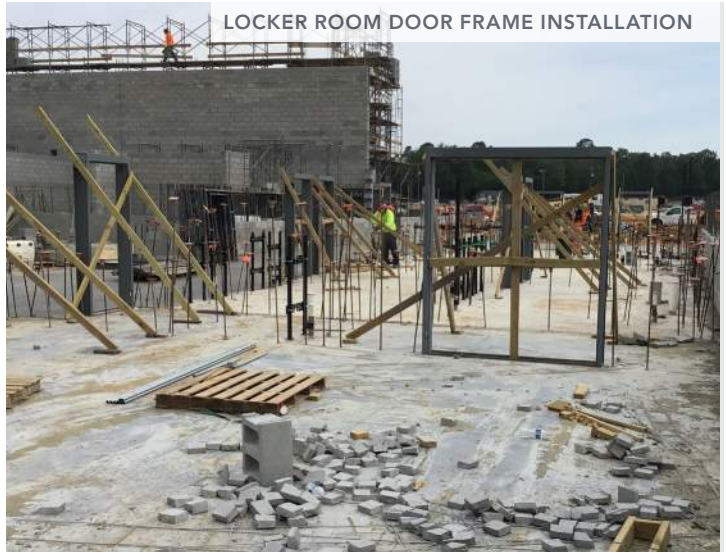

LOCKER ROOM DOOR FRAME INSTALLATION



AUXILIARY GYM UNDERWAY



AUXILIARY GYM EXTERIOR WALL



FOUNDATION INSTALLATION
