

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

EXECUTIVE SUMMARY REPORT



JANUARY 2022

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

ACTIVITIES CURRENTLY UNDERWAY:

- The new stacking drive and associated sitework is complete.
- The final phase of sitework is underway.
- The new fire access drive has been installed.
- The new walking path and tricycle track have been installed.
- Fence installation is in progress.
- Playground equipment installation is in progress.

PROJECT SCHEDULE:

Notice to Proceed:

January 12, 2020

Substantial Completion Date:

February 15, 2022

Schedule Status:

The building is complete and the site is operational. Due to rain delays and unforeseen conditions, the substantial completion date has been extended.

PROJECT ACCOUNTING: (As of Pay Application #23, dated 12.31.21)

- Original Contract Sum: \$ 9,666,700.00
- Net Change by Change Orders: \$ 0.00
- Contract Sum to Date: \$ 9,666,700.00
- Total Completed and Stored to Date: \$ 8,999,367.39


APPROVED CHANGES:

None

PENDING CHANGES:

None

KEY PLAN

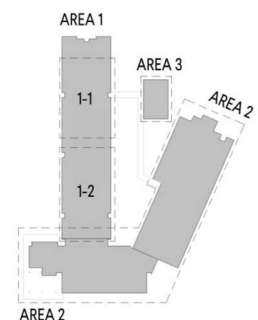

MILLBROOK ELEMENTARY SCHOOL ADDITION AND RENOVATIONS

BUILDING PROCESS IMAGES:



New asphalt and concrete paving is in progress.



New fire access drive and fencing are in progress.



New walking path is in progress.



New walking path is in progress.



Exterior progress photo.



Kindergarten tricycle path has been installed.
