

BOARD AGENDA ITEM

May 12, 2026

SUBJECT:

Construction status report for the Wagener-Salley High School athletics project

BACKGROUND INFORMATION:

In an effort to keep the board current on the status and budget of this school construction project, the architects for this project, McMillan Pazdan Smith (MPS), and the administration prepare a bi-monthly status report for the board's review.

ADMINISTRATIVE CONSIDERATION:

A construction status report for the board is attached for review from McMillan Pazdan Smith (MPS)

RECOMMENDATIONS:

Review and accept the status information as indicated on the report.

ATTACHMENT:

Wagener-Salley athletics project executive summary report

PREPARED BY:

Tim Yarborough
Michael F. Jara



AIKEN COUNTY

PUBLIC SCHOOLS





EXECUTIVE SUMMARY REPORT

WAGGENER-SALLEY HIGH SCHOOL ATHLETICS, PARK & PAVILION

AIKEN COUNTY PUBLIC SCHOOL DISTRICT MAY 2026



AIKEN COUNTY
PUBLIC SCHOOLS



mcmillan
pazdan
smith
ARCHITECTURE

WAGGENER-SALLEY HIGH SCHOOL ATHLETICS, PARK & PAVILION


CURRENT AND UPCOMING ACTIVITIES:

- Roof sheeting continues
- Masonry
- Electrical
- Plumbing
- Bleachers
- Landscaping and Irrigation
- Turf
- Pickle Ball Court


ACTIVITIES COMPLETE:

- Football field base
- Park retaining wall

BASEBALL FIELD PREP

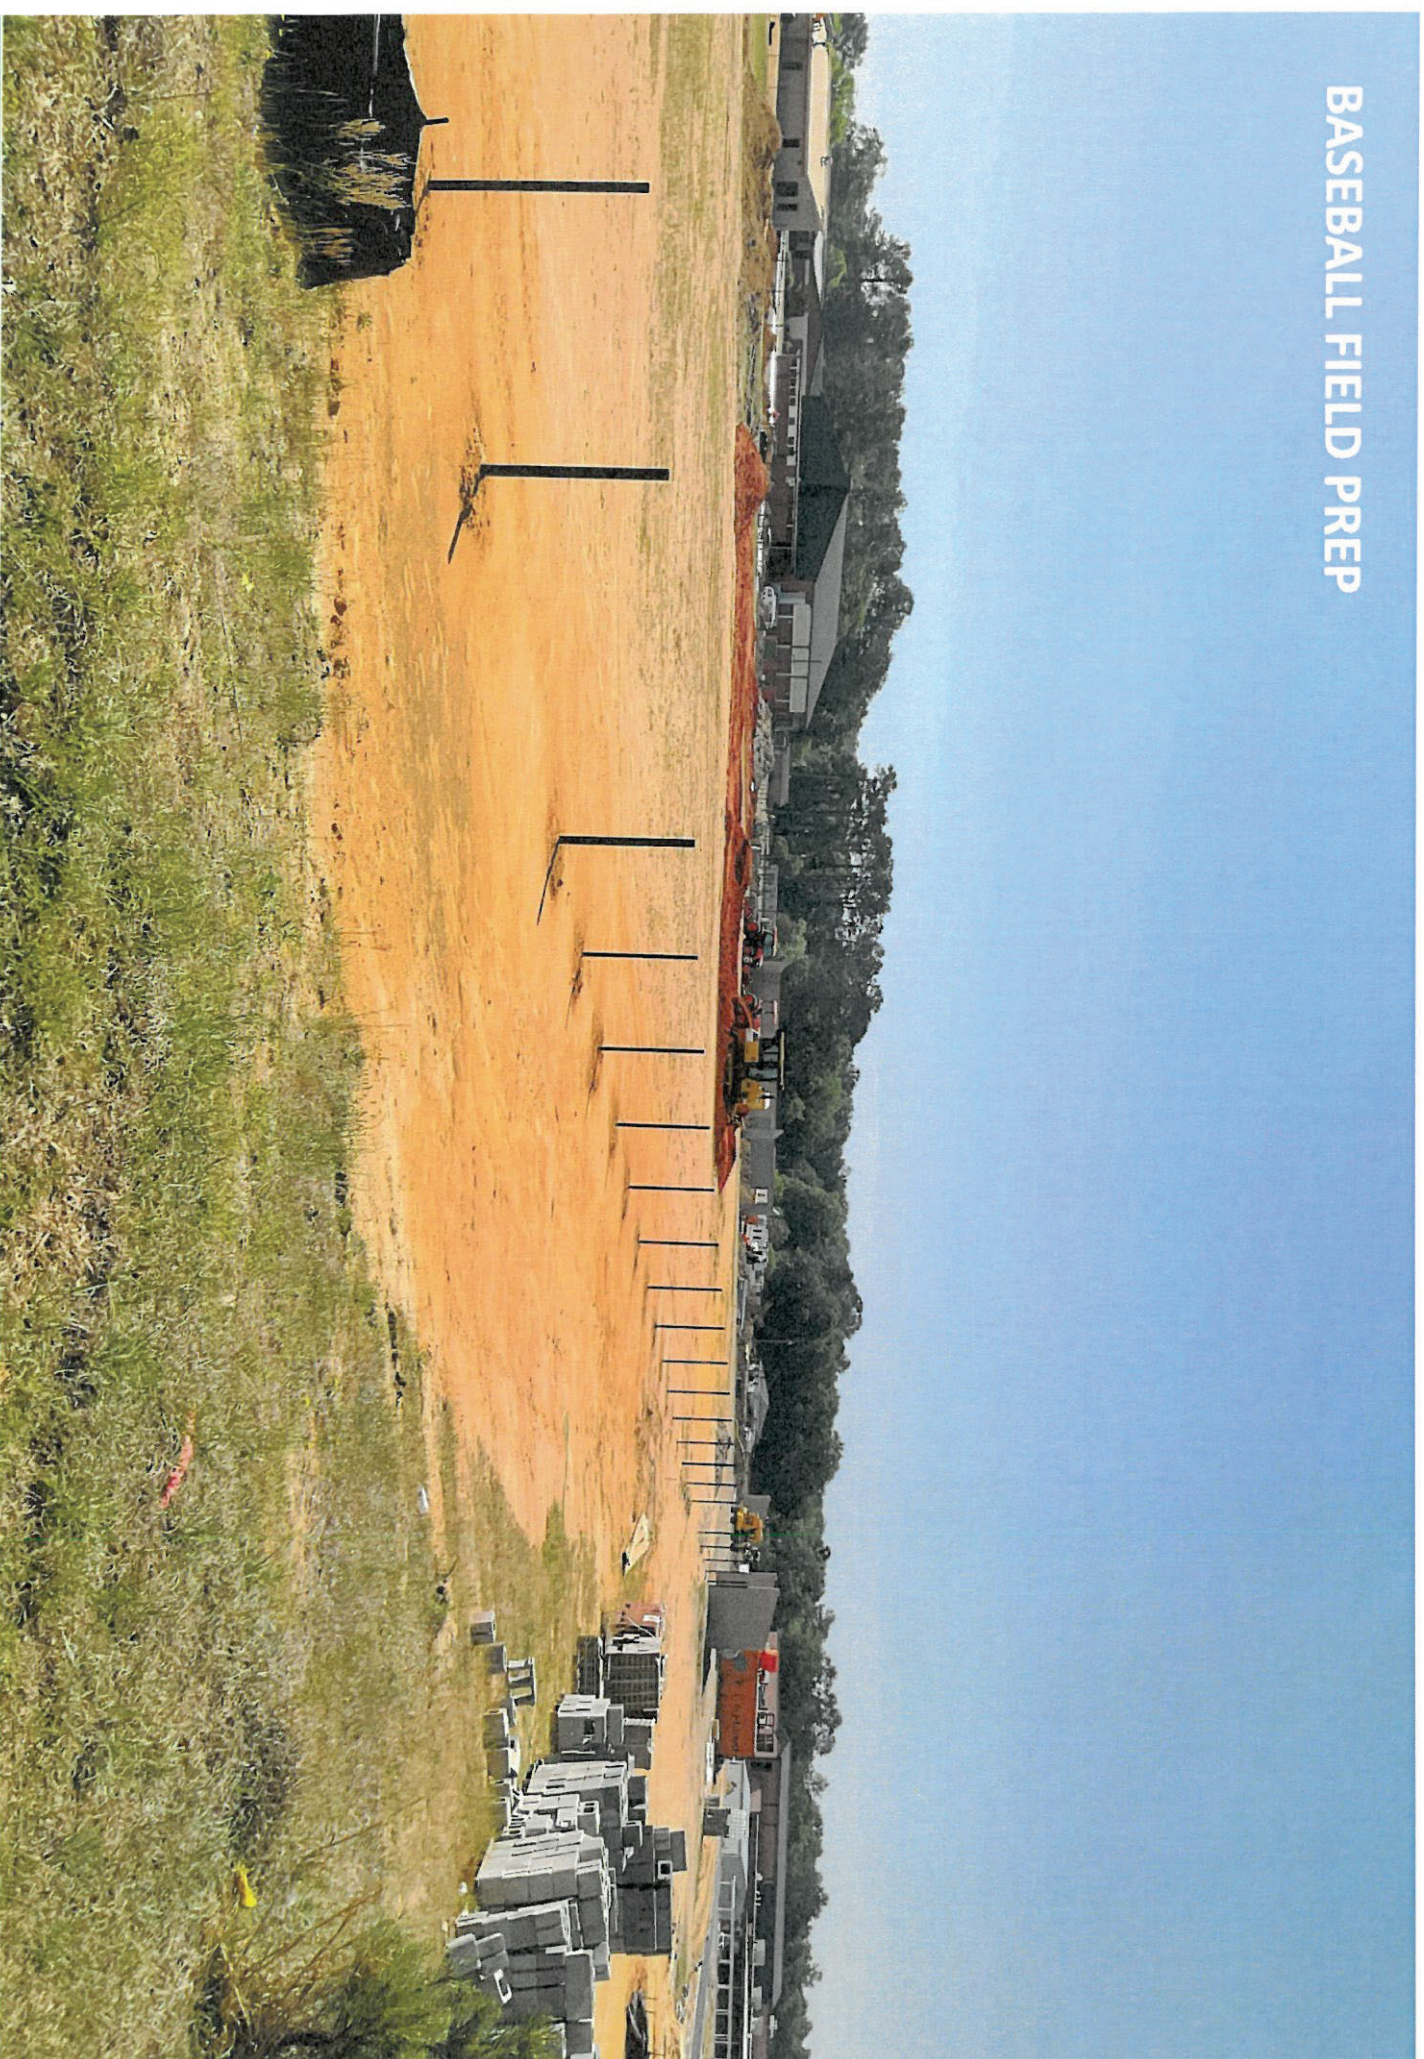


TRACK BASE

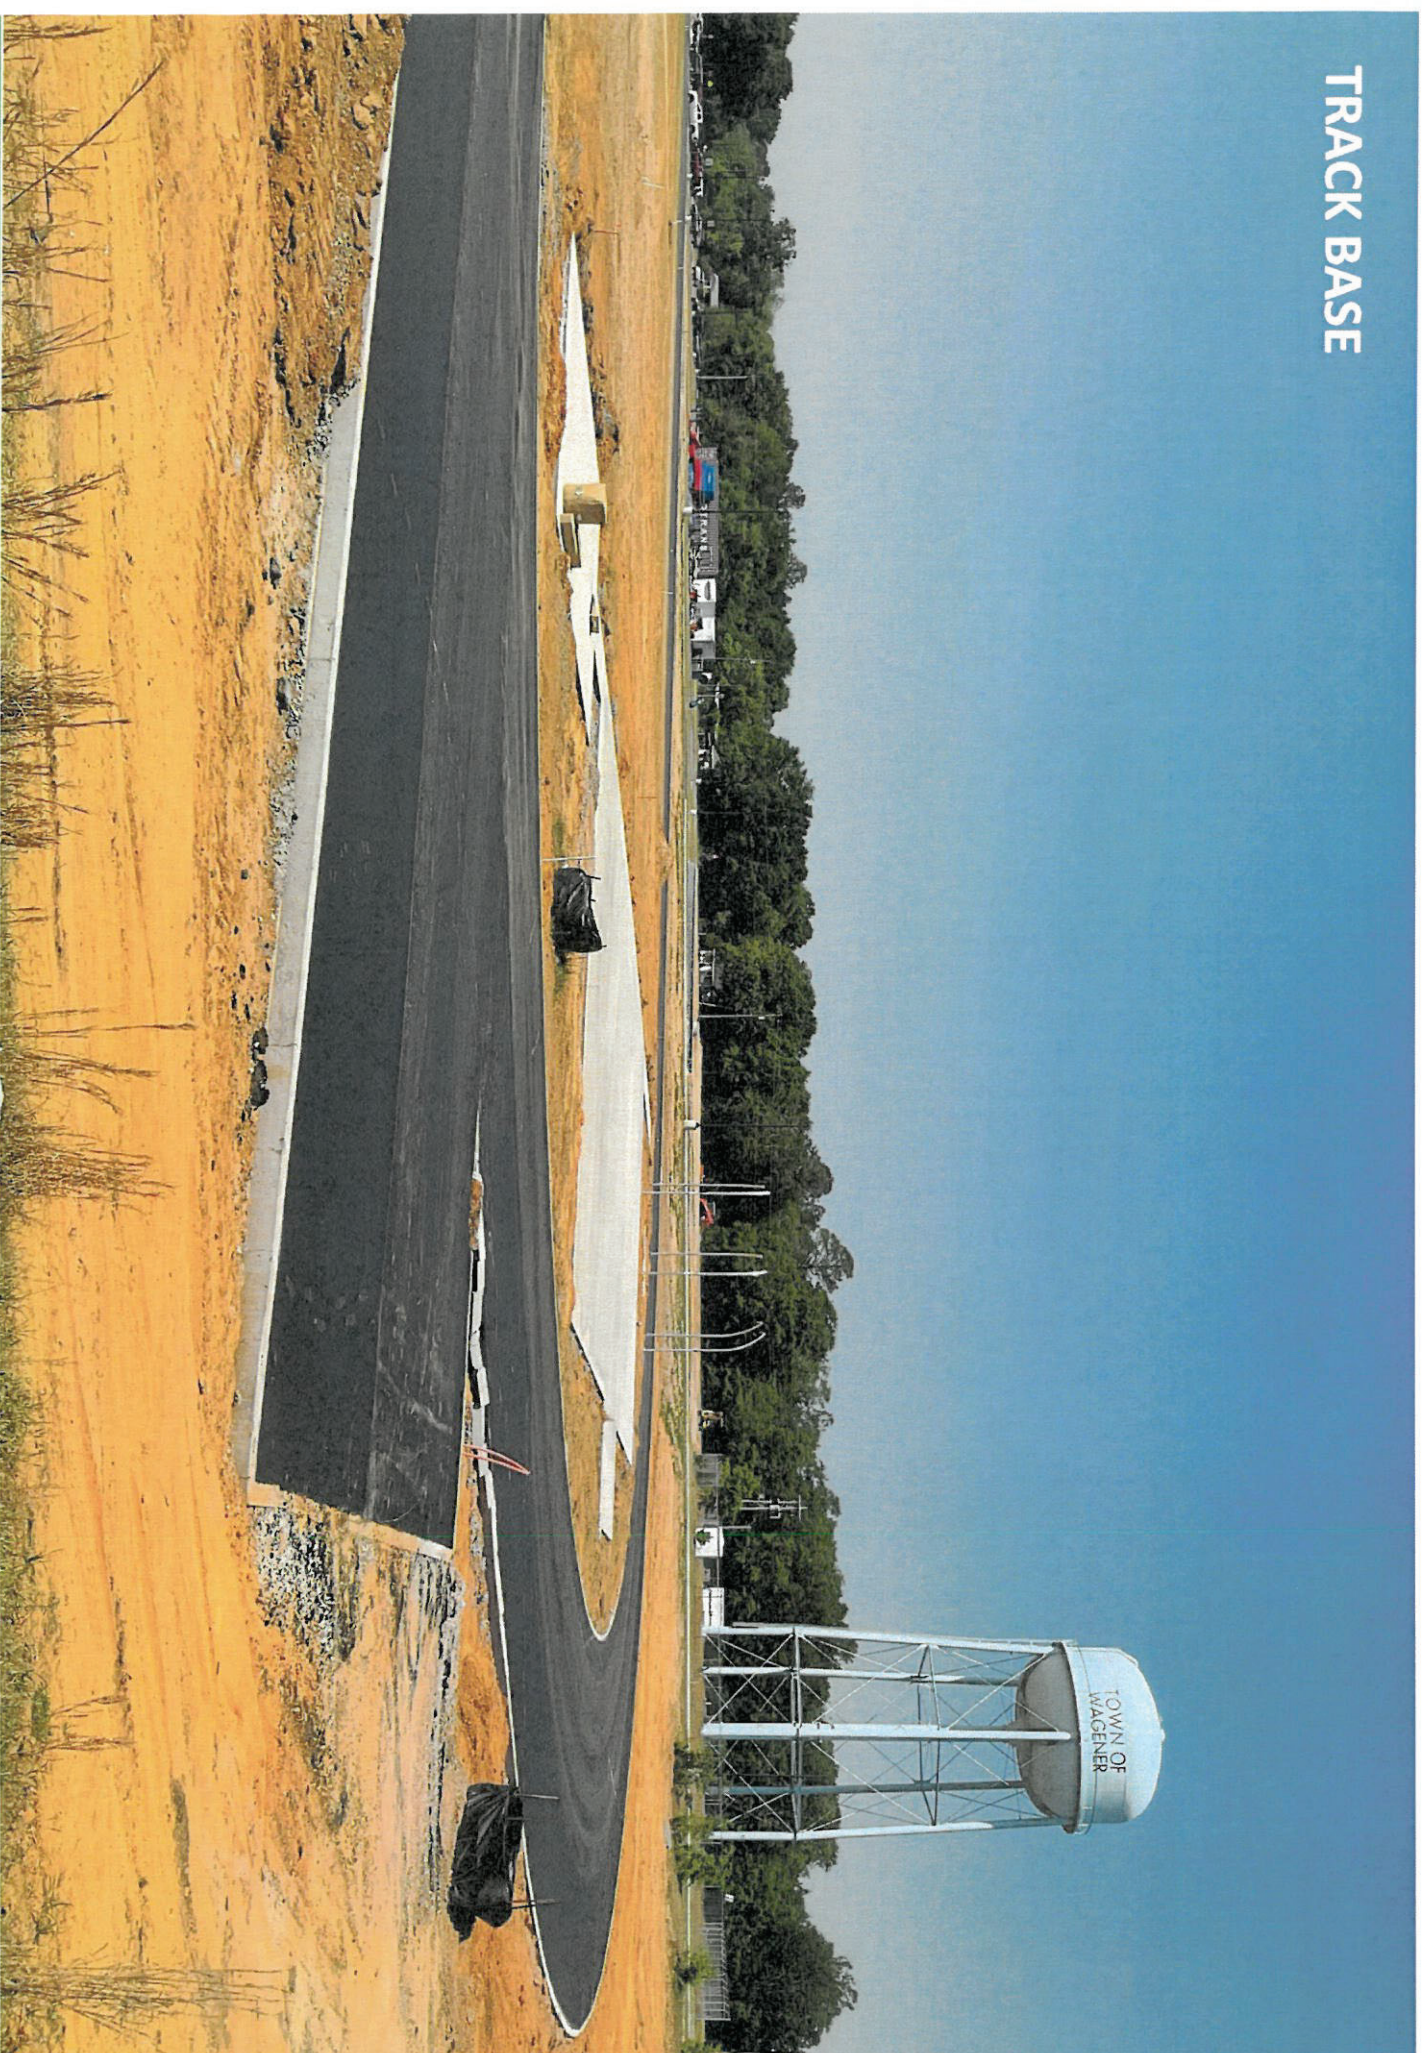

FOOTBALL STADIUM RETAINING WALL



FOOTBALL STADIUM VISITOR'S SIDE

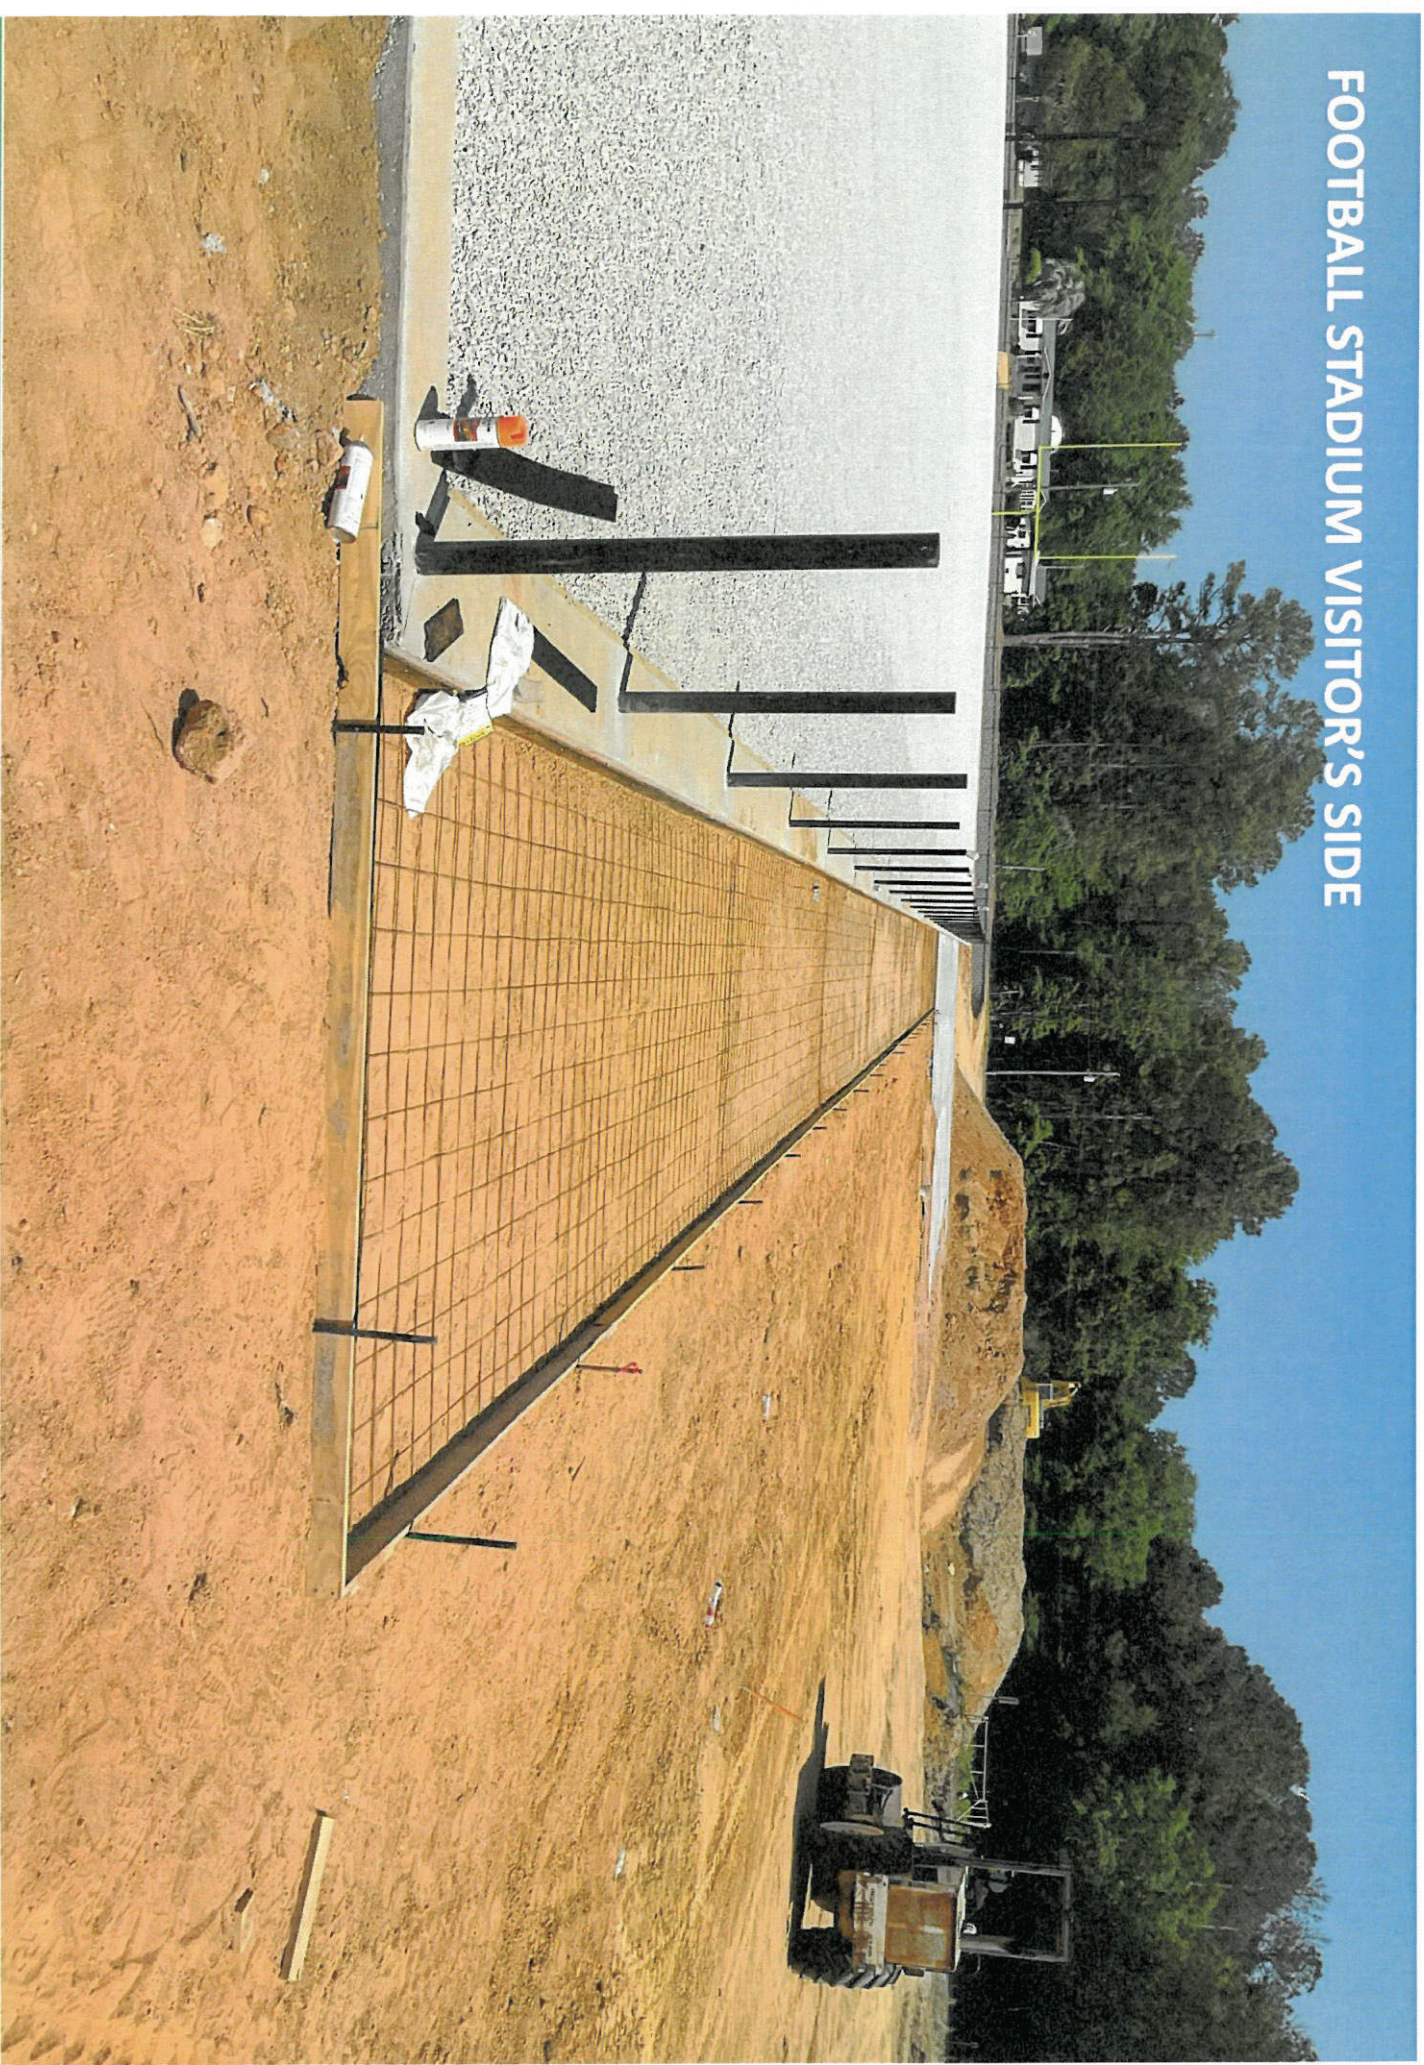

FOOTBALL STADIUM HOME SIDE BLEACHERS




FOOTBALL RESTROOMS



REAR VIEW OF RESTROOMS AND CONCESSIONS



PARK RETAINING WALL

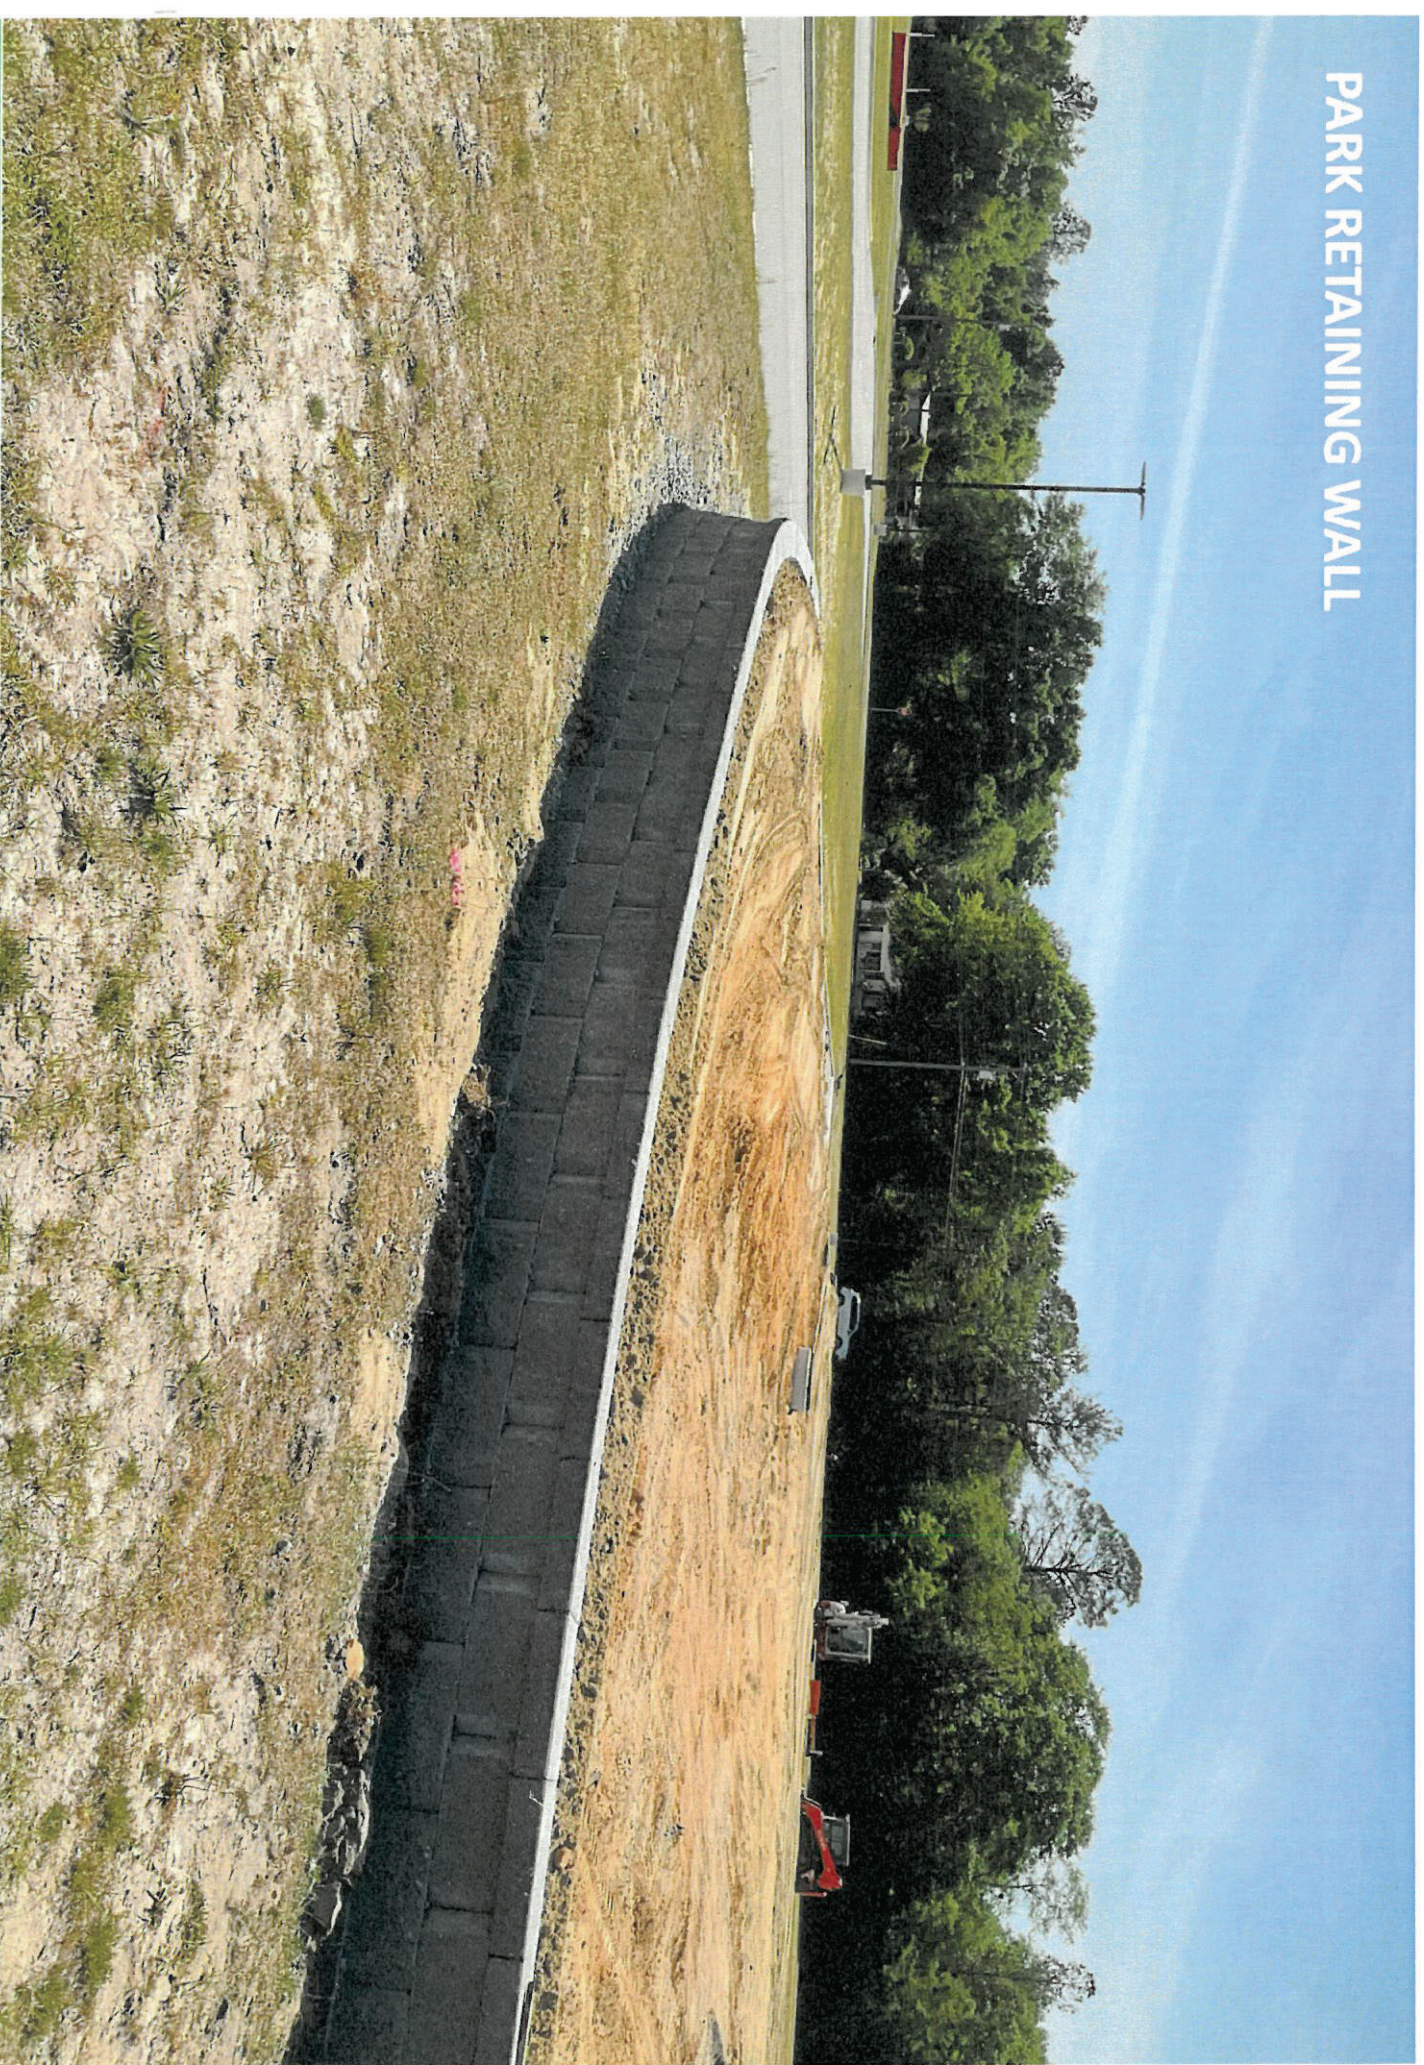


WAGGENER-SALLEY HIGH SCHOOL ATHLETICS, PARK & PAVILION

PROJECT SCHEDULE:

- Estimated date of Final Completion: January 2027
- Project is on schedule.

PROJECT BUDGET:

- Original Contract Sum: \$12,783,753.00
- Net Changes by COs: \$0.00
- Contract Sum to Date: \$12,783,753.00
- Amount Paid to Date: \$ 1,646,406.95 (As of April Pay App)

A photograph of a school gymnasium. In the foreground, a cheerleader in a blue and white outfit holds a large flag with green, yellow, and red sections. In the background, several students are playing basketball on a court. A basketball hoop and backboard are visible on the right side of the image. The gymnasium has a blue wall and a white ceiling with exposed trusses.

QUESTIONS & COMMENTS
